What the tracker does

One place to **plan**, **run** and **monitor** every QA activity of every part, through each trial.

PLAN
Set up what has to happen, and when

1 Plan & schedule · 2 Parts & ownership · 3 Activity design

RUN
Get every part's data in, checked and approved

4 Release & acknowledge · 5 Data entry · 6 Validation & approvals

MONITOR
See status early and act on it

7 Status & risk insight · 8 Project view · 9 Resource & travel planning · 10 Monitoring & reporting

1 Plan & schedule
Dates come from the model schedule, not from anyone's memory. p. 7

2 Parts & ownership
One part master, and every part has an owner. p. 12

3 Activity design
46 activities and 467 fields, and Admin can add more. p. 17

4 Release & acknowledge
Vendors only work on parts they have accepted. p. 24

5 Data entry
Enter once, in the way that suits the job. p. 30

6 Validation & approvals
Every entry is checked, and deviations follow a chain. p. 41

7 Status & risk insight
Red, yellow, green, and what is likely to slip next. p. 46

8 Project view
See the work as a tree and as a chain. p. 49

9 Resource & travel planning
Balance PIC workload, and make each vendor trip count. p. 53

10 Monitoring & reporting
Dashboards for every role, down to the part. p. 56

Built on one part master · MRD-driven dates · 7 roles with their own view of the data · 46 configurable activities · a full history of who did what

7	46	467	10	42	9
roles	activities	fields	capabilities	screens in this manual	milestone types

How the capabilities fit together

Read left to right and top to bottom. Each step hands over to the next, and nothing is submitted or approved without a person.

1
Model Coordinator
Enters MRDs for each model

2
Department Co-ordinator
Sets the section template; adds dummy parts

3
Admin
Defines activities and fields in the Builder

4
PIC
Reviews the part and releases it to the vendor

5
Vendor
Acknowledges the part, or returns it with a reason

6
Vendor and PIC
Enter data in grids, the part form or via AI import

7
PIC, SIC, DPM
Validate entries; approve deviations

8
Everyone
Watches RYG, dashboards and lessons learnt

Who uses which capability

Capability	Vendor	PIC	SIC	DPM	Model Coordinator	Dept Co-ordinator	Admin
1. Plan & schedule		•	•	○	•	•	•
2. Parts & ownership		•	•	○		•	•
3. Activity design	○	○	○	○	○	○	•
4. Release & acknowledge	•	•	•	•			
5. Data entry	•	•	○	○			
6. Validation & approvals		•	•	•			○
7. Status & risk insight	○	•	•	•	○	○	•
8. Project view			○	•	•		•
9. Resource & travel planning		•	•	•			•
10. Monitoring & reporting	○	•	•	•	○	○	•

• main user ○ can view

How this manual is organised

Level 1
Page 1 gives the capabilities on one page. This page shows how they connect.

Level 2
One page per capability: what it does, the rules you can rely on, and who uses it.

Level 3
One page per screen: what it is for and how to use it.

Appendix
The 46 activities and their 467 fields, each with its form.

Status colours: Green = on track or complete, Yellow = due within 7 days, Red = overdue, Grey = awaiting an MRD or not started. All screens show mock data in a prototype; SAP, ENOVIA, E-Doc and LMS connections are simulated.

Contents

Foundation: roles, access and Home p. 4
- Home (Admin) p. 5
- Home (PIC) p. 6

1. Plan & schedule p. 7
- Models & MRDs p. 8
- Section Template p. 9
- Applicability p. 10
- Settings p. 11

2. Parts & ownership p. 12
- Parts & Audit: part numbers p. 13
- Add dummy part p. 14
- ECN transfer p. 15
- PIC Assignments p. 16

3. Activity design p. 17
- Activities p. 18
- Builder: activity list p. 19
- Builder: Basics p. 20
- Builder: Fields p. 21
- Builder: Flow p. 22
- Builder: Timeline p. 23

4. Release & acknowledge p. 24
- My Work: parts released to you p. 25
- Return parts to the PIC p. 26
- My Work: pending release p. 27
- My Work: released to vendor p. 28
- Part form: returned by vendor p. 29

5. Data entry p. 30
- My Work: Workspace p. 31
- My Work: Worklist p. 32
- Entry grid (Vendor) p. 33
- Entry grid (PIC) p. 34
- Part Workspace p. 35
- Bulk Entry Grid p. 36
- Activity page p. 37
- Part form p. 38
- AI import panel p. 39
- AI review: dropdown matches and failed updates p. 40

6. Validation & approvals p. 41
- Validation grid p. 42
- Deviation Tracker p. 43
- Part form: Actions p. 44
- Part form: History p. 45

7. Status & risk insight p. 46
- Lessons Learnt p. 47
- Vendor scorecards p. 48

8. Project view p. 49
- WBS / Project p. 50
- Activity Dependencies p. 51
- Set dependency p. 52

9. Resource & travel planning p. 53
- Manpower Planning: PIC load p. 54
- Manpower Planning: vendor visits p. 55

10. Monitoring & reporting p. 56

Appendix A. Activity reference p. 57
- 46 activities, 467 fields, one form each

Appendix B. Sign-off summary p. 138


FOUNDATION ALL CAPABILITIES

Foundation: roles, access and Home


Seven roles share one application. The menu, the data and the actions on screen follow the role.

Role	What the role does	Main screens
Vendor	Acknowledges or returns released parts, then enters its own fields for its own parts.	My Work, entry grid, Activities
PIC	Reviews and releases parts, enters PIC fields, validates vendor entries, marks Not applicable, raises deviations.	My Work, Part Workspace, Bulk Entry Grid, Parts & Audit, Applicability
SIC	Section-level review; assigns PICs; validates and approves in the deviation chain.	Activities, PIC Assignments, Deviation Tracker, WBS
DPM	Tracks completion across vendors; approves deviations; edits dependencies.	Dashboards, Lessons Learnt, Dependencies, Manpower
Model Coordinator	Enters each model and its milestone MRDs; every planned date follows from these.	Models & MRDs, WBS, Dependencies
Department Co-ordinator	Sets which activities apply to the section and their MRD offsets; adds dummy part numbers.	Section Template, Parts & Audit, PIC Assignments
Admin	Designs activities and flows, maintains sections and milestones.	Builder, Settings, all other screens

PIC, SIC and Department Co-ordinator work in section NP1; the Vendor sees only its own parts; DPM, Model Coordinator and Admin are not restricted. Switch role from the Home page or the top-right menu.




Home (Admin) · p. 5



Home (PIC) · p. 6

Home (Admin)

Used by: Admin

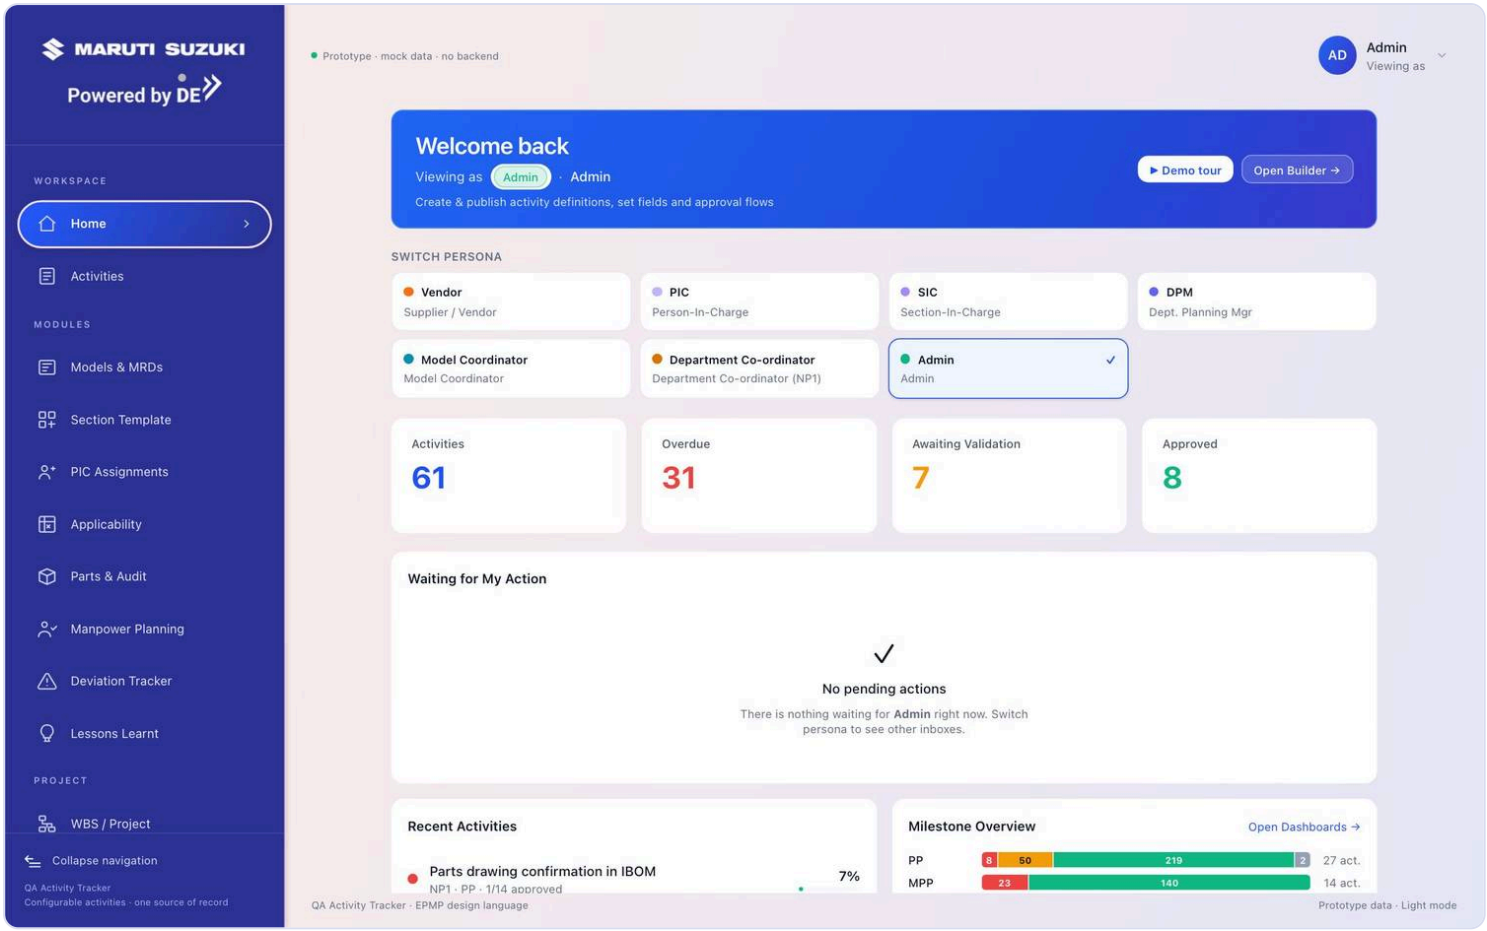

Purpose

The landing page. It shows who you are viewing as, a persona switcher, headline counts and the work waiting for you.


> **Note.** Admin has no inbox of its own, so “Waiting for My Action” is empty here.

How to use

1. Use the persona cards to switch role and see that role’s menu and inbox.
2. Read the four tiles: Activities, Overdue, Awaiting Validation, Approved.
3. “Demo tour” walks through the main flows step by step.

Home (PIC)

Used by: PIC

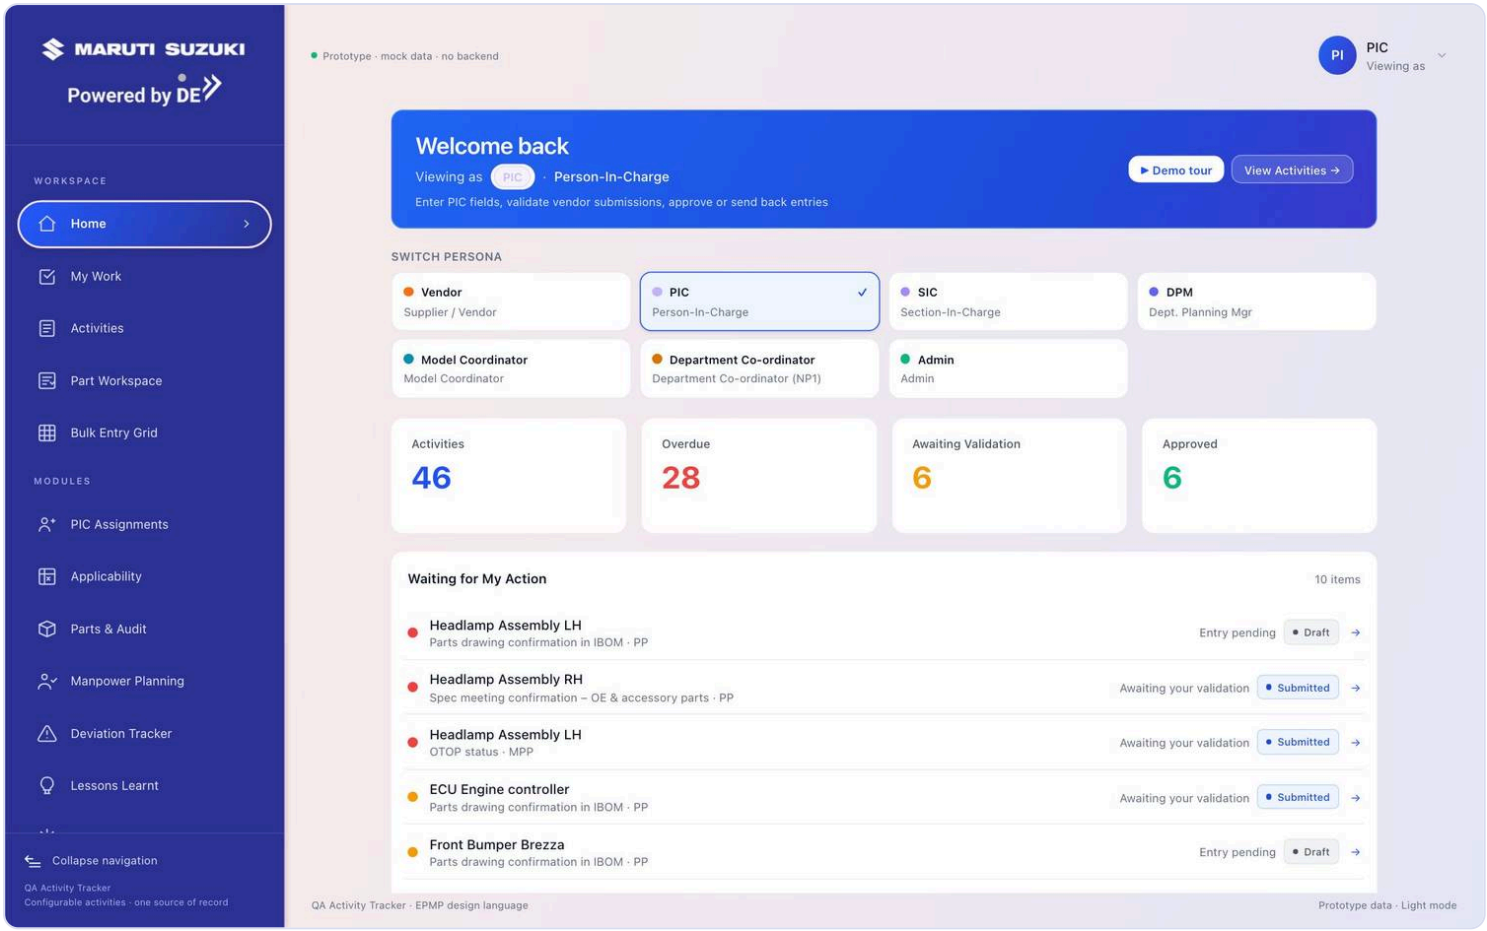

Purpose

The same page for a PIC. The inbox lists vendor submissions to validate and entries still pending.

> **Note.** Counts come from the current data and follow the role's scope.

How to use

1. Each row shows part, activity and milestone, and its state (Draft, Submitted).
2. The coloured dot shows timeline status against the planned end date.
3. Click a row to open the entry.

CHAPTER 1 PLAN

Plan & schedule

Dates come from the model schedule, not from anyone’s memory.

What it does

Every planned date is derived. The Model Coordinator enters the MRD of each model milestone. The Department Co-ordinator decides which activities apply to the section, under which milestone, with start and end as MRD ± days. PICs mark the parts an activity does not apply to.

What you can do


- MRD per model for PP, MPP, Pilot and SOP, plus Jig, Kani, Weld, Engine and Assembly.
- Section Template: one row per activity with a milestone and start / end offsets; edit, duplicate, remove or add rows.
- Dates recalculate the moment an MRD or offset changes; an activity with no MRD shows “Awaiting MRD”.
- Applicability matrix: PIC ticks the parts an activity does not apply to; changes are staged until applied.
- Settings: add or rename sections and milestones (PP, MPP, Pilot and SOP are mandatory).

Rules you can rely on


- Planned dates are never typed by hand.
- Parts marked Not applicable are left out of completion % and RYG.
- Only a PIC can mark Not applicable, and only for activities where Admin has allowed it in the Builder; PIC, SIC and Admin can reverse a mark.
- Sections and roles are scoped: PIC, SIC and Department Co-ordinator work in NP1.

Used by


Model Coordinator, Department Co-ordinator, PIC, SIC, Admin




Models & MRDs · p. 8



Section Template · p. 9




Applicability · p. 10



Settings · p. 11

C1A Models & MRDs

Used by: Model Coordinator, Admin

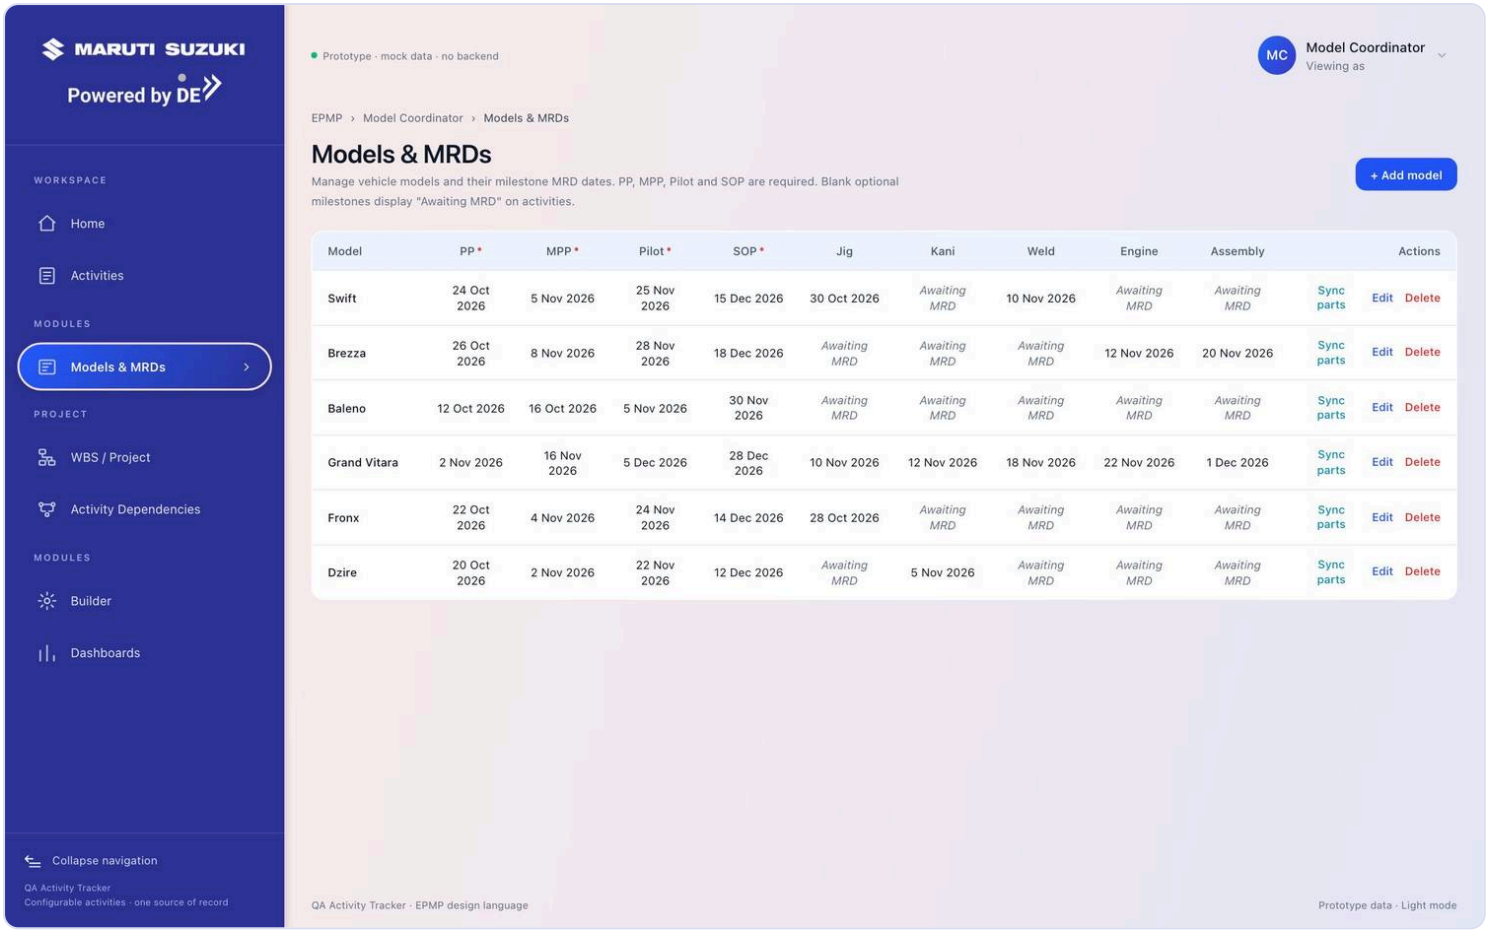

Purpose

Maintain vehicle models and the MRD date of every milestone. PP, MPP, Pilot and SOP are required; other milestones show “Awaiting MRD” until a date is set.


> **Note.** All activity due dates recalculate from these dates.

How to use

1. “Add model” creates a model and its milestone dates.
2. “Edit” changes MRD dates; “Delete” removes a model.
3. “Sync parts” refreshes the model’s part list.

Section Template

Used by: Department Co-ordinator, Admin

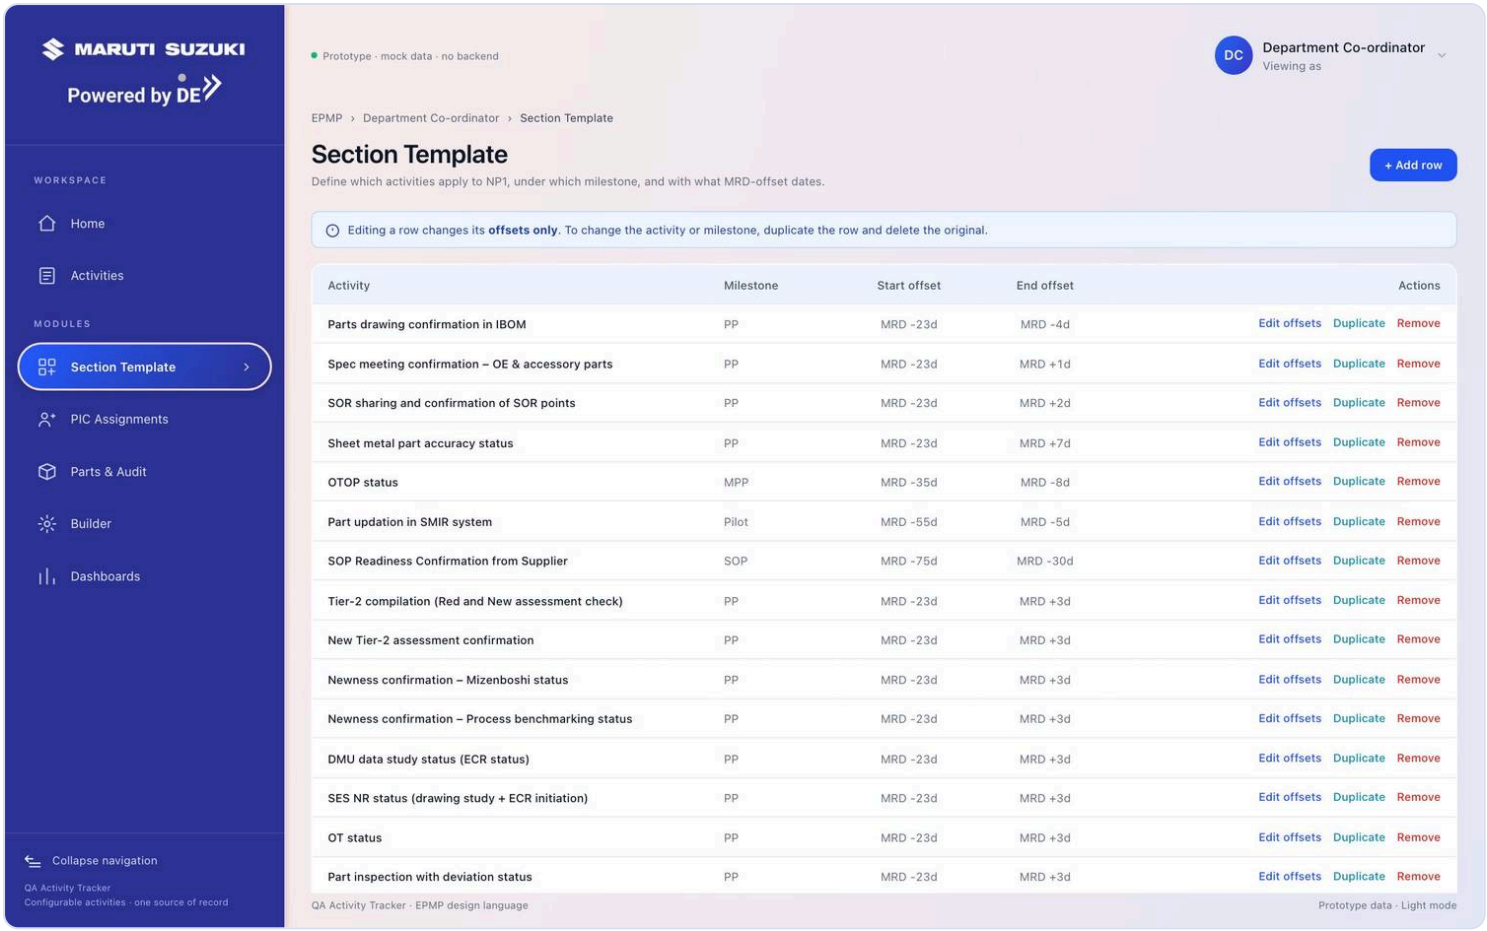

Purpose

Defines which activities apply to the section, under which milestone, and with what offsets from the MRD.


> **Note.** Editing a row changes its offsets only.

How to use

1. Read each row: activity, milestone, start offset, end offset (days from MRD).
2. “Edit offsets” changes the start and end of that row; “Duplicate” copies it; “Remove” deletes it; “Add row” adds an activity.
3. To change the activity or milestone, duplicate the row and delete the original.

Applicability

Used by: PIC, SIC, Admin

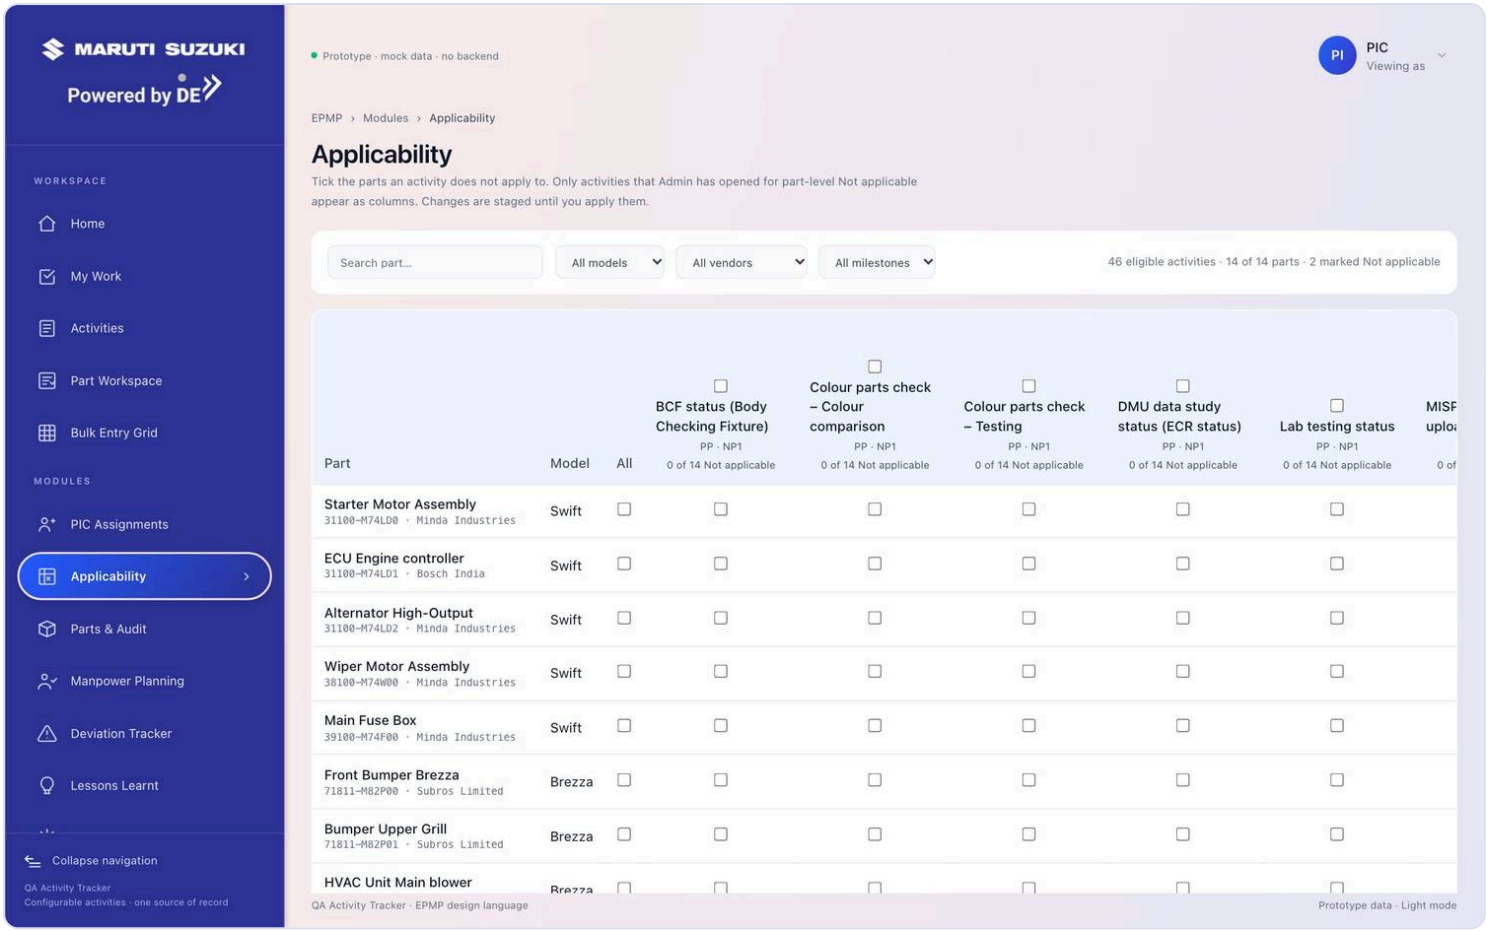

Purpose

Tick the parts for which an activity does not apply. Only activities that Admin has opened for part-level Not applicable appear as columns.


> **Note.** Not-applicable parts are excluded from completion % and RYG.

How to use

1. Search or filter by model, vendor or milestone.
2. Tick a cell to mark a part not applicable for that activity; the “All” column ticks a whole row.
3. Apply the staged changes to save them.

Settings

Used by: Admin

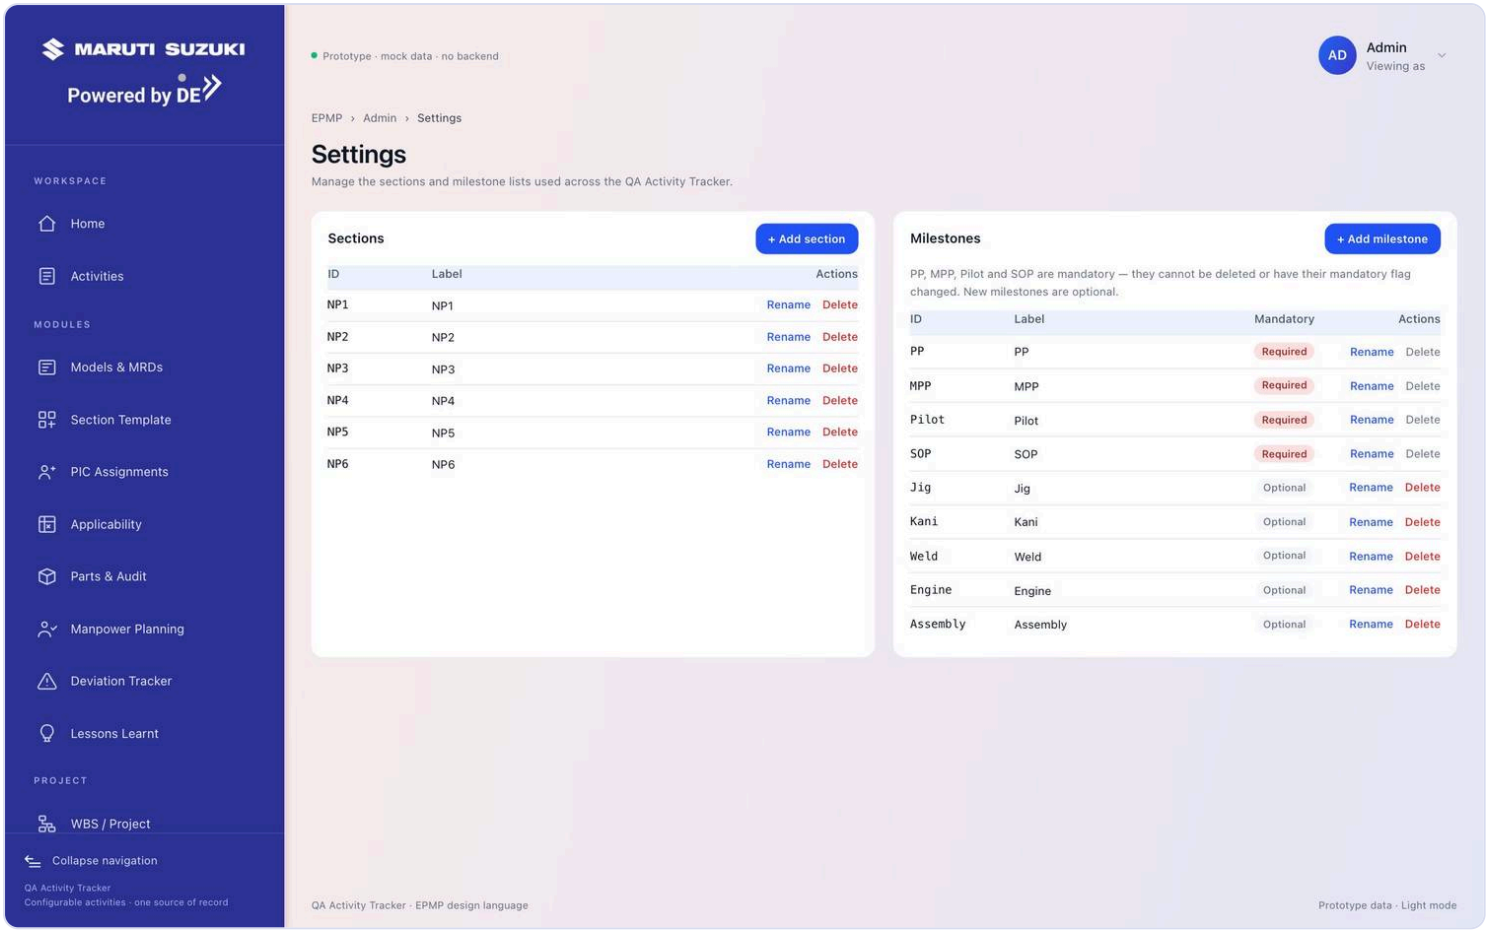

Purpose

The master lists used across the tracker: sections and milestones.

How to use

1. Sections: add, rename or delete.
2. Milestones: add new MRD types. PP, MPP, Pilot and SOP are required and cannot be deleted; the others are optional.

CHAPTER 2 PLAN

Parts & ownership

One part master, and every part has an owner.

What it does

The part list is the base of everything. Parts arrive from SAP; when SAP has no number yet, the Department Co-ordinator adds a dummy part. Each part has a PIC, and a part's history can move to its ECN-revised number.

What you can do


- Part numbers with model, section, type (New Part / ECN), origin (SAP / Dummy), status, release state and vendor details.
- Add dummy part (Department Co-ordinator): part, model, section, vendor, department, type and an optional PIC.
- ECN transfer: moves every activity entry to the revised part number and marks the old part superseded.
- PIC Assignments: SAP PIC versus current PIC, effective-dated reassignment, and a "Who did what" report.
- Audit report: which PIC completed what, and part-number events (created, transferred).

Rules you can rely on


- Dummy parts are flagged "Dummy" until SAP issues a number.
- ECN transfer is allowed only within the same vendor.
- A later PIC assignment replaces the earlier one from its effective date; only SIC or Admin can assign.
- Dummy part numbers can be added only by the Department Co-ordinator (and Admin).

Used by


PIC, SIC, DPM, Department Co-ordinator, Admin




Parts & Audit: part numbers · p. 13



Add dummy part · p. 14




ECN transfer · p. 15



PIC Assignments · p. 16

Parts & Audit: part numbers

Used by: PIC, SIC, DPM, Department Co-ordinator, Admin

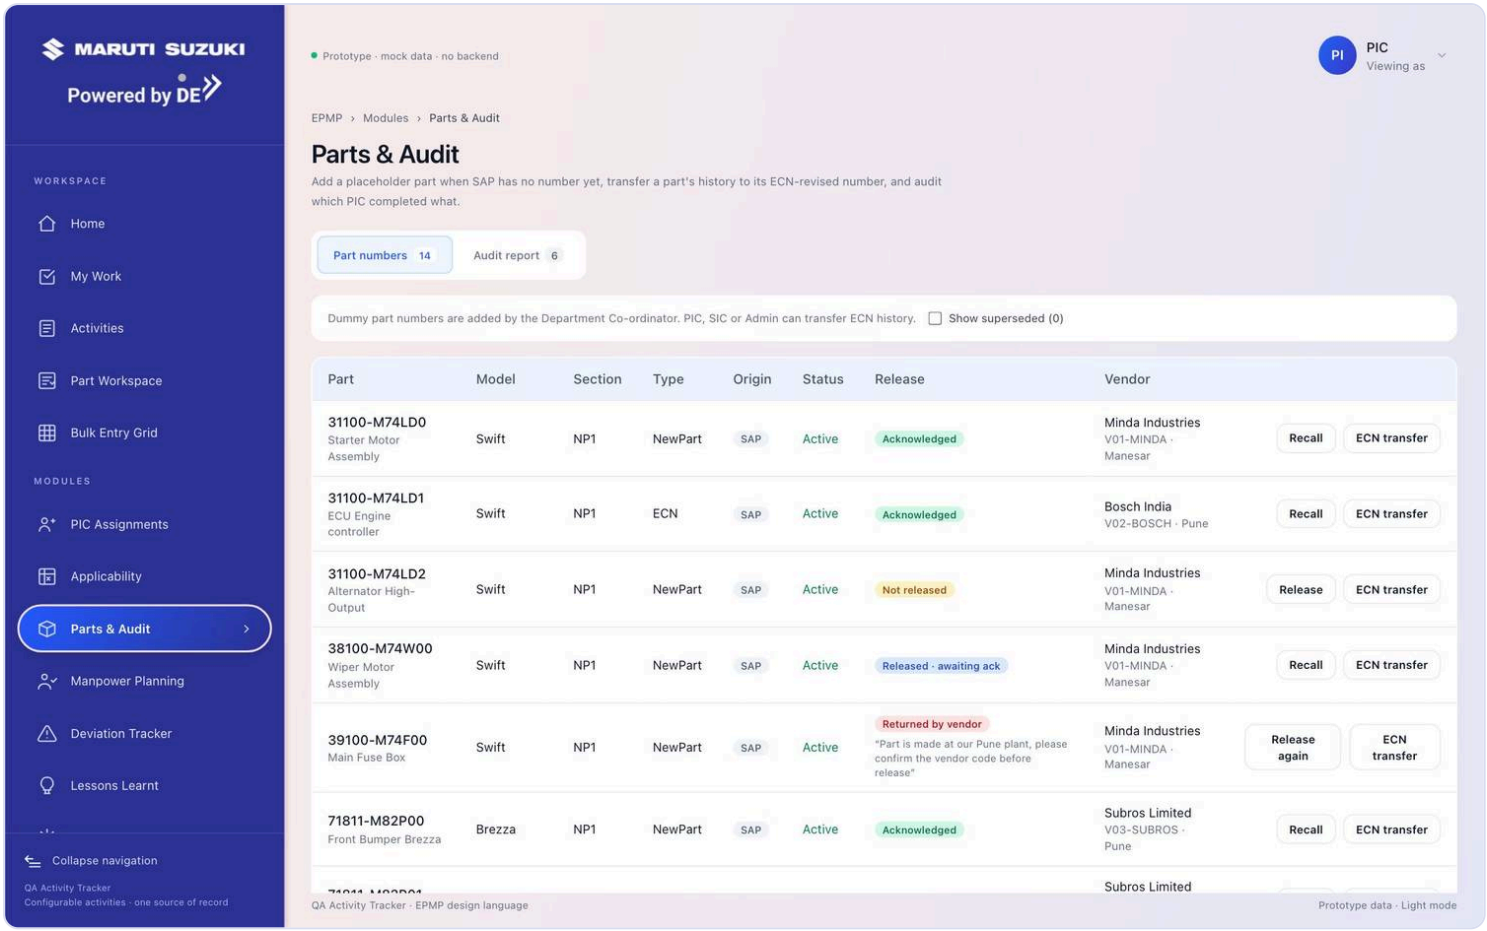

Purpose

The part master with vendor details and the release state of every part.


> **Note.** Dummy parts are added only by the Department Co-ordinator; other roles see a hint instead of the button.

How to use

1. The Release column shows Not released, Released · awaiting ack, Acknowledged, or Returned by vendor with the vendor's reason.
2. "Release", "Recall" or "Release again" changes the state.
3. "ECN transfer" moves a part's history to its ECN-revised number.
4. "Show superseded" includes replaced parts.

C2B Add dummy part

Used by: Department Co-ordinator

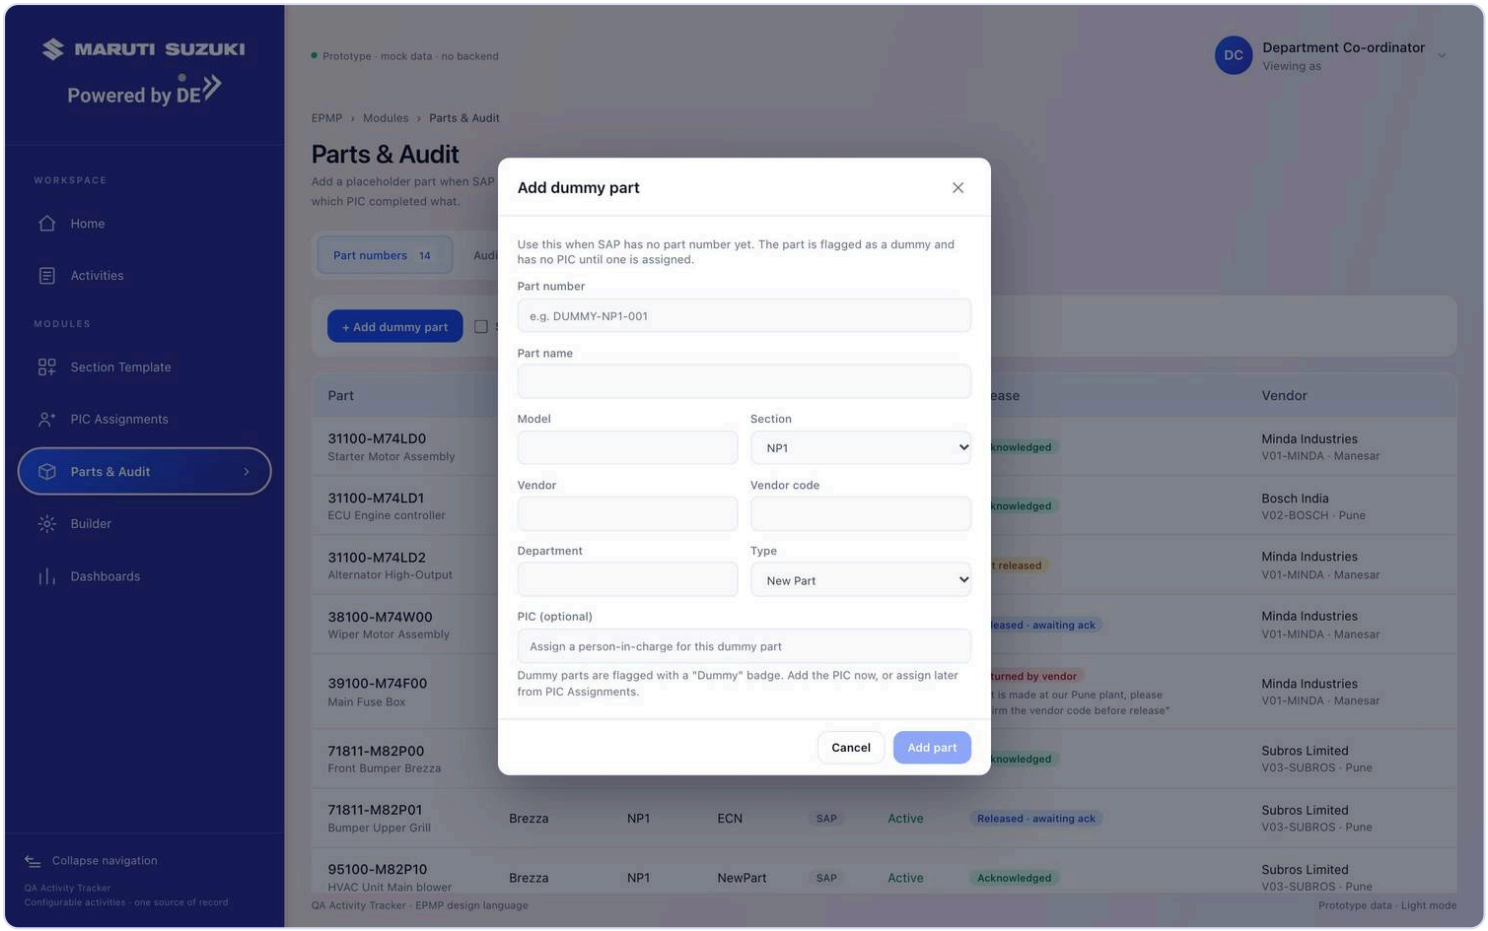

Purpose

Create a placeholder part when SAP has no part number yet. It is flagged “Dummy” until replaced.

> **Note.** All required fields must be filled before “Add part” is enabled.


How to use

1. Enter part number and name, model, section, vendor, vendor code and department.
2. Choose the type (New Part or ECN) and optionally assign a PIC.
3. Click “Add part”.

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐

ECN transfer

Used by: PIC, SIC, Admin

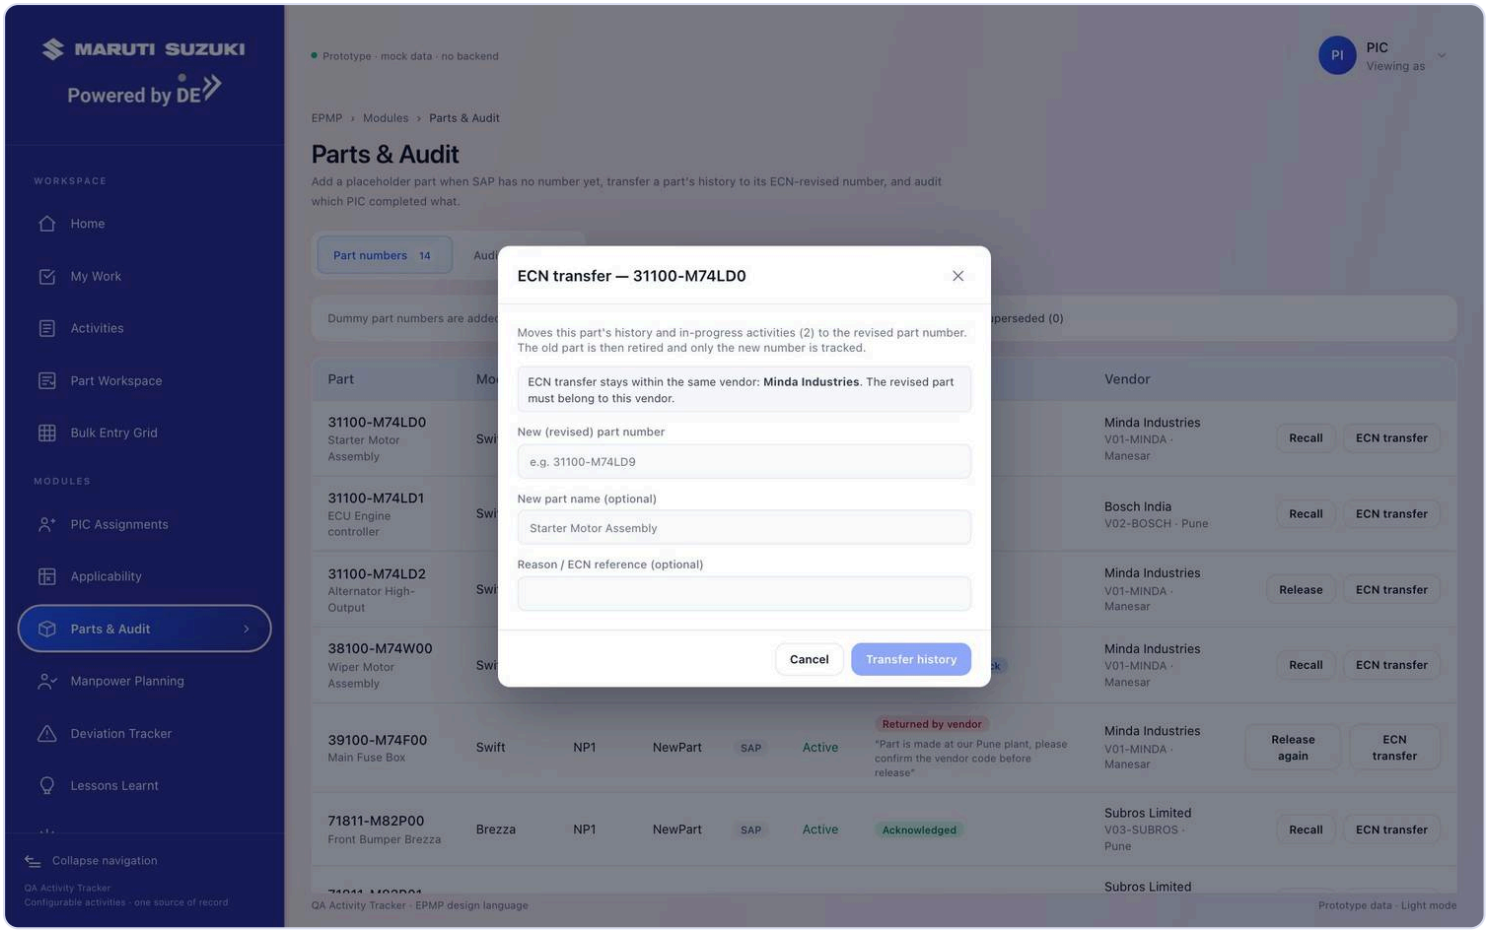

Purpose

Moves the full activity history of a part to its ECN-revised number.


> **Note.** The new part must belong to the same vendor as the old one.

How to use

1. Choose “ECN transfer” on the old part.
2. Enter the new part number; the part name and a reason are optional.
3. Confirm. Every entry is cloned to the new part and the old part is marked superseded.

PIC Assignments

Used by: SIC, DPM, Department Co-ordinator, PIC, Admin

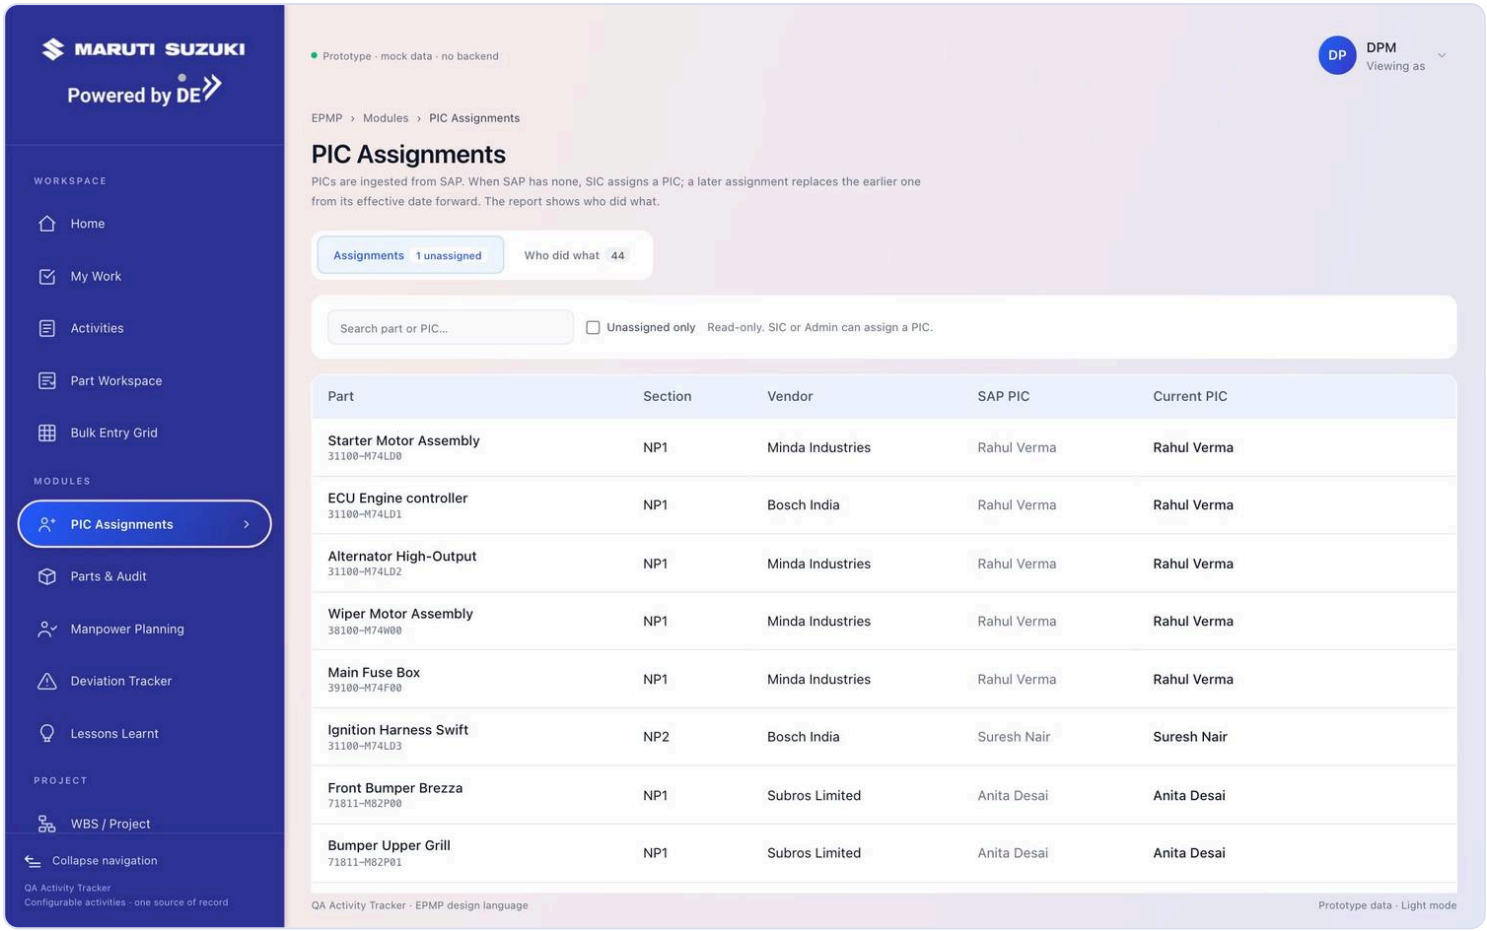

Purpose

Shows the PIC SAP holds and the current PIC for every part, and the history of who did what.

> **Note.** Only SIC or Admin can assign a PIC; other roles see the list read-only.

How to use

1. Search by part or PIC, or tick “Unassigned only”.
2. Compare SAP PIC with Current PIC.
3. “Who did what” tab reports the work each PIC completed.

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐

CHAPTER 3 PLAN

Activity design

46 activities and 467 fields, and Admin can add more.

What it does

Activities are data, not code. Each activity defines its fields, who enters and validates each field, where the value comes from, the approval flow and a timeline template. The 46 seeded activities follow the client field-validation sheet.

What you can do


- Activities catalogue by milestone with planned dates, part count, completion and RYG.
- Builder in five steps: Basics, Fields, Flow, Timeline, Review, with a live preview and auto-save.
- Field types: text, long text, number, percent, date, yes / no, dropdown, multi-select, file, flag, table.
- Field source badges: Manual, Mapping, Calculated, ENOVIA, SAP, E-Doc.
- Options per activity: PIC may mark parts Not applicable; vendor may set a planned timeline.

Rules you can rely on


- Activity IDs stay stable, so history and dashboards keep working when fields change.
- Dropdown values are fixed lists; free text cannot be saved into a dropdown.
- Planned dates are not set in the Builder; they come from the Section Template.
- Only Admin can create or edit activity definitions.

Used by


Admin (design); everyone (catalogue)




Activities · p. 18




Builder: activity list · p. 19




Builder: Basics · p. 20



Builder: Fields · p. 21




Builder: Flow · p. 22



Builder: Timeline · p. 23

Activities

Used by: All roles

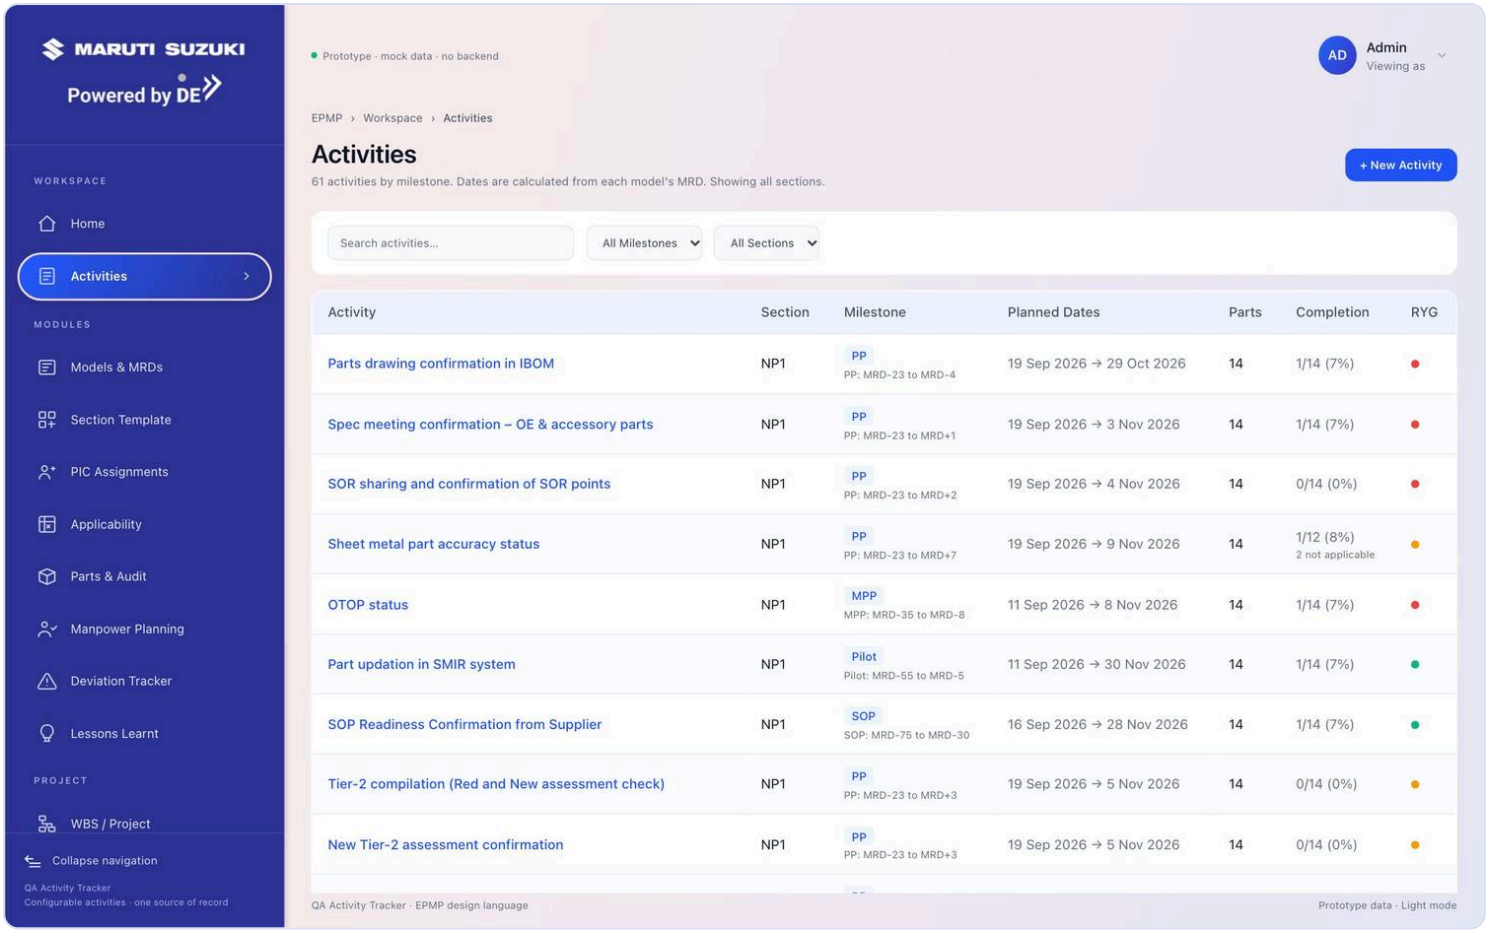

Purpose

The catalogue of activity definitions by milestone for the section. Dates are calculated from each model's MRD.

> **Note.** The list shows 61 rows because some of the 46 activities appear under more than one milestone.


How to use

1. Search by name or filter by milestone and section.
2. Each row shows milestone and offsets, planned dates, parts, completion and RYG.
3. Click an activity to open its part-wise page.
4. "New Activity" opens the Builder.

C3B

Builder: activity list

Used by: Admin

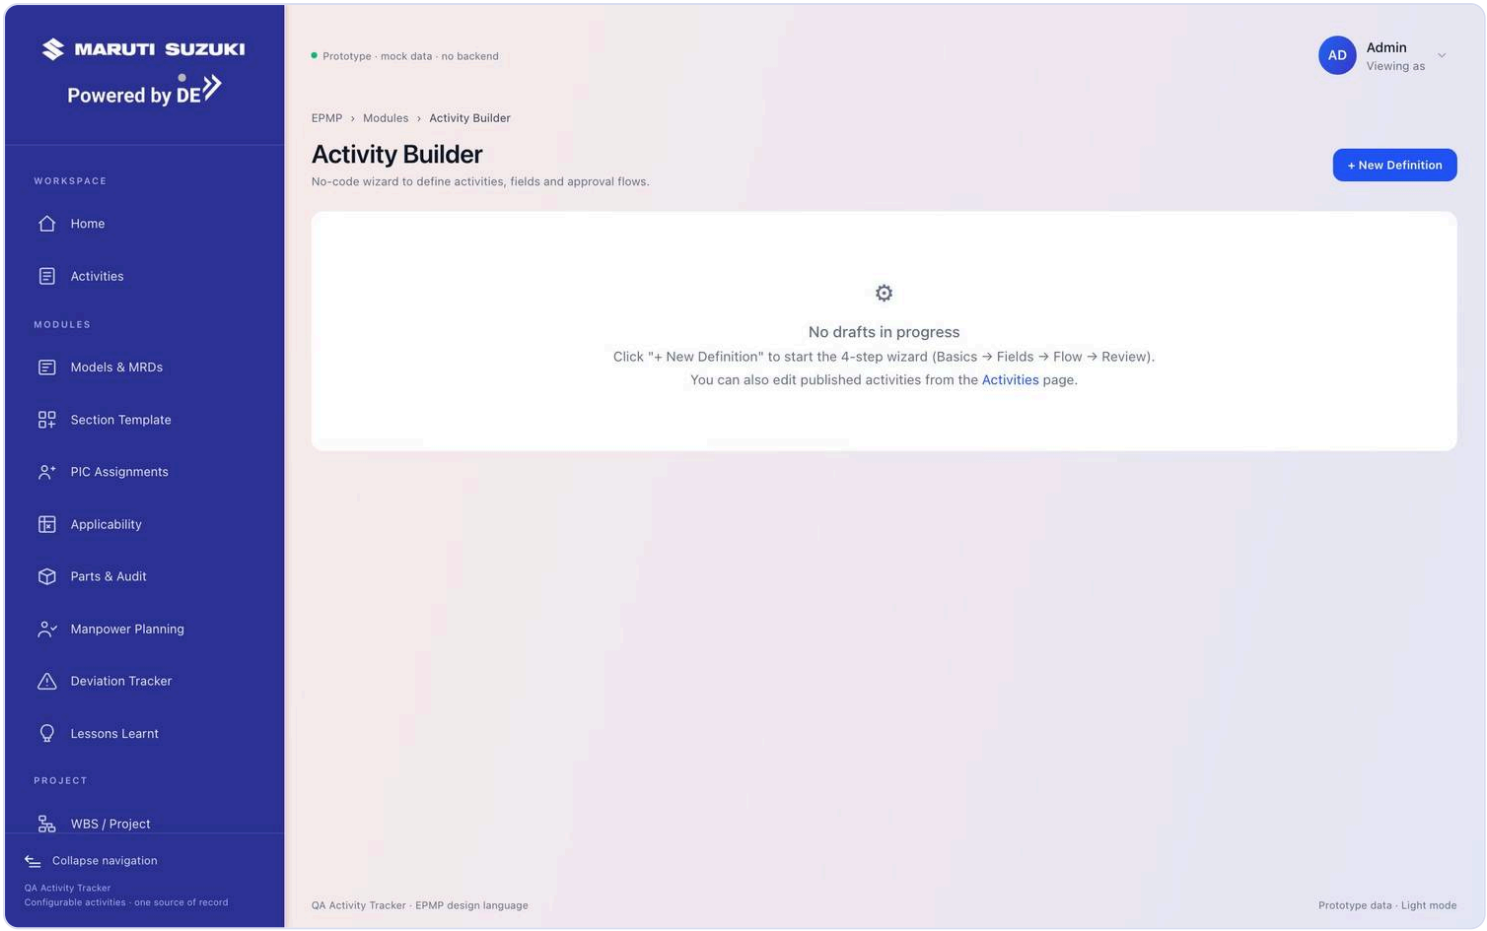

Purpose


The Activity Builder is a no-code wizard to define activities, fields and approval flows. Drafts in progress are listed here.

How to use

1. “New Definition” starts the wizard.
2. Open an existing activity from the Activities page to edit it.

Builder: Basics

Used by: Admin

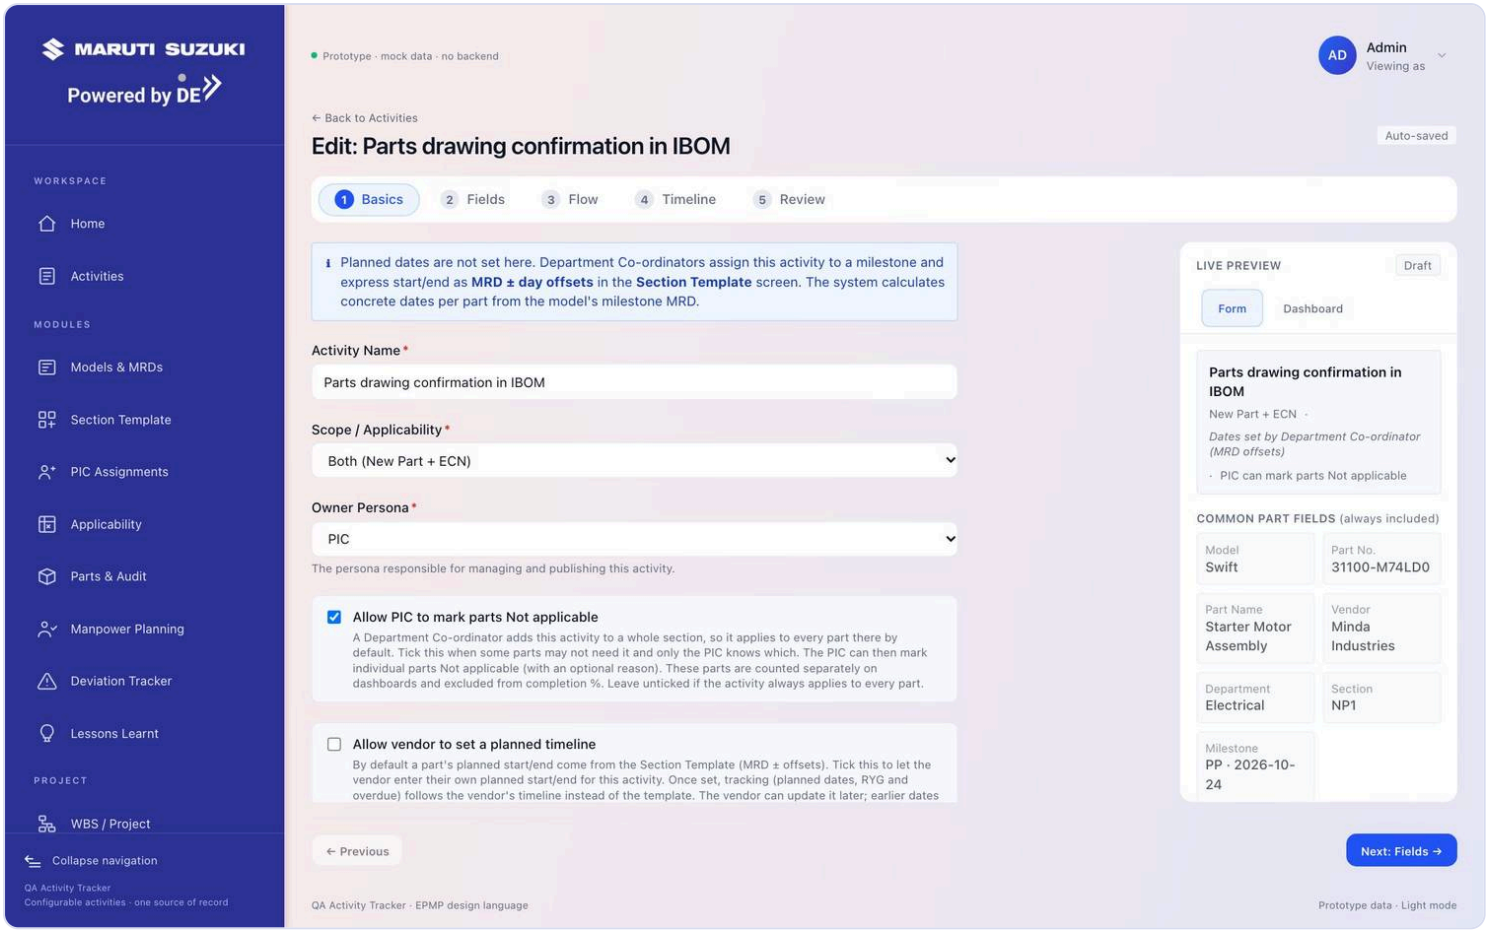

Purpose

Step 1: name, scope, owner persona and options. Planned dates are not set here.


> **Note.** Shown as an edit of an existing activity.

How to use

1. Enter the activity name.
2. Choose the scope (for example Both: New Part + ECN) and the owner persona.
3. Tick “Allow PIC to mark parts Not applicable” or “Allow vendor to set a planned timeline” where needed.

Builder: Fields

Used by: Admin

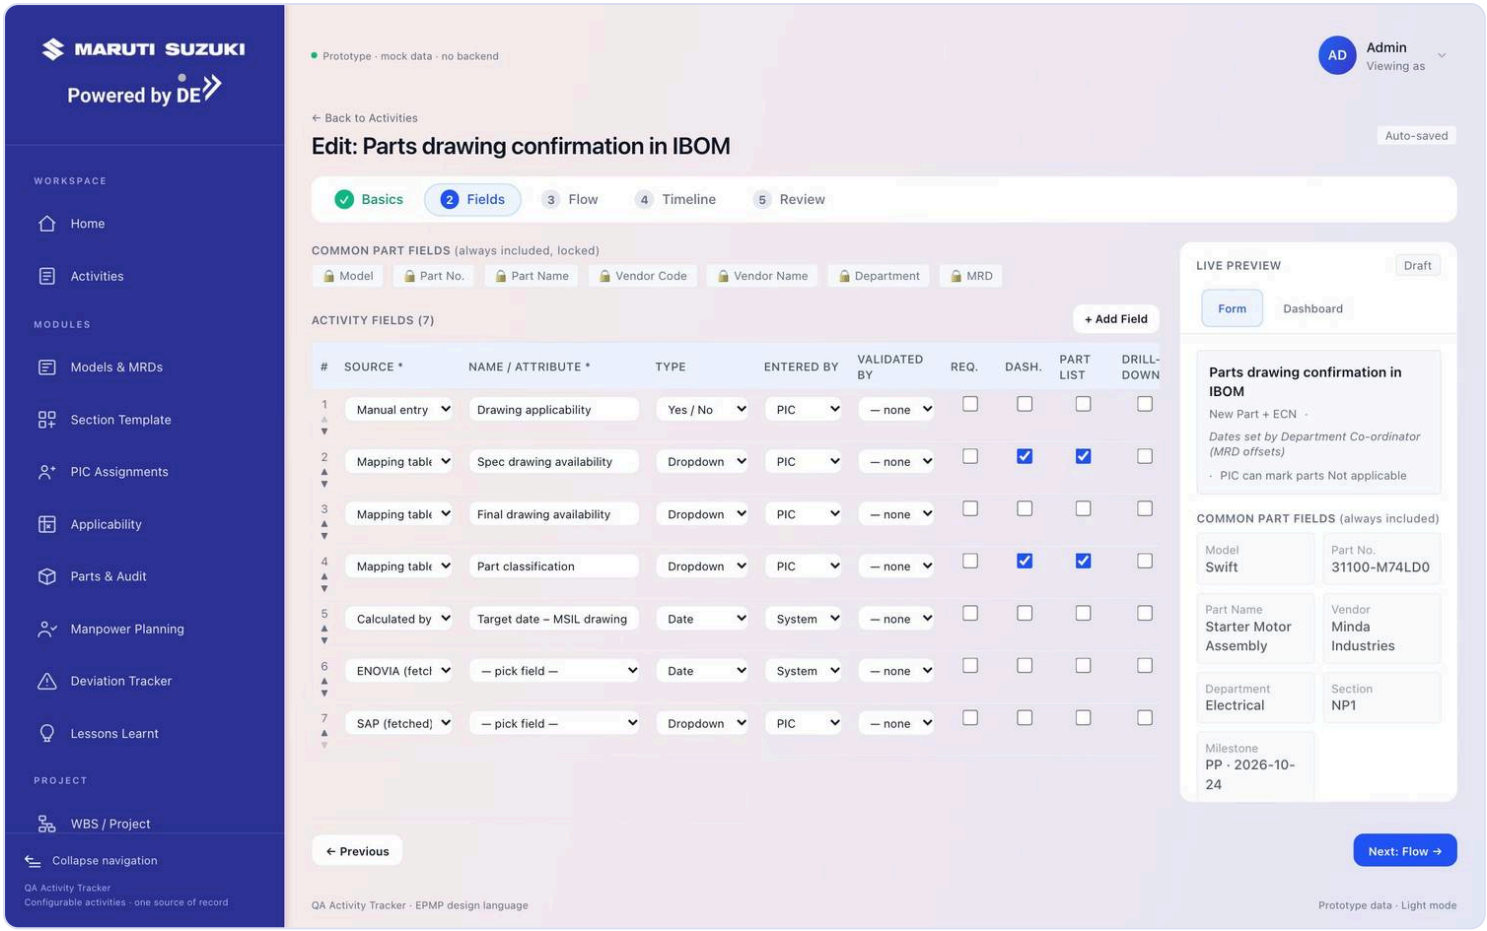

Purpose

Step 2: define the fields of the activity. Common part fields are always included and locked.


> **Note.** Sources include manual entry, mapping table, calculated, ENOVIA and SAP.

How to use

1. “Add Field” creates a row; choose source, name, type, who enters it and who validates it.
2. Tick Req., Dash., Part list or Drill-down as needed.
3. Reorder with the arrows; the live preview shows the form.

Builder: Flow

Used by: Admin

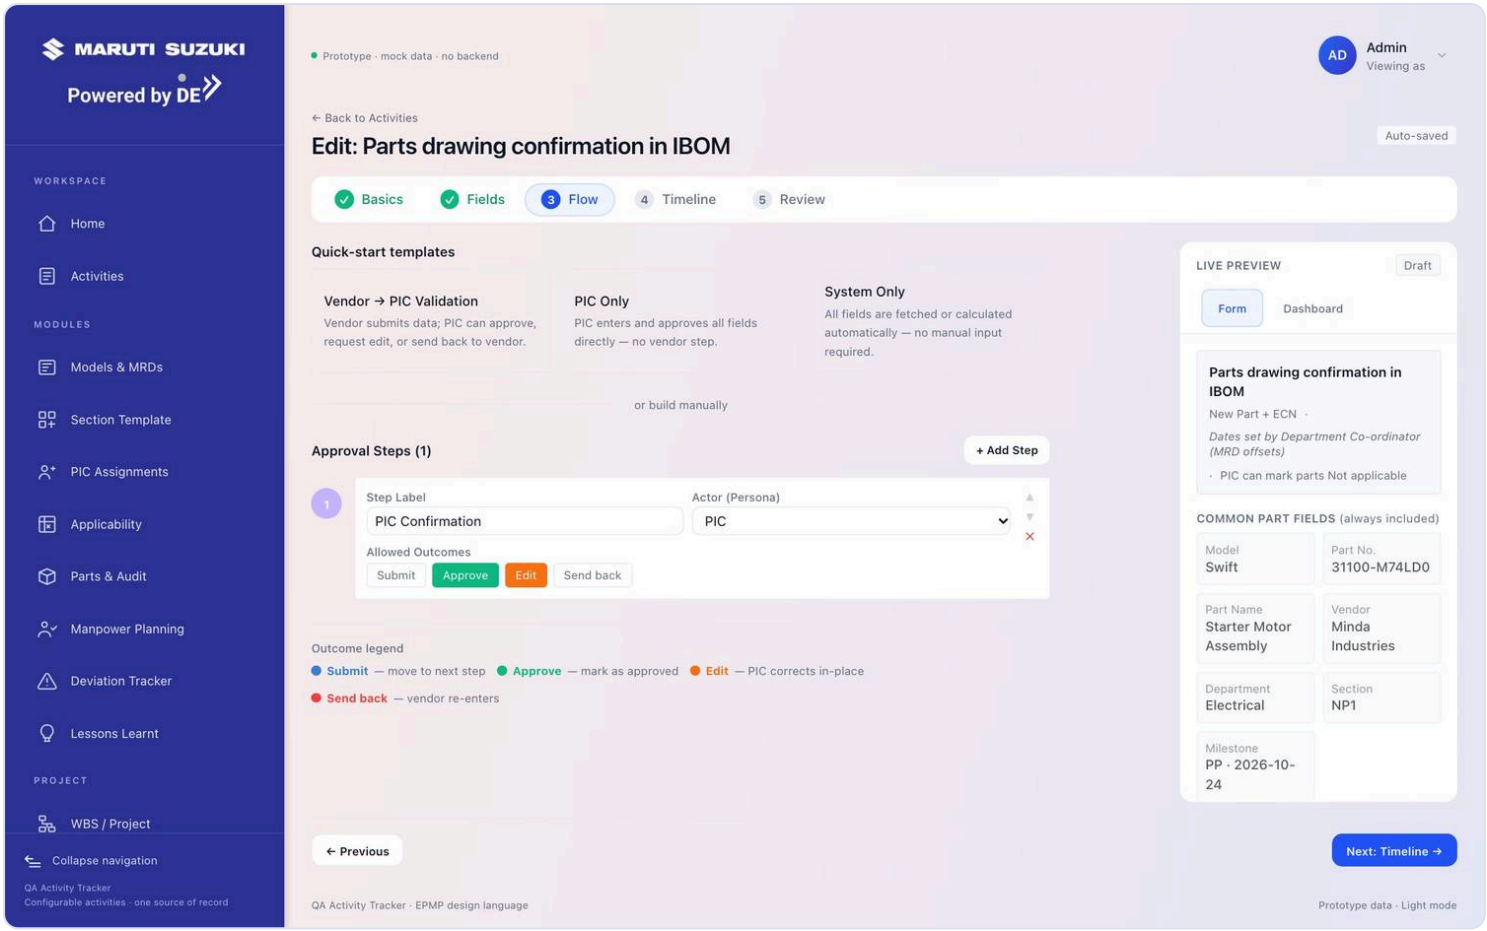

Purpose


Step 3: the approval flow of the activity.

How to use

1. Pick a quick-start template: Vendor → PIC Validation, PIC Only or System Only.
2. Or build manually: add steps, set the label and the actor.
3. Choose the allowed outcomes: Submit, Approve, Edit, Send back.

Builder: Timeline

Used by: Admin

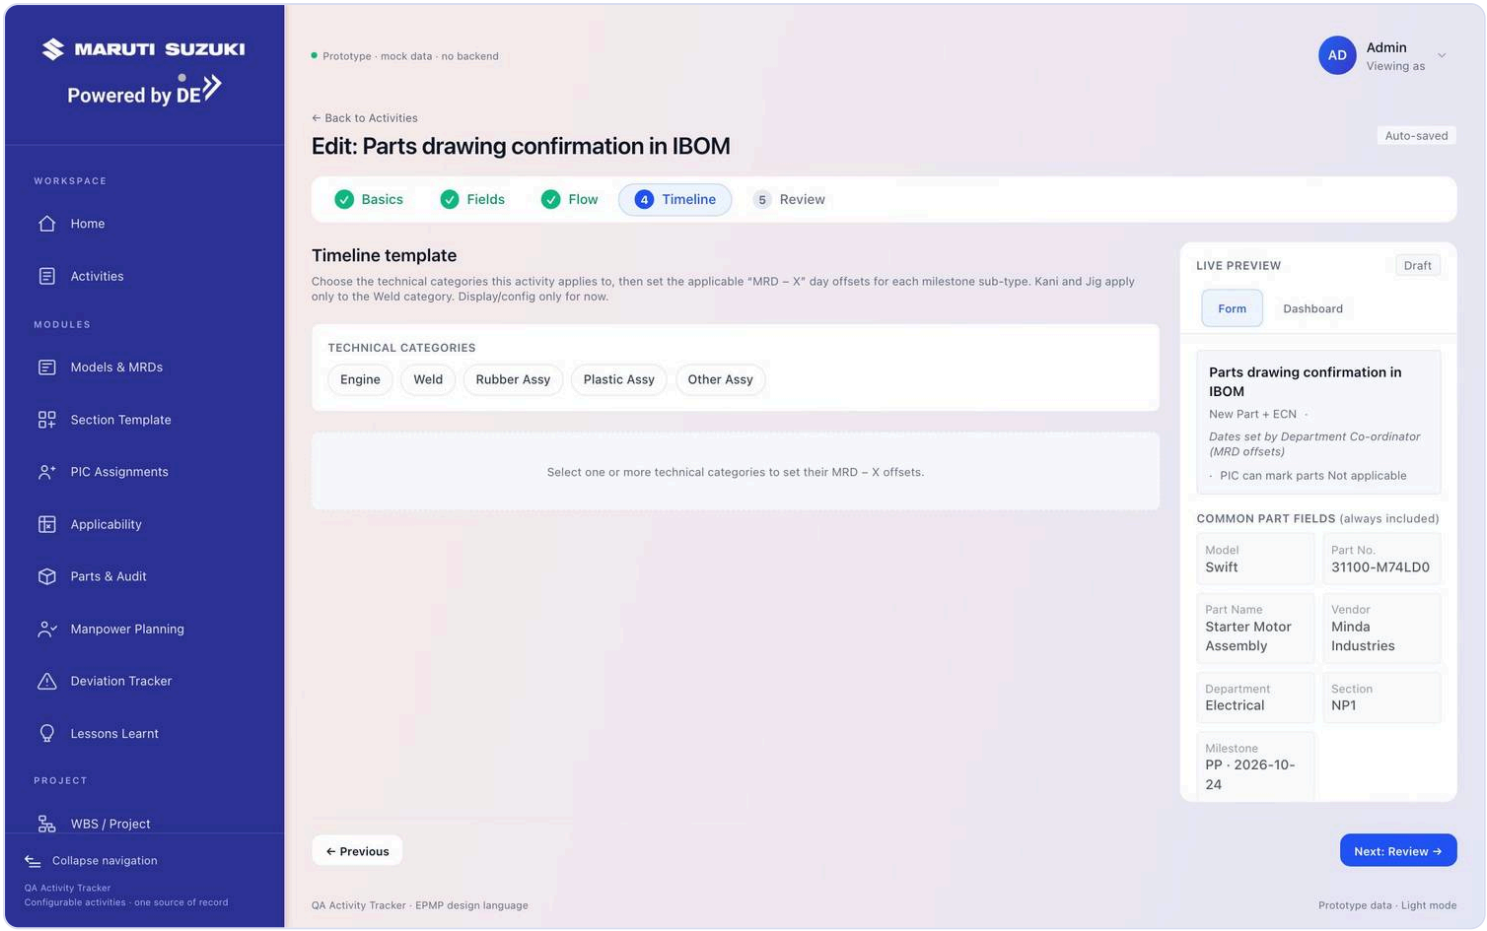

Purpose

Step 4: timeline template per technical category.

> **Note.** The Review step then summarises everything before publishing.

How to use

1. Choose the technical categories the activity applies to.
2. Set the MRD – X day offsets for each milestone sub-type.

CHAPTER 4 RUN

Release & acknowledge

Vendors only work on parts they have accepted.

What it does

The PIC reviews a part and releases it to the vendor. The vendor must then acknowledge the part or return it with a reason, for one part or several together. Everyone can see how many parts are released, pending and returned.

What you can do


- Release, Recall and Release again, from Parts & Audit, the part form, or in bulk from My Work.
- Vendor panel in My Work: Awaiting my acknowledgement, Acknowledged, Returned by me, with tick-box selection.
- Acknowledge selected, or Return selected with a mandatory reason.
- PIC panel in My Work: Released to vendor (with awaiting and acknowledged counts), Pending release, Returned by vendor.
- Release state and the vendor's reason show on the part list and the part form; each step is written to the history.

Rules you can rely on


- A vendor cannot enter data on a part until it has acknowledged it.
- A returned part goes back to the PIC and stays out of the vendor's worklist until released again.
- A new release always reopens the acknowledge-or-return question.
- The vendor never sees parts the PIC has not released.

Used by


PIC, SIC, DPM (release); Vendor (acknowledge or return)




My Work: parts released to you · p. 25




Return parts to the PIC · p. 26



My Work: pending release · p. 27



My Work: released to vendor · p. 28




Part form: returned by vendor · p. 29

C4A

My Work: parts released to you

Used by: Vendor

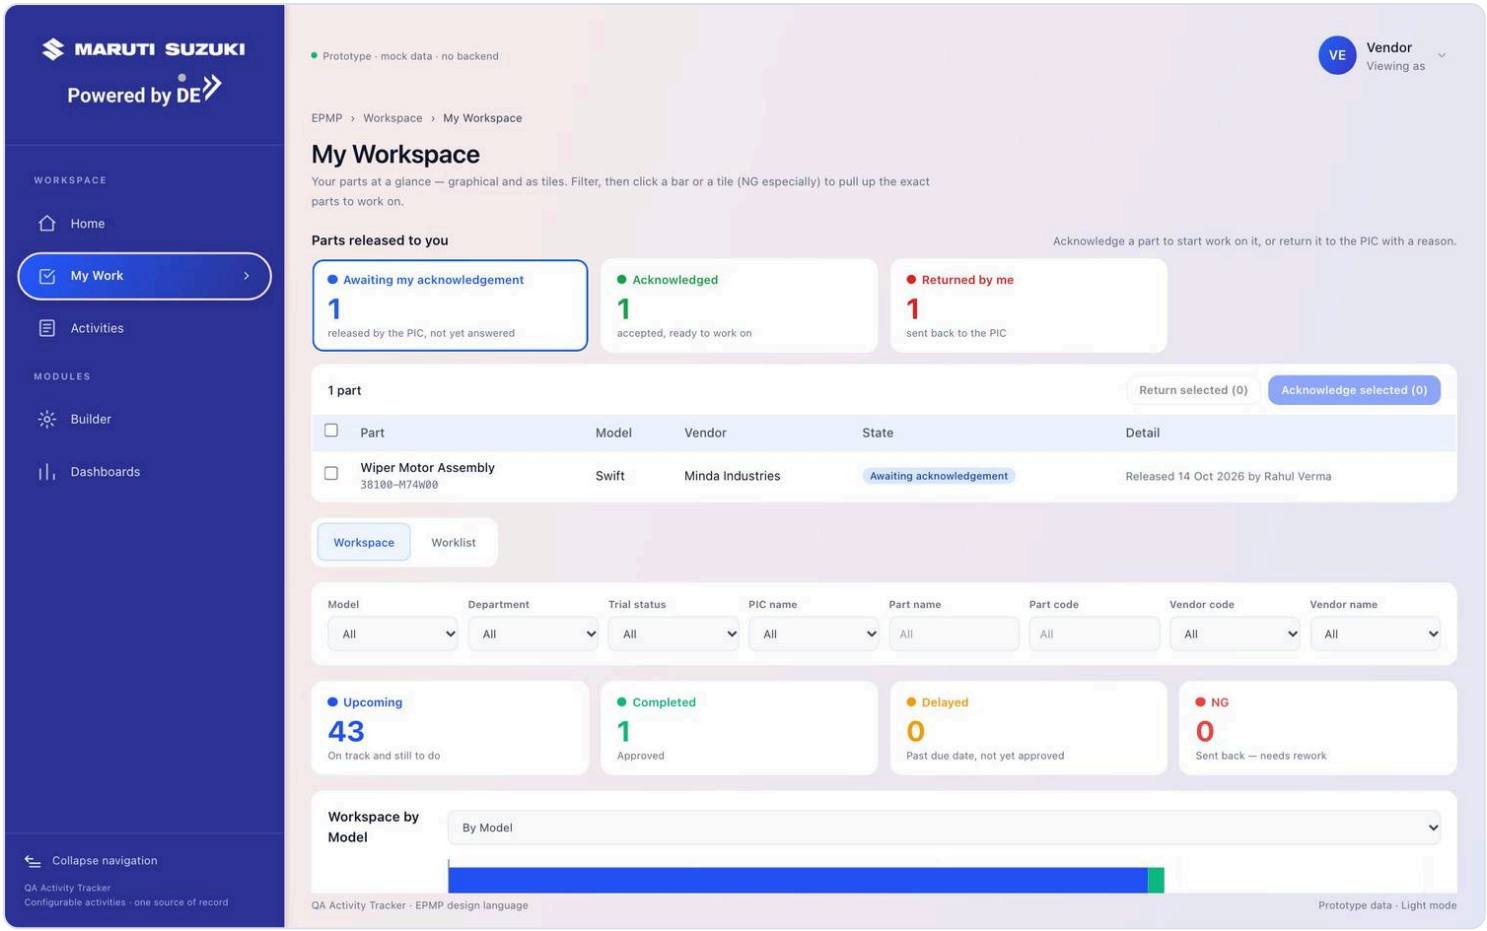

Purpose

The vendor's release panel. Parts the PIC released wait here until the vendor acknowledges or returns them.

> **Note.** Parts that are not released are not shown to the vendor at all.


How to use

1. Read the tiles: Awaiting my acknowledgement, Acknowledged, Returned by me.
2. Tick one or several parts in the list.
3. "Acknowledge selected" accepts them; they appear in your worklist.

C4B

Return parts to the PIC

Used by: Vendor

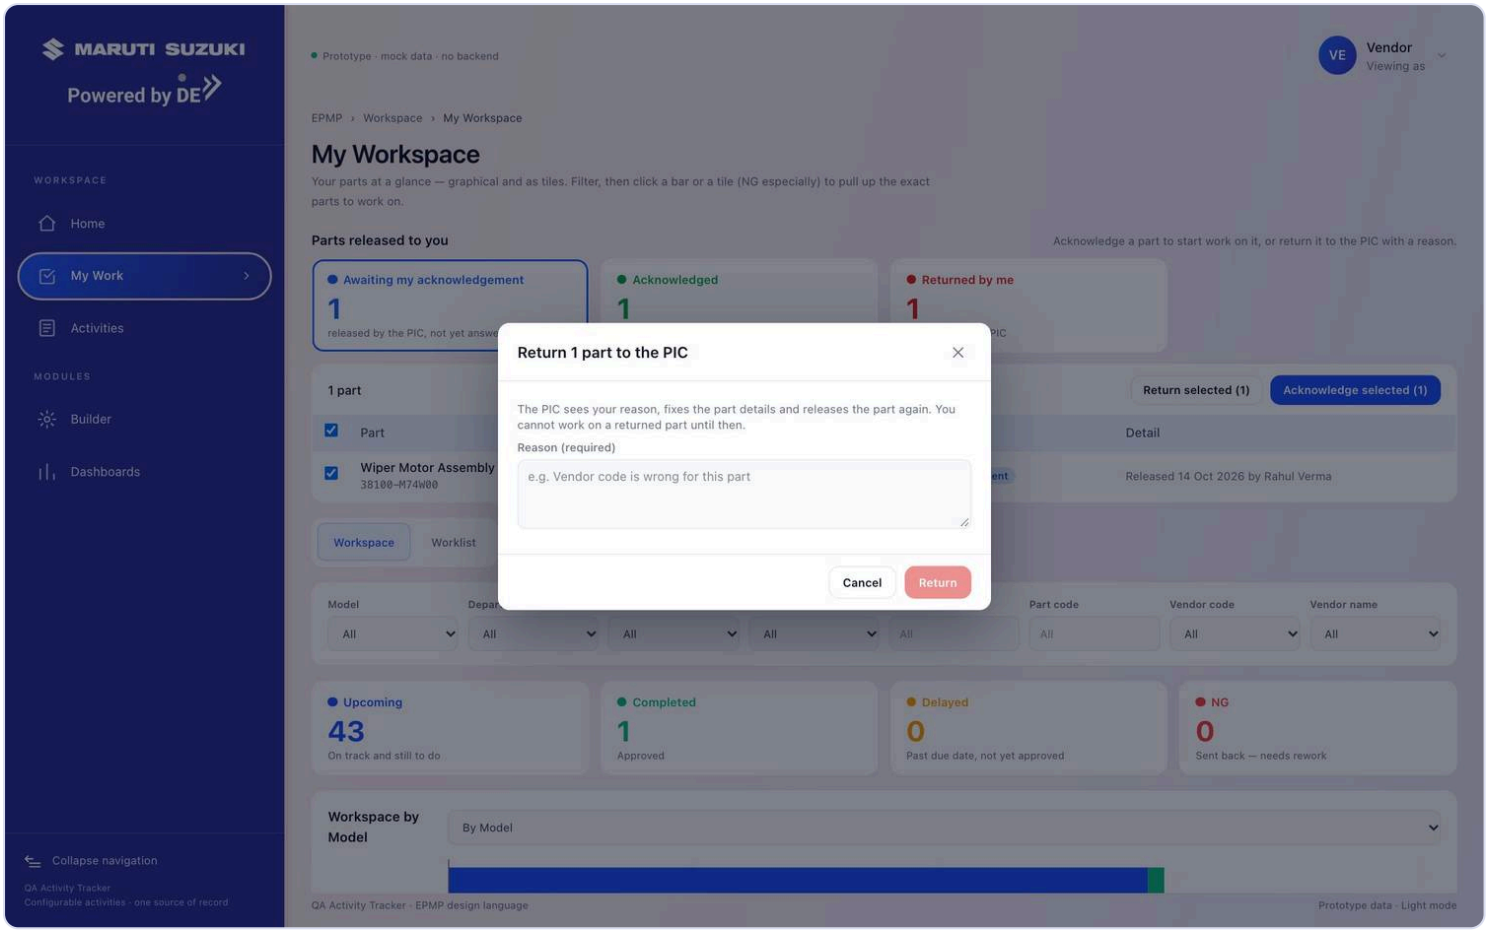

Purpose

Returns the selected parts to the PIC with a reason.


> **Note.** A returned part is not worked on until it is released again.

How to use

1. Tick the parts, then “Return selected”.
2. Type the reason (required).
3. Click “Return”. The PIC sees the reason and releases the parts again once fixed.

My Work: pending release

Used by: PIC, SIC, DPM

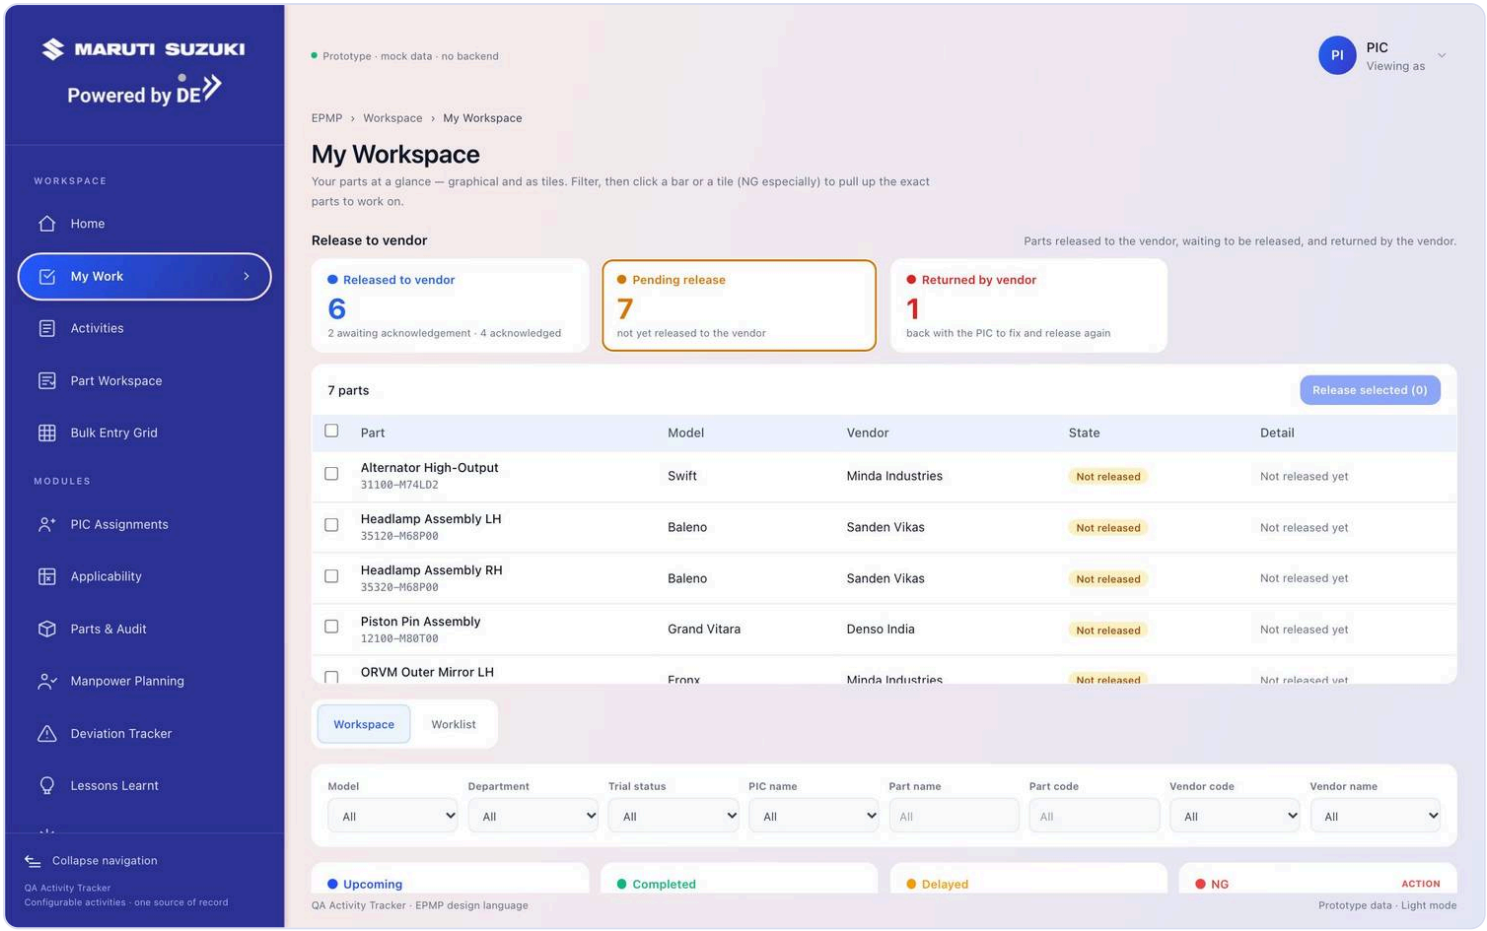

Purpose

The PIC's view of the same handshake. The tiles show Released to vendor, Pending release and Returned by vendor.


> **Note.** The list shows the reason for a return and who released a part and when.

How to use

1. Click a tile to list those parts.
2. Tick parts that are pending or returned and use "Release selected" to release them together.

My Work: released to vendor

Used by: PIC, SIC, DPM

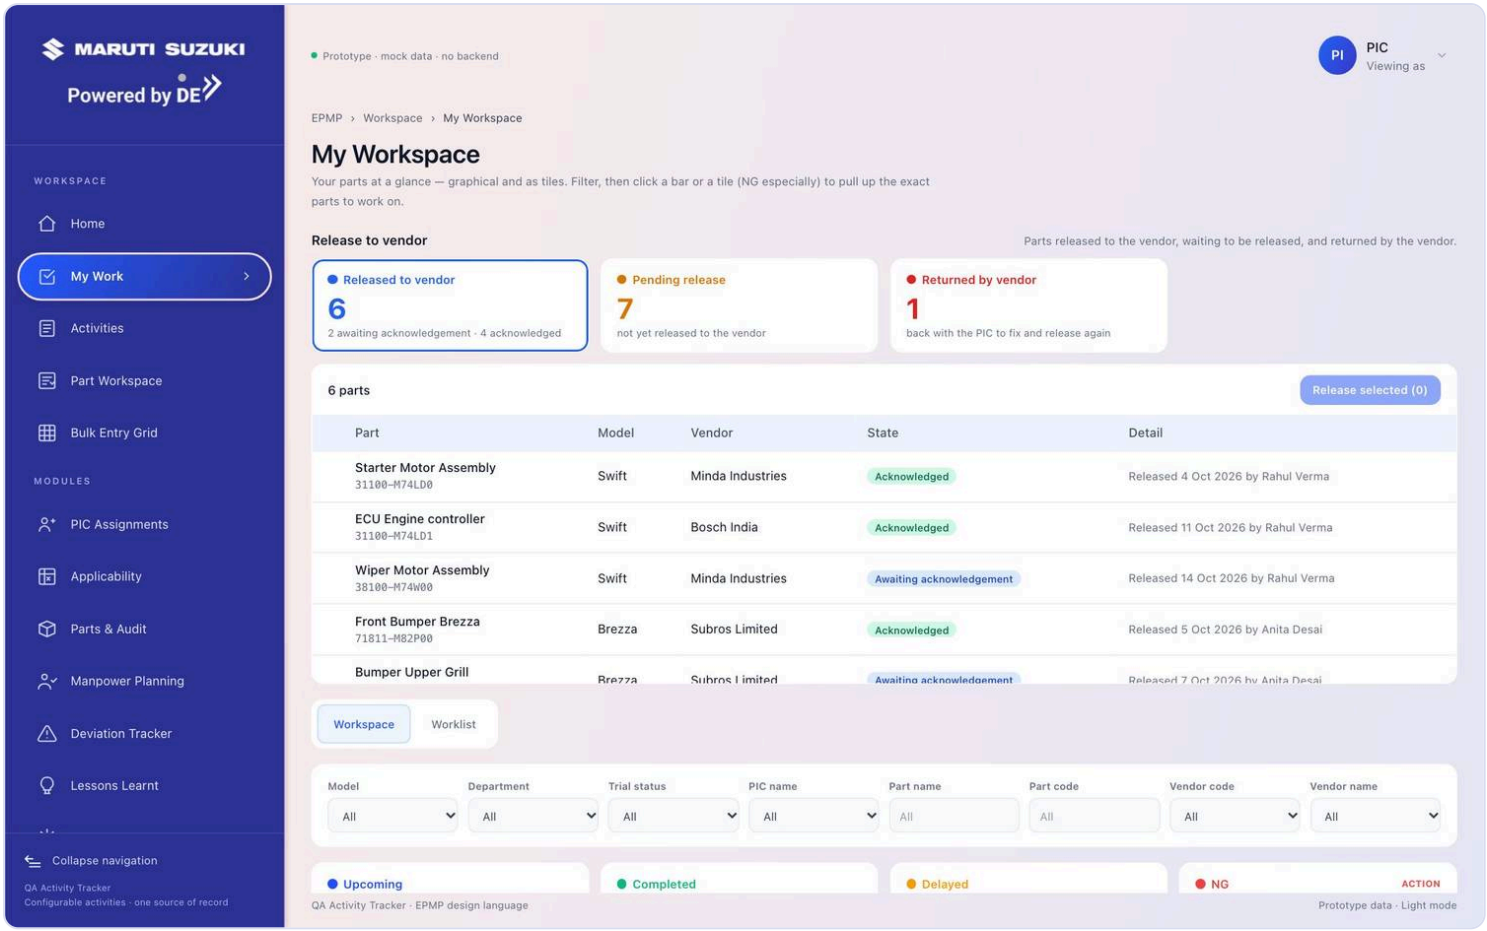

Purpose

Released parts split into those awaiting acknowledgement and those acknowledged.

> **Note.** To withdraw a part, use Recall in Parts & Audit or the part form.


How to use

1. Click “Released to vendor”.
2. Read the state and detail of each part.

C4E

Part form: returned by vendor

Used by: PIC

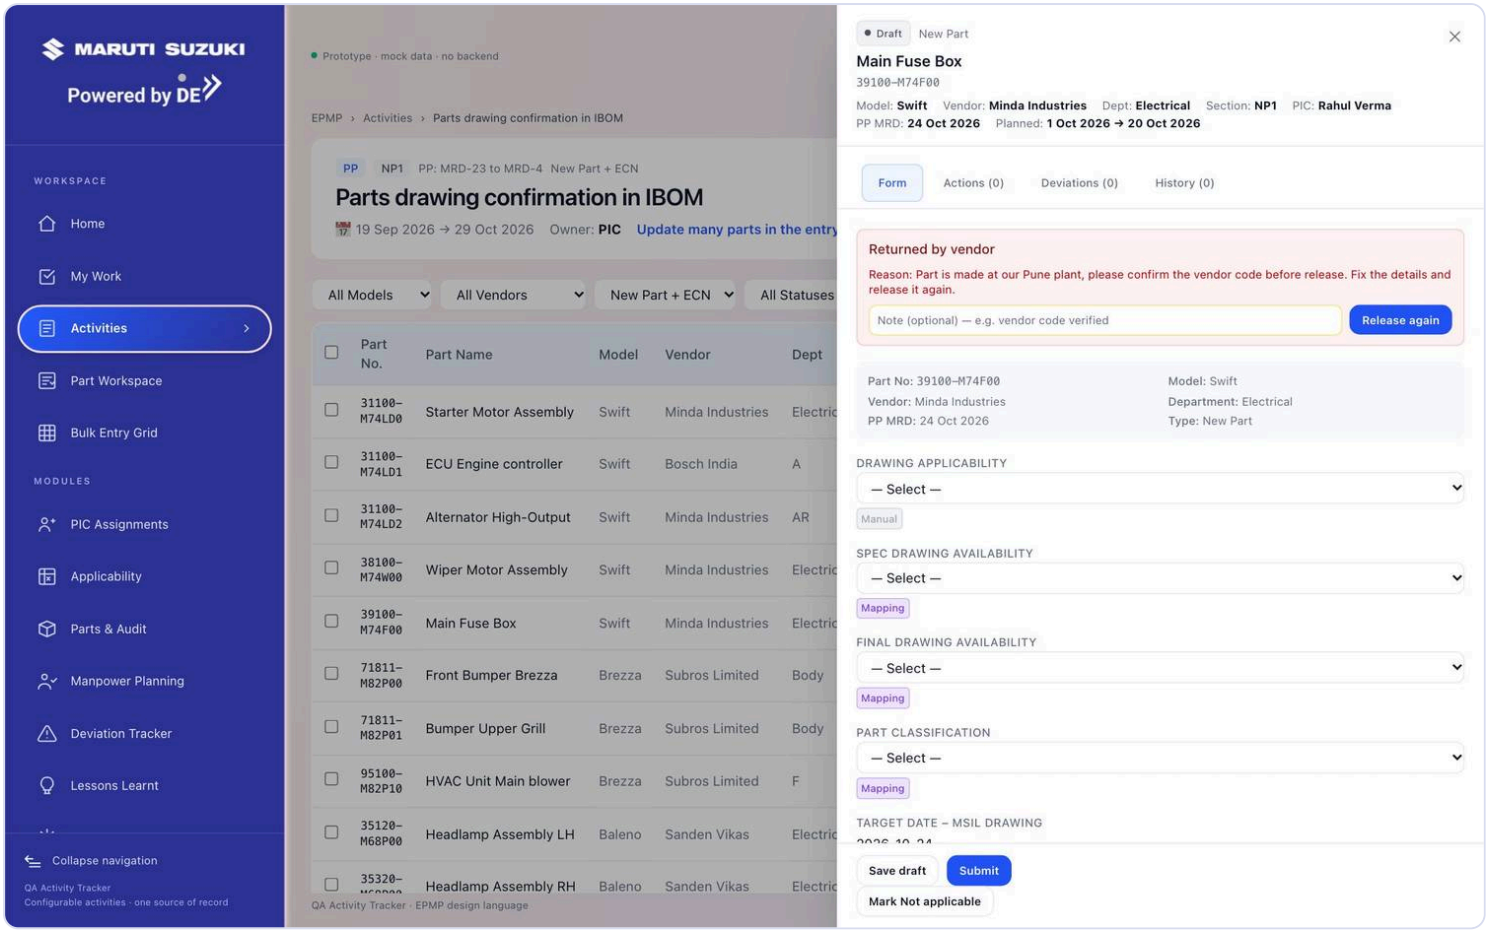

Purpose

The part form banner tells the PIC that the vendor returned the part, and why.

How to use

1. Read the vendor’s reason in the banner.
2. Correct the part details.
3. Click “Release again”, with an optional note.

CHAPTER 5 RUN

Data entry

Enter once, in the way that suits the job.

What it does

Vendors and PICs enter data where it fits their work: a worklist, an entry grid for many parts, one screen for a whole part, or one grid for everything. Fetched and calculated fields fill themselves. An AI import path shows how files and mails will turn into proposed values that a person reviews.

What you can do


- My Work: Workspace (Upcoming, Completed, Delayed, NG tiles, chart, parts table) and Worklist (what to enter, what to validate).
- Entry grids: one row per part, fill a column, copy down, Save drafts, Submit all ready, Download CSV.
- Part Workspace: all activities of one part on one screen, progress bar, “Also fill other parts of the same vendor”.
- Bulk Entry Grid: parts as rows, every activity field as columns.
- Activity page and part form: field source badges, read-only calculated fields, Refresh for fetched fields, Save draft, Submit, Mark Not applicable.
- AI import review (illustration): proposals with confidence, dropdown picks shown as exact or closest match, failed updates listed with reasons.

Rules you can rely on


- Vendors see only their own parts and the fields assigned to the vendor.
- AI never approves, edits or sends back; nothing is submitted without a person’s review.
- For dropdown fields AI may pick the nearest allowed value, shows how it did, and closest matches always need a decision.
- Updates AI could not make are listed, not applied, and never dropped silently.

Used by


Vendor, PIC




My Work: Workspace · p. 31




My Work: Worklist · p. 32




Entry grid (Vendor) · p. 33




Entry grid (PIC) · p. 34




Part Workspace · p. 35




Bulk Entry Grid · p. 36




Activity page · p. 37



Part form · p. 38




AI import panel · p. 39



AI review: dropdown matches and failed updates · p. 40

C5A My Work: Workspace

Used by: Vendor, PIC, SIC, DPM

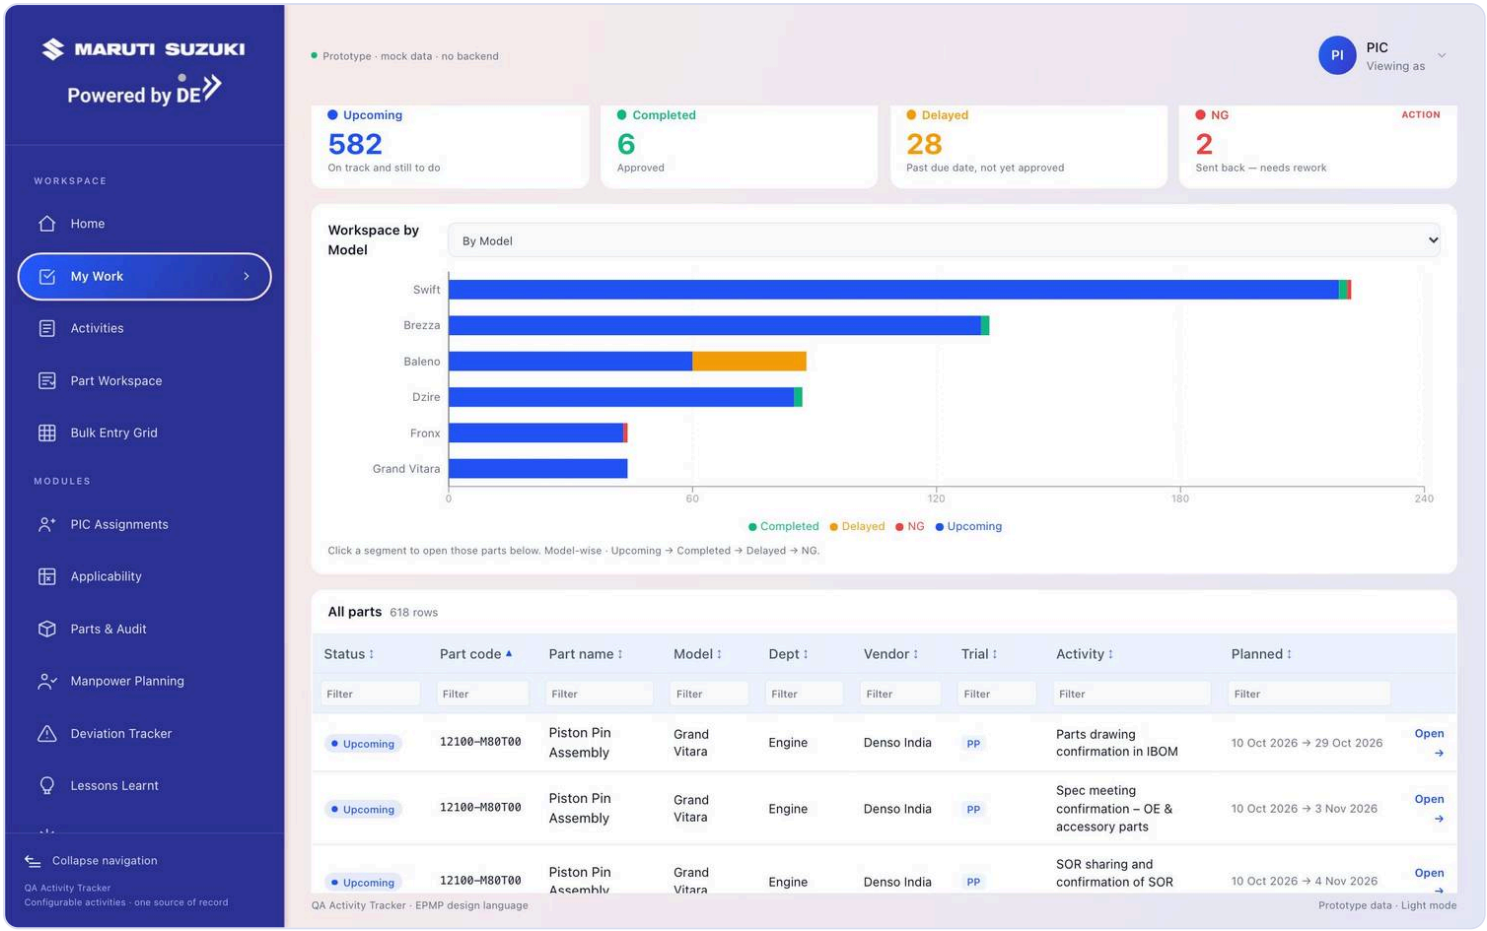

Purpose


A graphical view of your parts: Upcoming, Completed, Delayed and NG tiles, a chart and the parts table.

How to use

1. Filter by model, department, trial status, PIC, part, vendor code or name.
2. Click a tile or chart segment to pull up those parts.
3. “Open →” on a row opens that part’s form.

C5B My Work: Worklist

Used by: Vendor, PIC

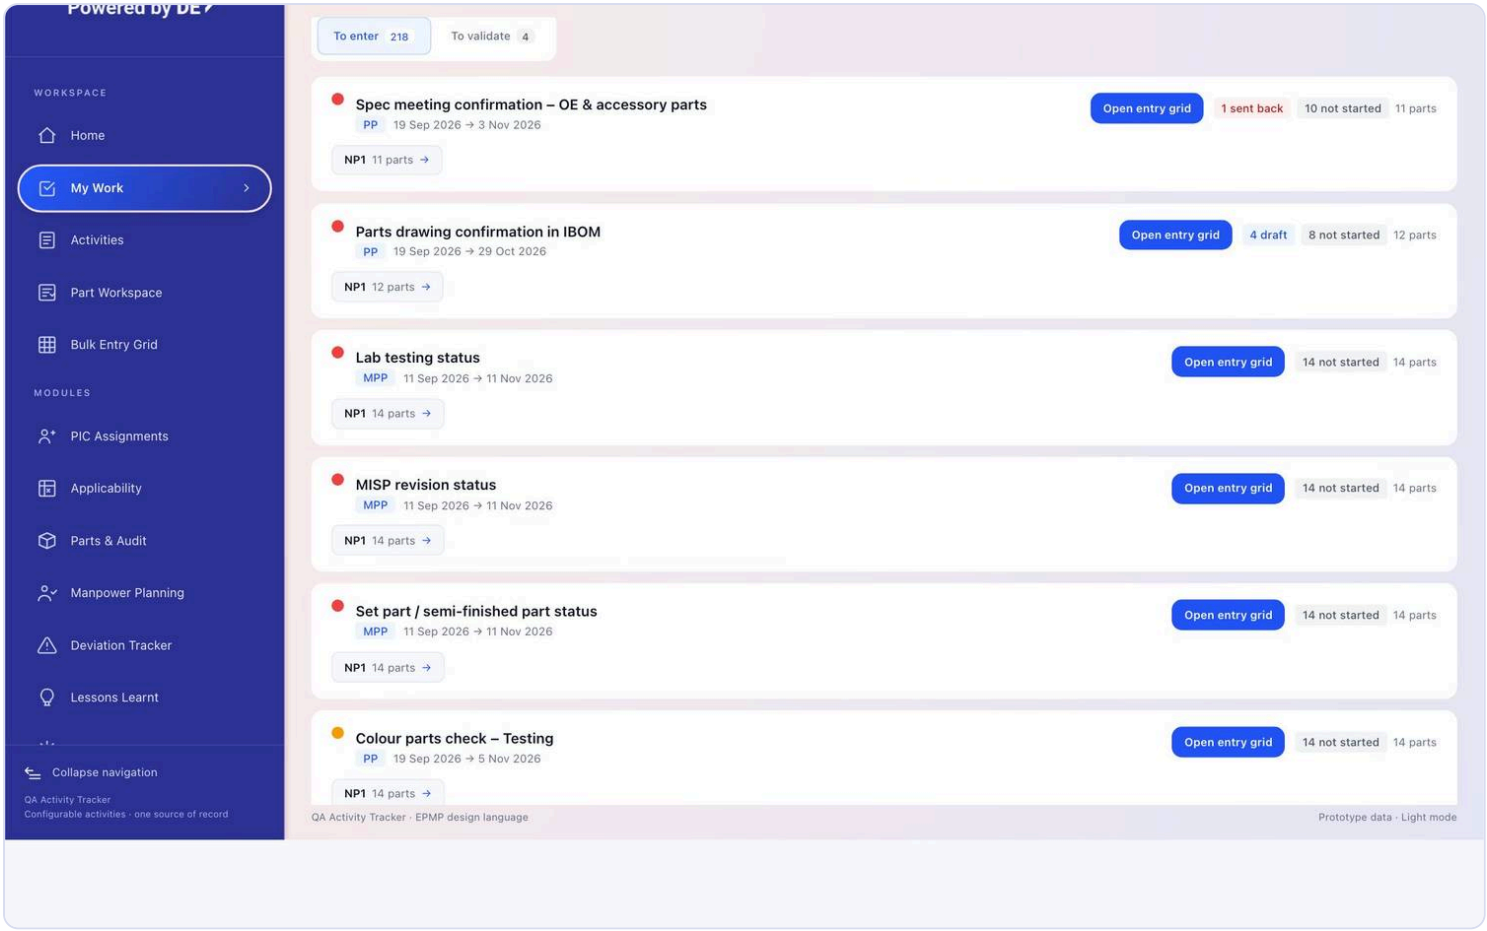

Purpose

What to enter and what to validate, grouped by activity and ordered by urgency.


> **Note.** Counts show how many parts are not started, in draft or sent back.

How to use

1. Use the “To enter” and “To validate” tabs.
2. “Open entry grid” or “Open validation grid” works on all parts of that activity together.

Entry grid (Vendor)

Used by: Vendor

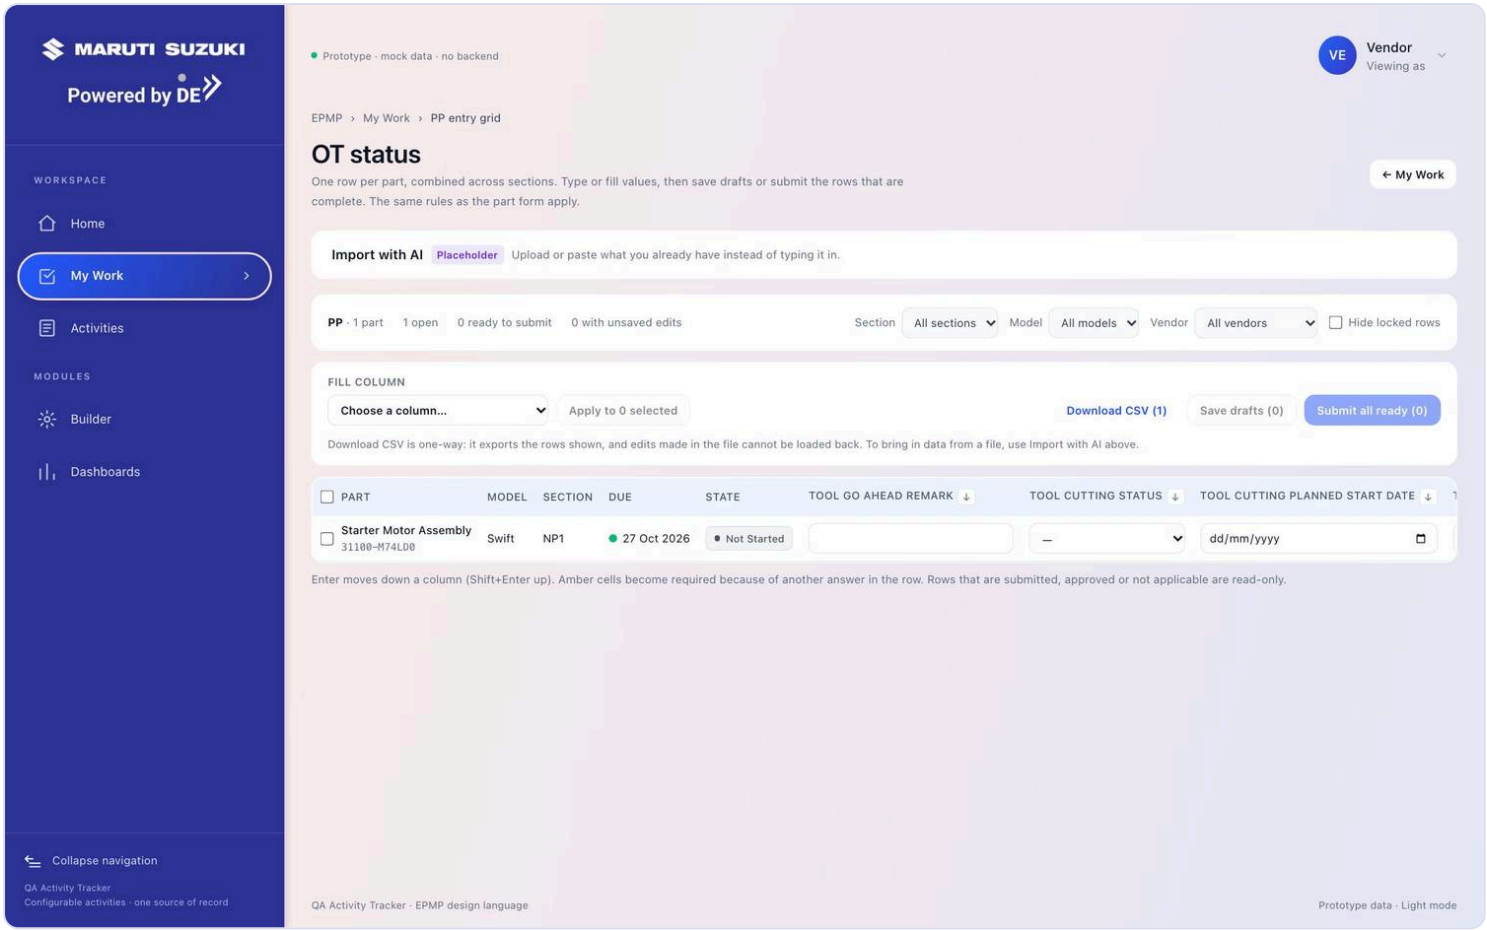

Purpose

One row per part, one column per vendor field. The vendor updates many parts in one table.


> **Note.** Download CSV exports the rows shown.

How to use

1. Type or pick values in the cells; amber cells become required because of another answer.
2. “Fill column” applies one value to all ticked rows.
3. “Save drafts” keeps partial work; “Submit all ready” sends only complete rows to the PIC.

Entry grid (PIC)

Used by: PIC

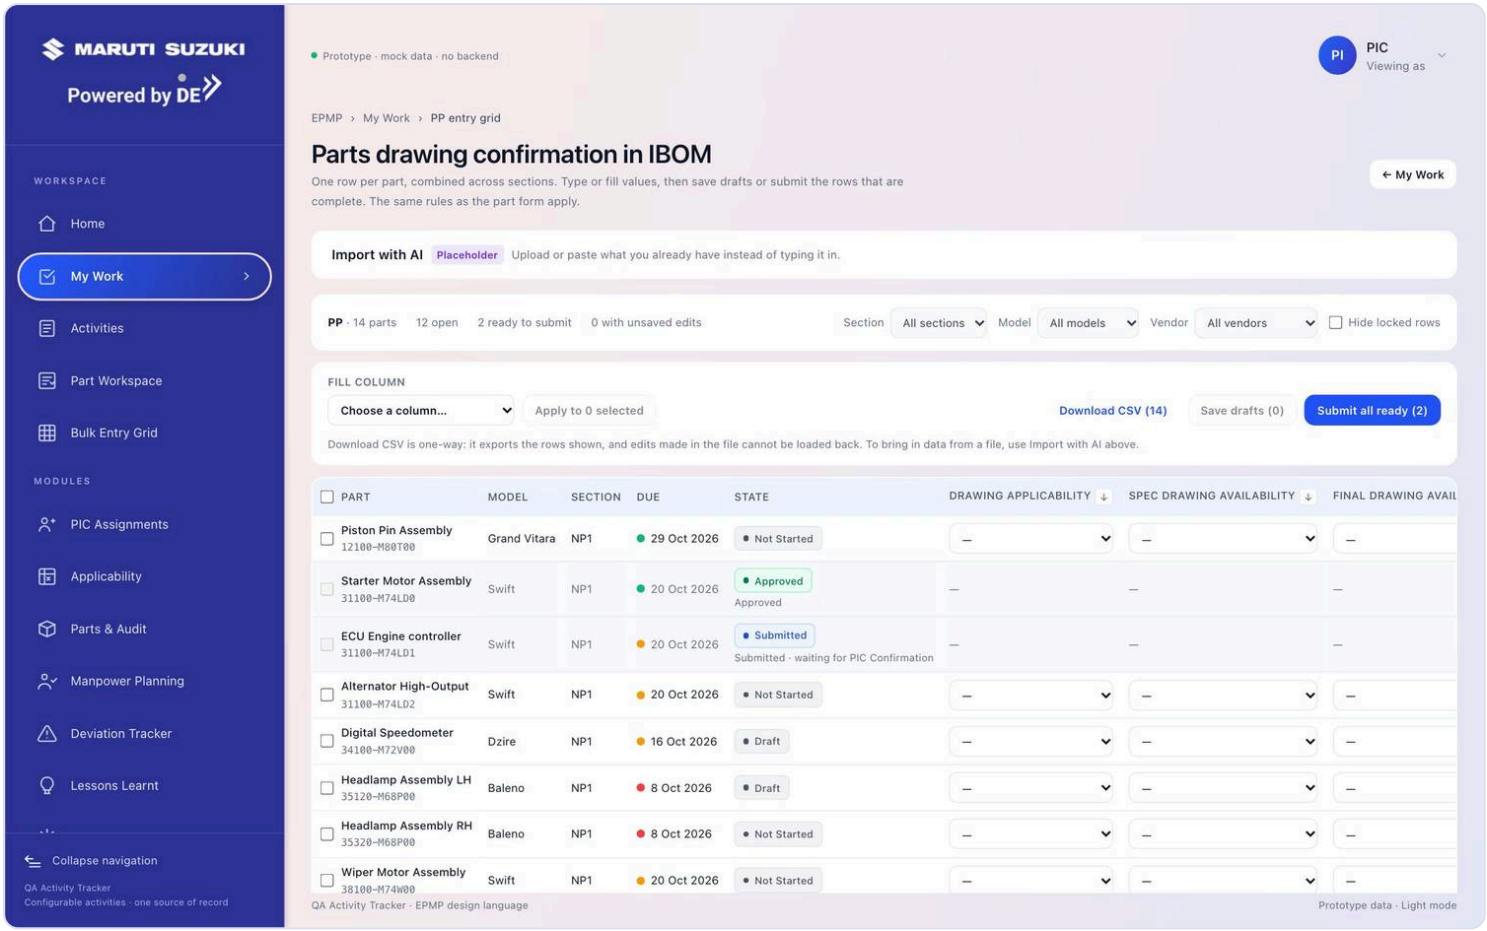

Purpose

The same grid for activities the PIC enters first, such as drawing confirmation.


> **Note.** Calculated and fetched columns are read-only.

How to use

1. Fill the PIC columns, or use “Fill column”.
2. Locked rows (Approved, Submitted) are grey and read-only.
3. Submit the rows that are complete.

Part Workspace

Used by: PIC, SIC, DPM

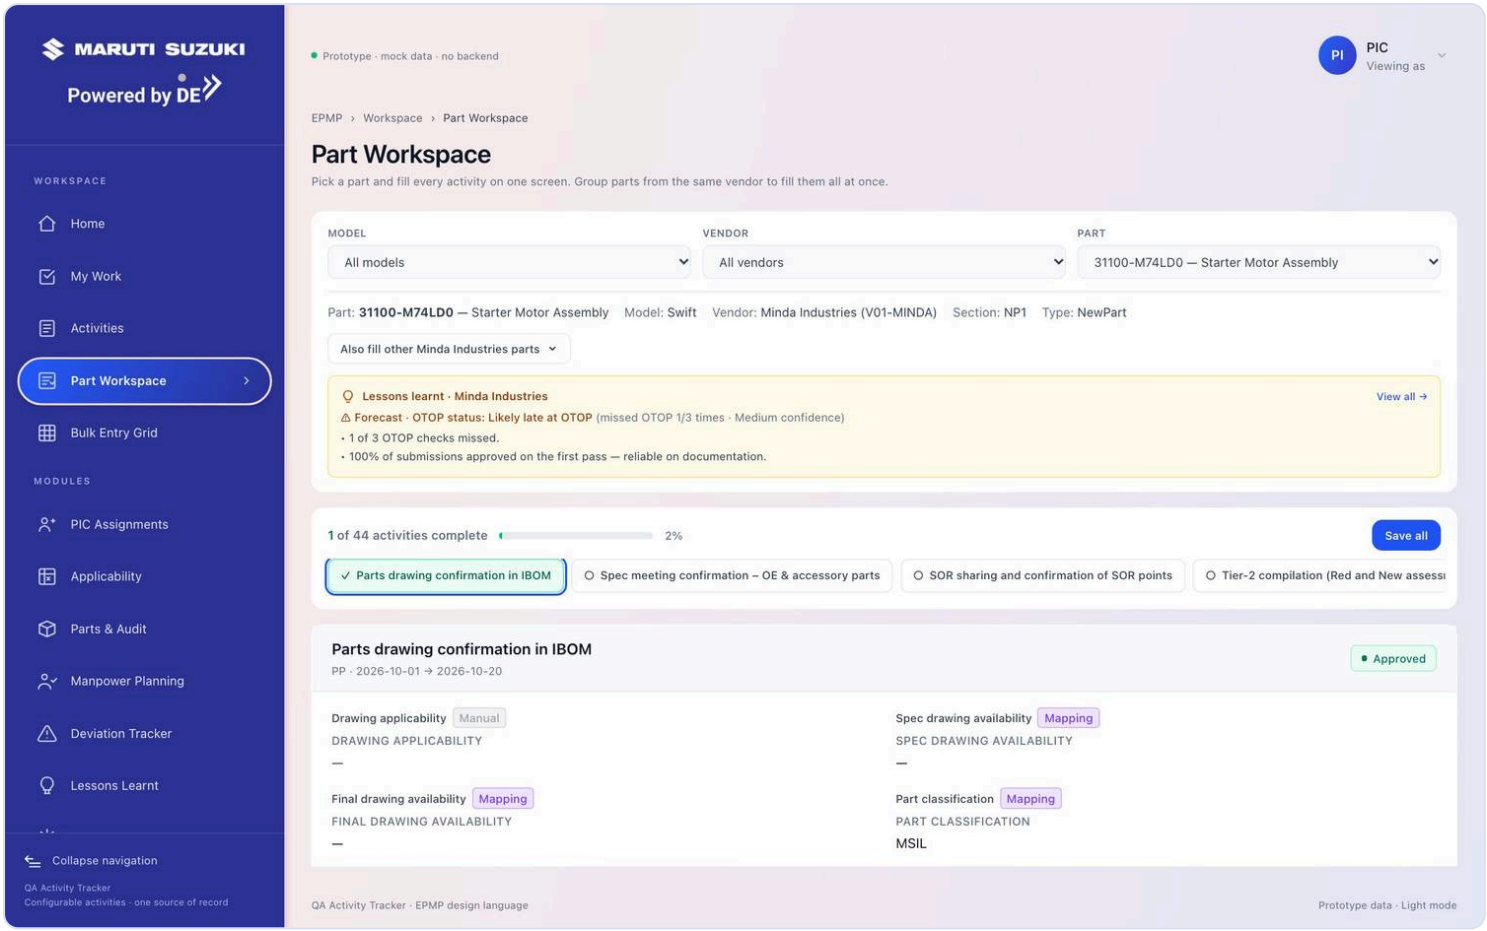

Purpose

Fill every activity of one part on one screen. The top pane stays fixed and only the sections scroll.


> **Note.** A lessons-learnt callout warns when the vendor has a delay pattern.

How to use

1. Pick model, vendor and part.
2. “Also fill other parts of this vendor” copies values to that vendor’s other parts.
3. Read “N of M activities complete”; tabs turn green when complete.
4. “Save all” stores every section.

Bulk Entry Grid

Used by: PIC, SIC, DPM

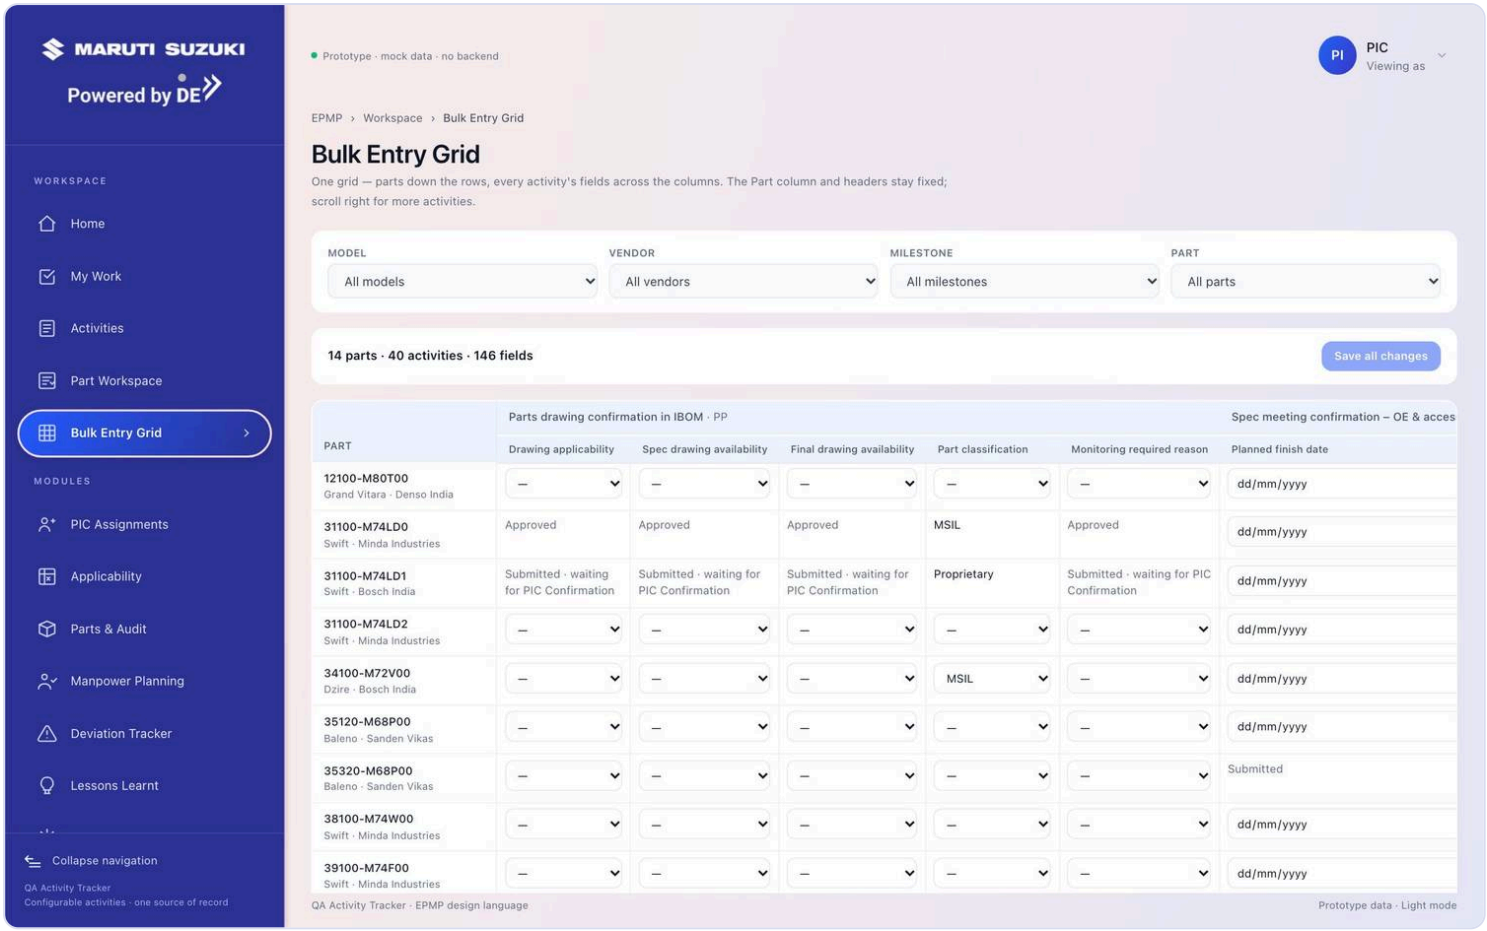

Purpose

Parts down the rows, every activity's fields across the columns. Part column and headers stay fixed while you scroll.


> **Note.** Best for mass updates. Use the Part Workspace for one part at a time.

How to use

1. Filter by model, vendor, milestone or part.
2. Edit cells directly; the header line shows the size of the grid.
3. "Save all changes" stores every edit.

Activity page

Used by: All roles

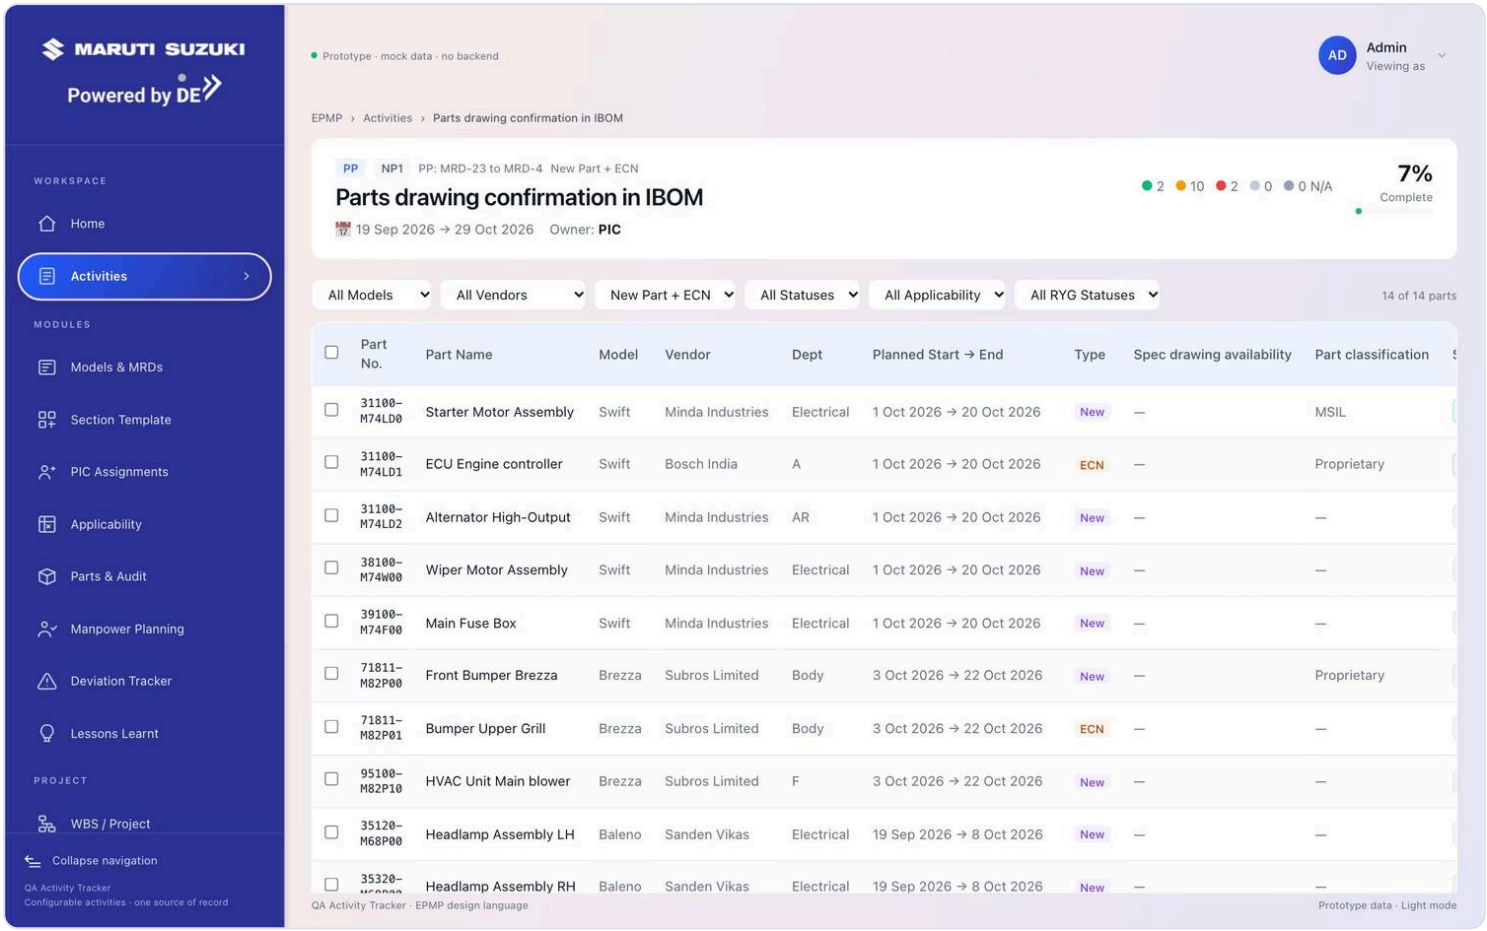

Purpose


Part-wise status of one activity at one milestone, with RYG, completion and the list columns the activity defines.

How to use

1. Filter by model, vendor, type, status, applicability or RYG.
2. Click a part to open its form.
3. Tick parts to mark them Not applicable (PIC).

C5H Part form

Used by: PIC, Vendor

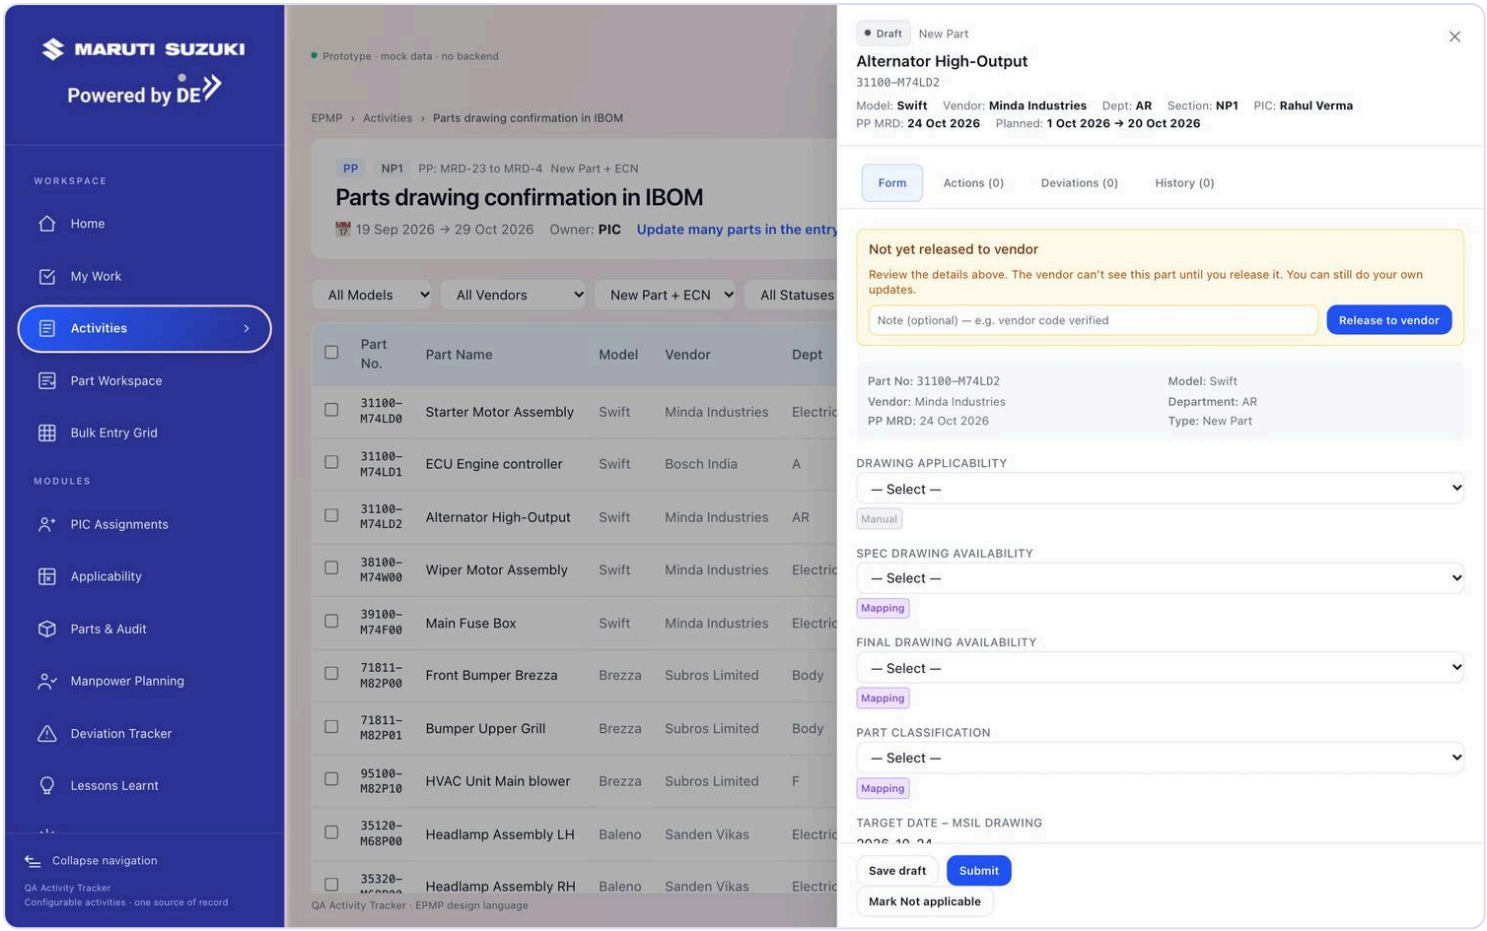

Purpose

The form for one part and one activity, opened beside the list.


> **Note.** The release banner shows whether the part is released, acknowledged or returned.

How to use

1. Fields carry a source badge: Manual, Mapping, Calculated, ENOVIA or SAP.
2. Calculated fields are read-only; fetched fields have a Refresh button.
3. “Save draft”, “Submit” or “Mark Not applicable”.

C5I AI import panel

Used by: Vendor, PIC

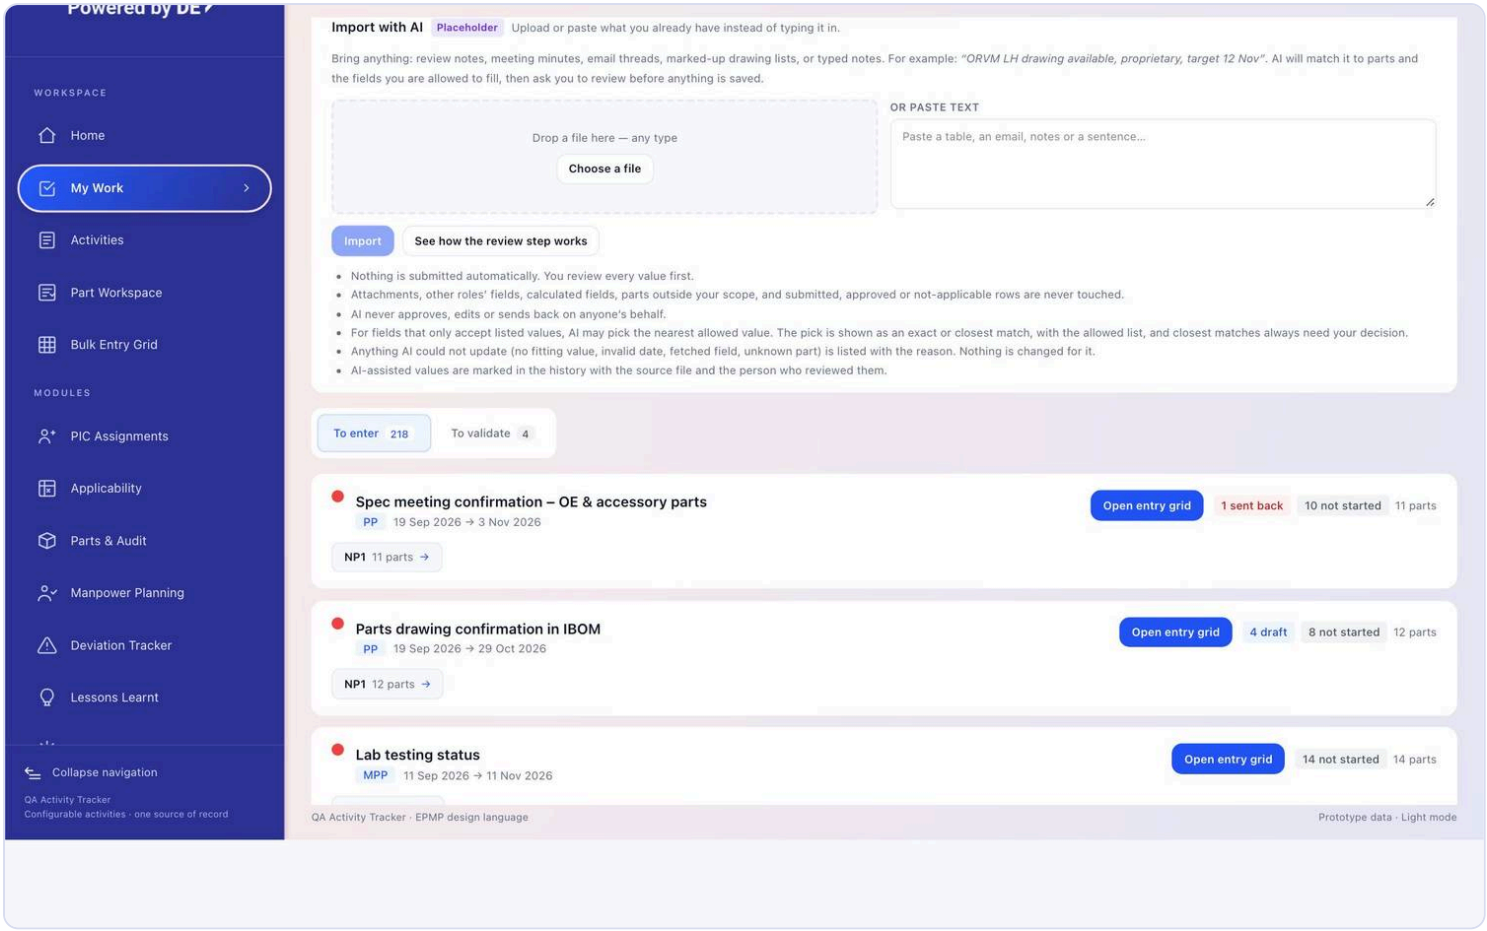

Purpose

The entry point for importing from a file, mail or typed text. It is a placeholder in the prototype.


> **Note.** Nothing is read or changed in the prototype.


How to use

1. Choose a file or paste text.
2. Read the rules listed in the panel.
3. "See how the review step works" opens the review screen.

C5J AI review: dropdown matches and failed updates

Used by: Vendor, PIC

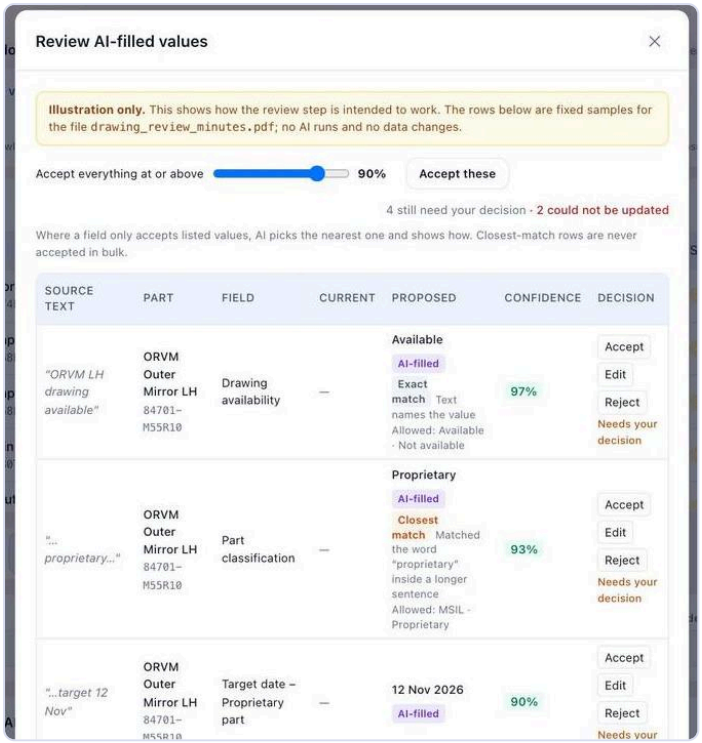

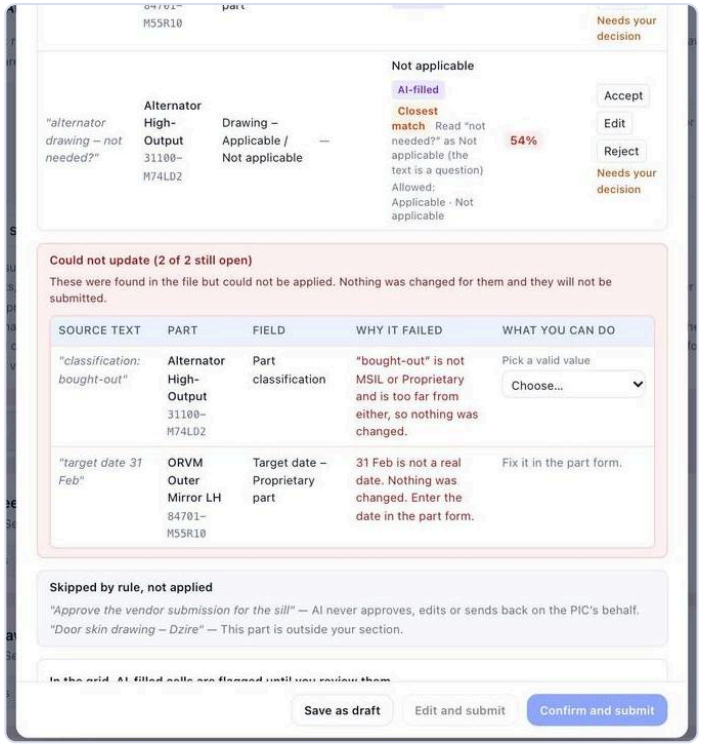

Purpose

Shows how AI-filled values are reviewed before anything is saved. This is an illustration with fixed samples.

> **Note.** Failed updates are never applied or submitted.

How to use

1. Each proposal shows confidence and, for dropdown fields, an Exact or Closest match tag, how the text was read and the allowed values.
2. Closest matches are never accepted in bulk; Accept, Edit (a list of allowed values) or Reject each.
3. “Could not update” lists what AI could not apply, with the reason; pick a valid value where one exists.
4. Tick “I have reviewed” before Confirm and submit.

CHAPTER 6 RUN

Validation & approvals

Every entry is checked, and deviations follow a chain.

What it does

Vendor entries wait for the PIC. The PIC approves, edits or sends back, one row or many. When a result needs a deviation, it moves through a PIC → SIC → DPM approval chain. Actions and history keep the follow-up in the system.

What you can do


- Validation grid: tick rows, Approve selected, Send back selected with a written reason, Save PIC edits.
- Entry states: Draft, Submitted, Approved, Sent back, Not applicable.
- Deviation Tracker: every deviation, its flow, stage, status, E-Doc number and target date.
- Part form tabs: Actions (owner, target date, status), Deviations, History (who, when, what).

Rules you can rely on


- Approve selected skips rows where a required PIC field is empty, and lists them.
- A send-back needs a reason, which is stored in the row's history.
- SIC and DPM validate only; they do not enter vendor or PIC fields.
- Prebuilt activities use the PIC → SIC → DPM deviation chain.

Used by


PIC, SIC, DPM




Validation grid · p. 42



Deviation Tracker · p. 43




Part form: Actions · p. 44



Part form: History · p. 45

C6A Validation grid

Used by: PIC

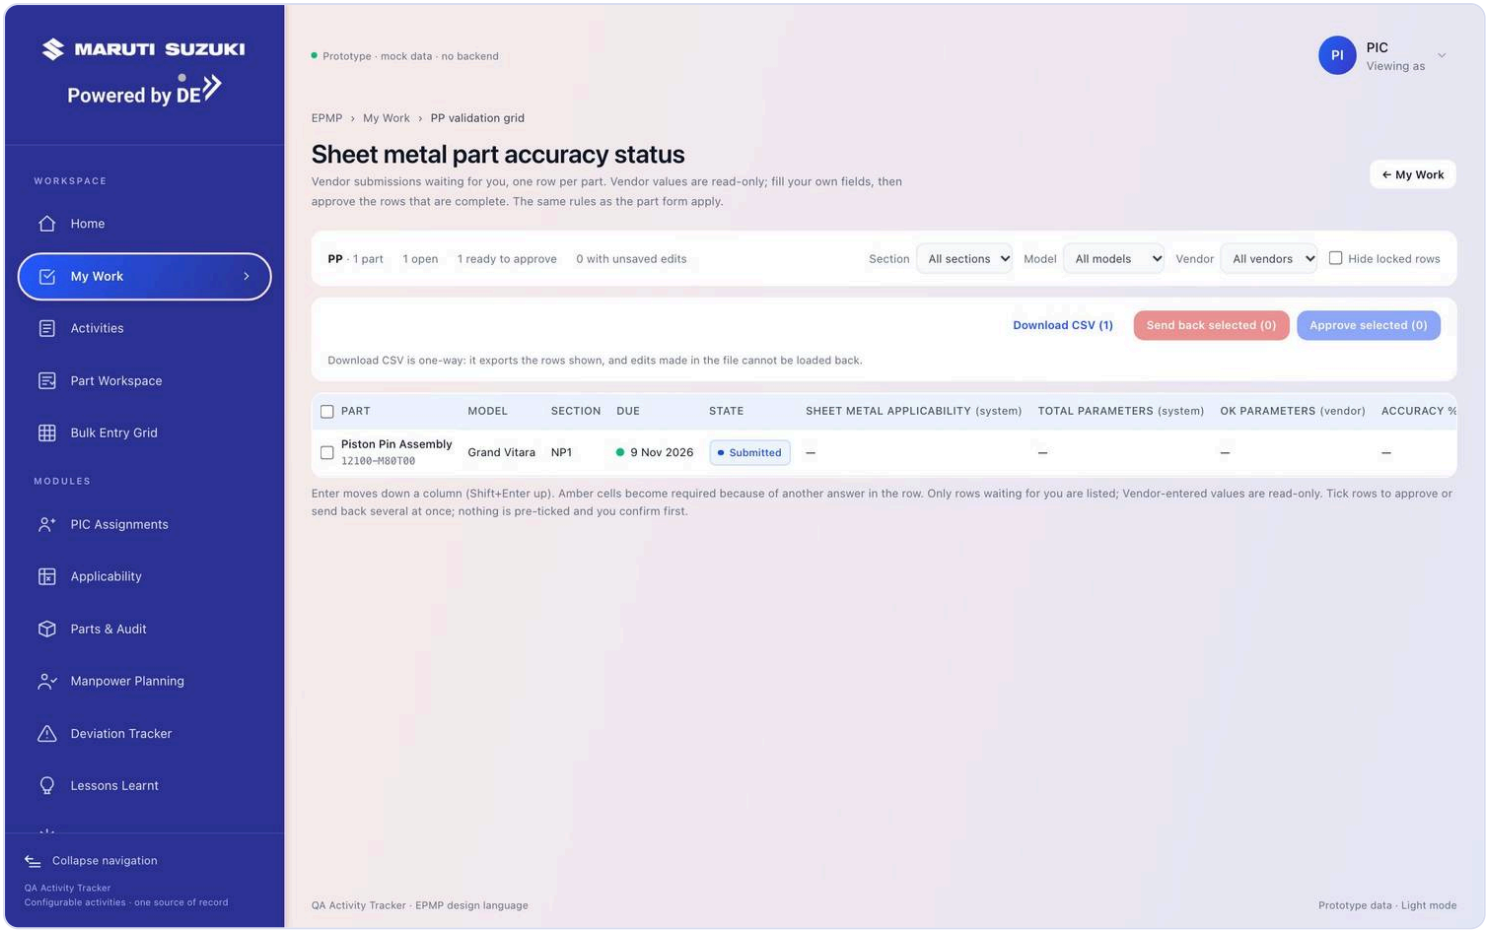

Purpose

Vendor submissions waiting for the PIC, one row per part. Vendor values are read-only.

> **Note.** SIC and DPM can validate only.


How to use

1. Tick the rows to act on; nothing is pre-ticked.
2. “Approve selected” skips rows where a required PIC field is empty and lists them.
3. “Send back selected” asks for a reason that goes into each row’s history.
4. “Save PIC edits” stores PIC values without approving.

C6B

Deviation Tracker

Used by: PIC, SIC, DPM, Admin

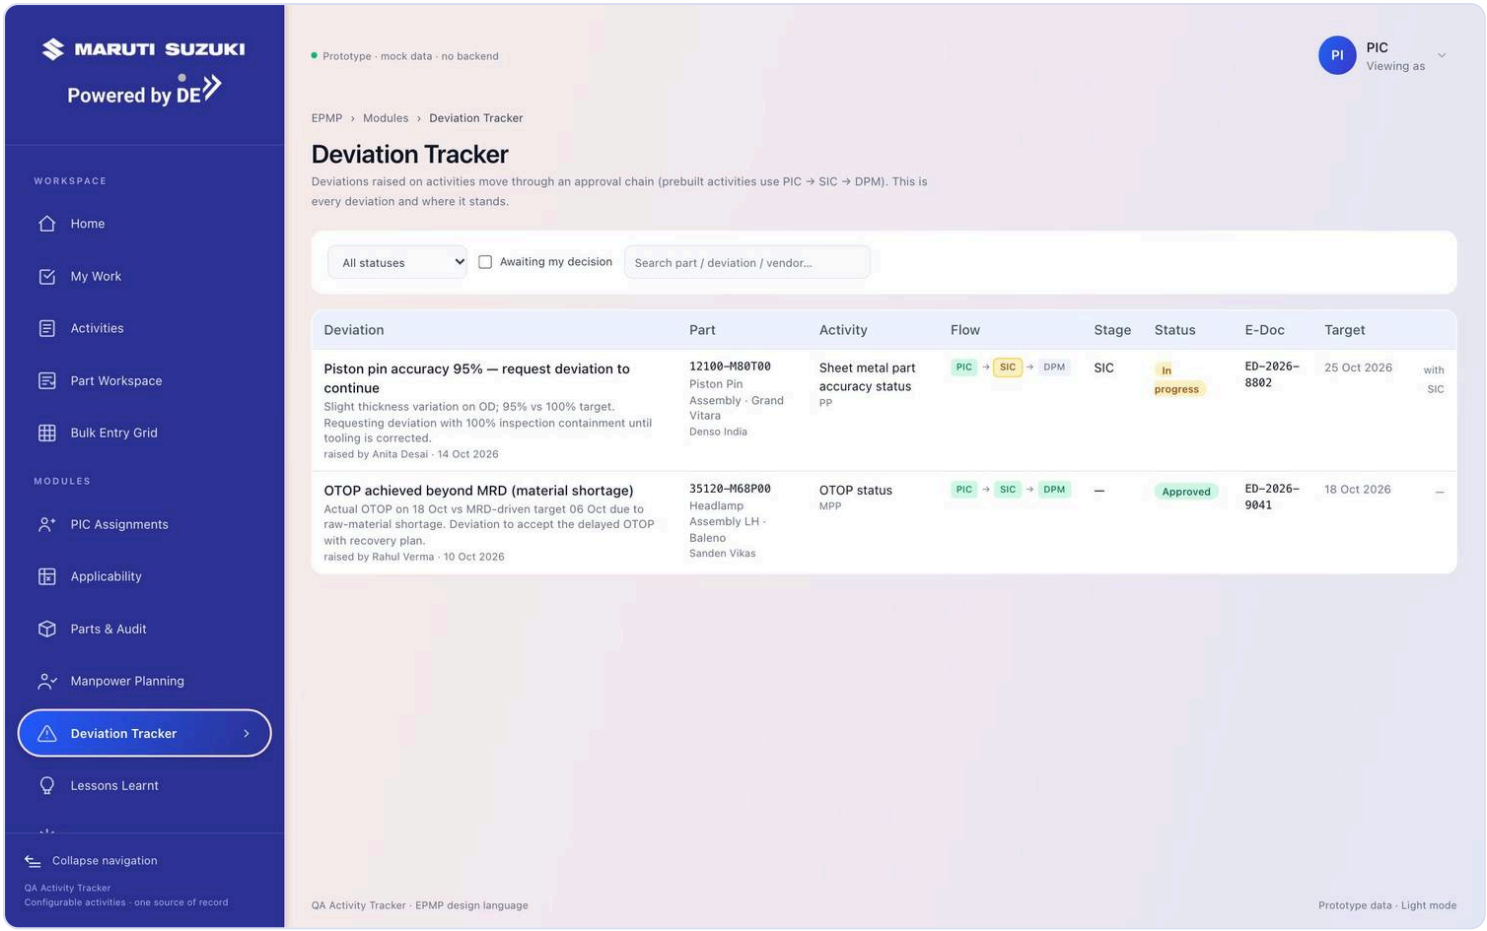

Purpose

Every deviation, with the approval flow and where it stands.


How to use

1. Filter by status, tick “Awaiting my decision”, or search part, deviation or vendor.
2. Each row shows part, activity, flow (PIC → SIC → DPM), stage, status, E-Doc number and target date.
3. Approve or reject at your stage.

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐

Part form: Actions

Used by: PIC, SIC, DPM

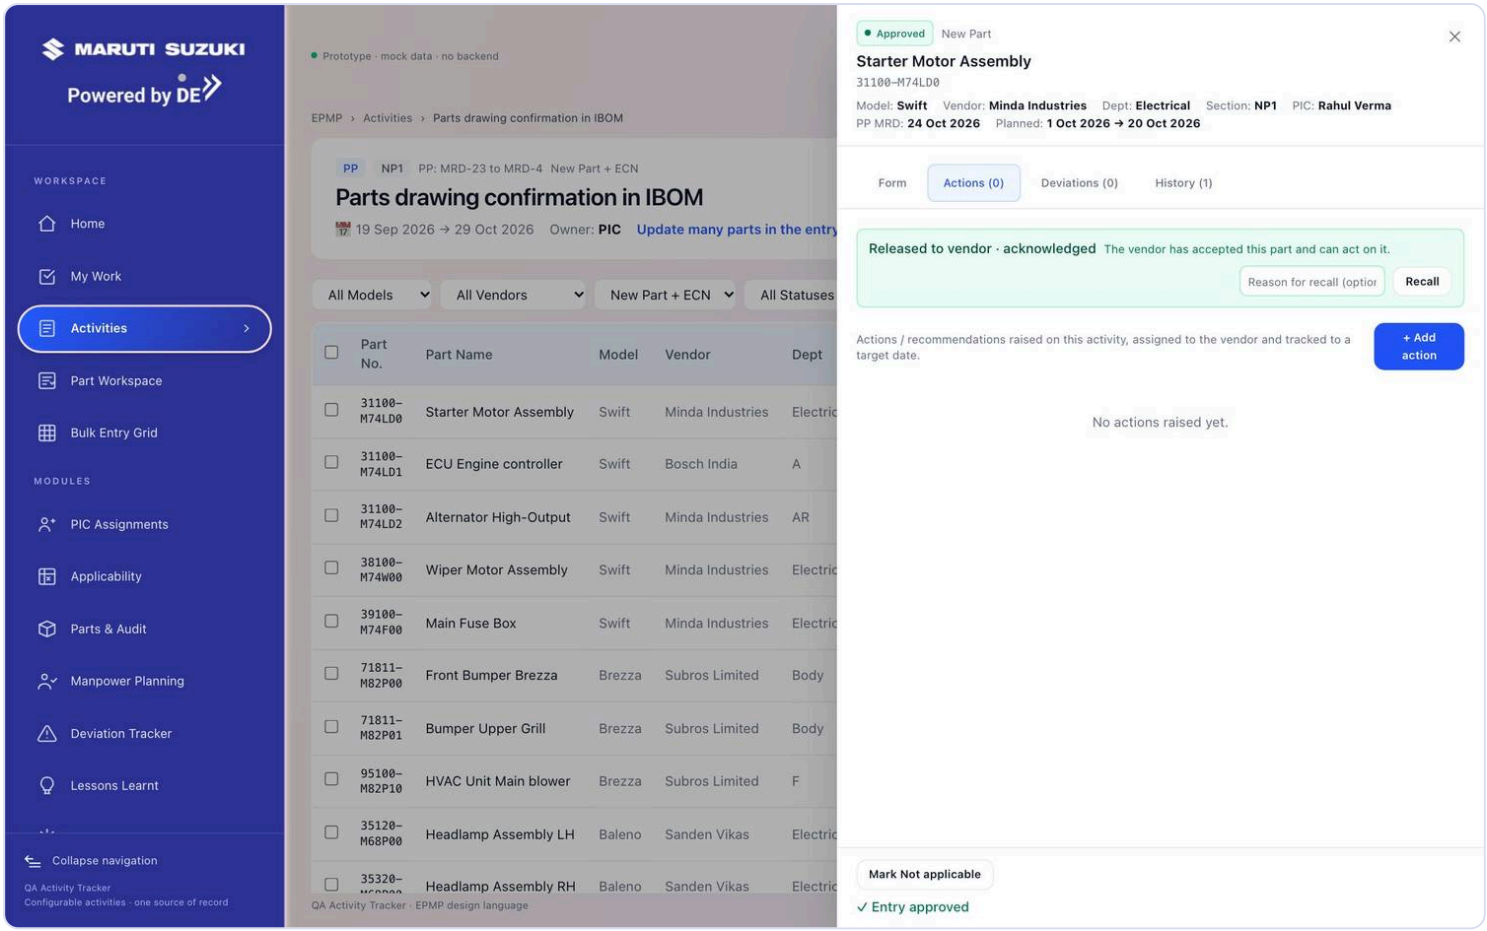

Purpose

Follow-up actions on a part, with owner, target date and status.

> **Note.** Replaces open points kept in Excel.


How to use

1. Open the Actions tab.
2. Add an action, set the target date, update the status.

C6D

Part form: History

Used by: All roles

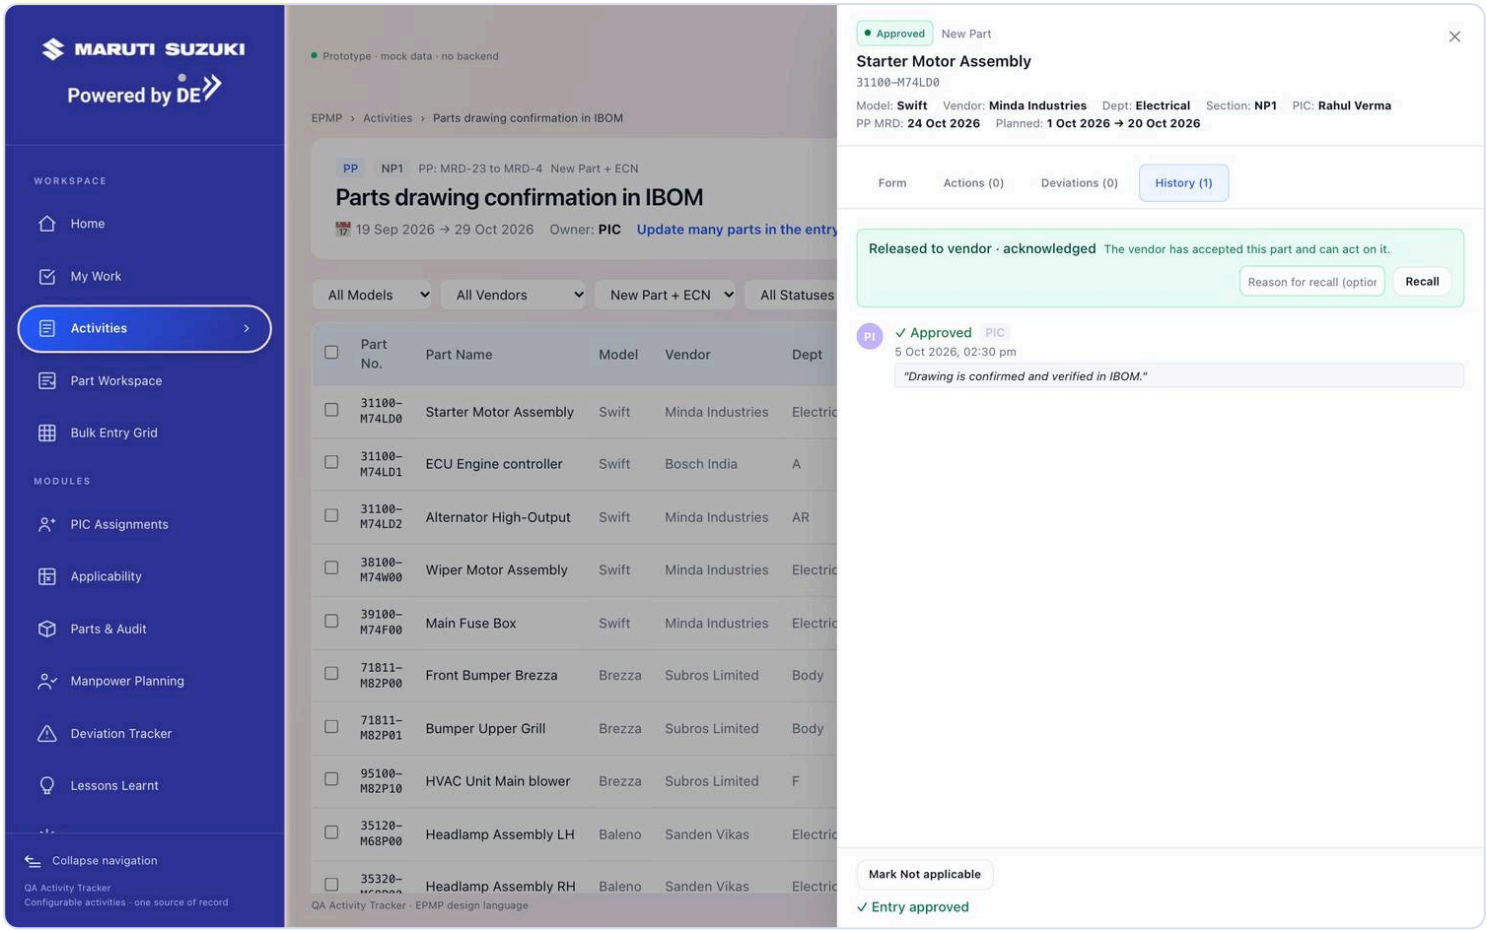

Purpose

The audit trail of the part: who did what, when and why.

How to use

1. Open the History tab.
2. Read entries such as Released to vendor, Acknowledged, Returned, Submitted, Approved.

CHAPTER 7 MONITOR

Status & risk insight

Red, yellow, green, and what is likely to slip next.

What it does

RYG is calculated from the planned end date and the approval state, and shows everywhere. Lessons Learnt turns the tracker's own history into vendor scorecards, heat maps, insights and a forecast of parts likely to slip.

What you can do


- RYG: Red when past the planned end, Yellow when due within 7 days, Green otherwise or once approved, Grey while awaiting an MRD.
- Lessons Learnt: AI insights, Forecast of at-risk parts with reason and confidence, Vendor scorecards.
- Vendor × activity heat map, or activities as rows for a single vendor.
- One filter bar (vendor and technical category) applies to every section.
- Part Workspace risk callout when a vendor has a delay pattern.

Rules you can rely on


- Insights and the forecast are rule-based, not a trained model.
- RYG recalculates whenever an MRD, an offset or an approval changes.
- Not-applicable parts do not count towards RYG.

Used by

All roles (DPM and above for Lessons Learnt)




Lessons Learnt · p. 47



Vendor scorecards · p. 48

Lessons Learnt

Used by: DPM, SIC, PIC, Admin

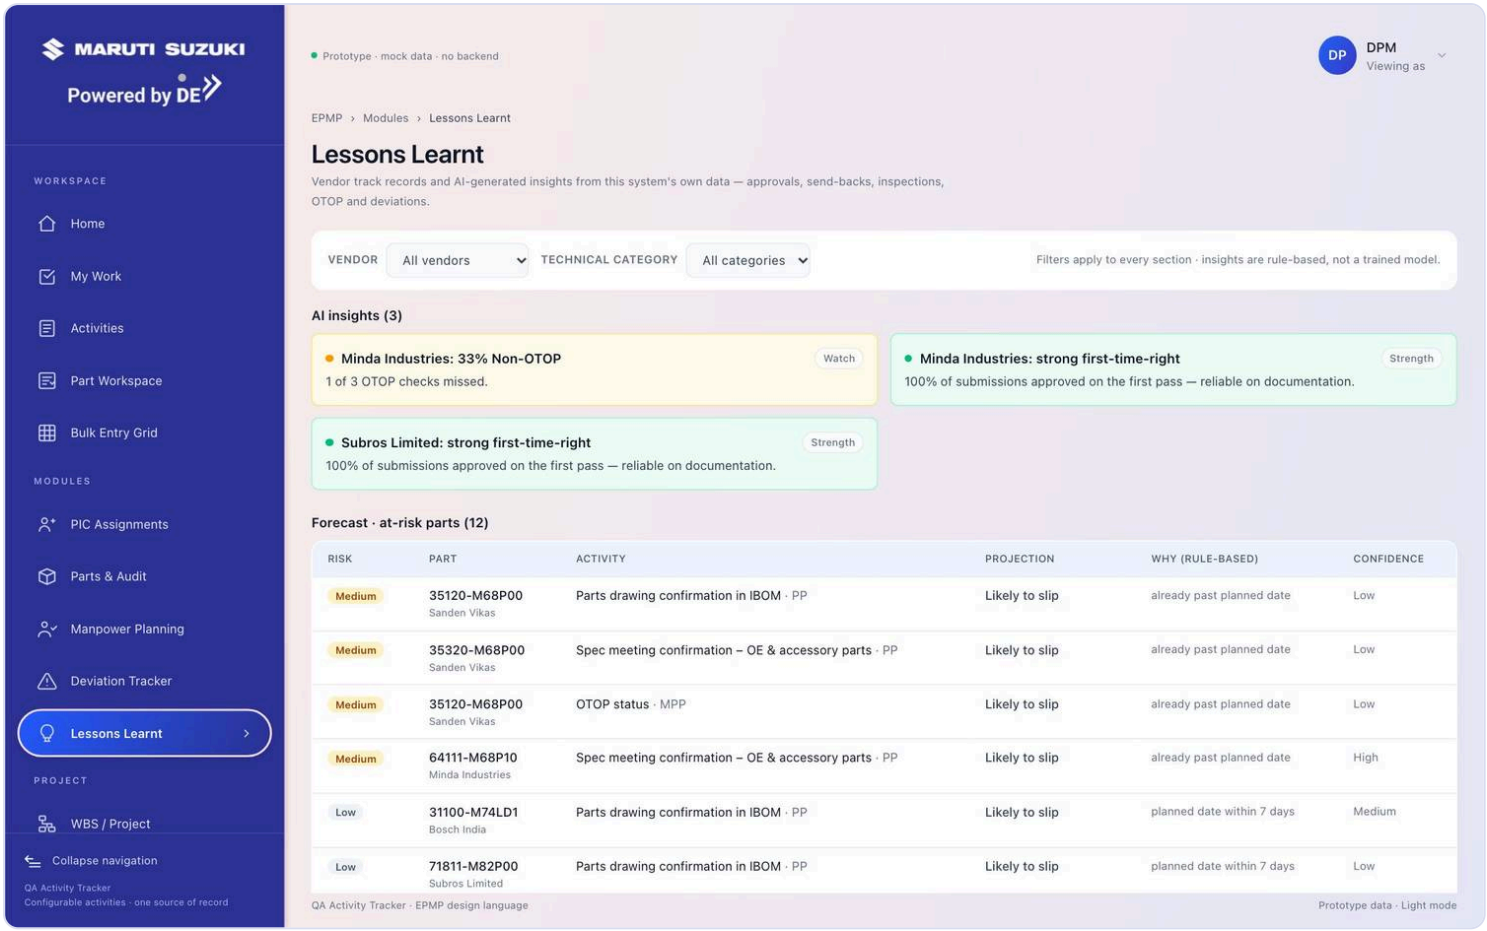

Purpose

Insights drawn from the tracker's own data: approvals, send-backs, inspections, OTOP and deviations.


> **Note.** Insights are rule-based, not a trained model.

How to use

1. Use the Vendor and Technical category filters; they apply to every section.
2. Read the AI insight cards.
3. The forecast table lists at-risk parts with risk, projection, reason and confidence.

Vendor scorecards

Used by: DPM, SIC, PIC, Admin

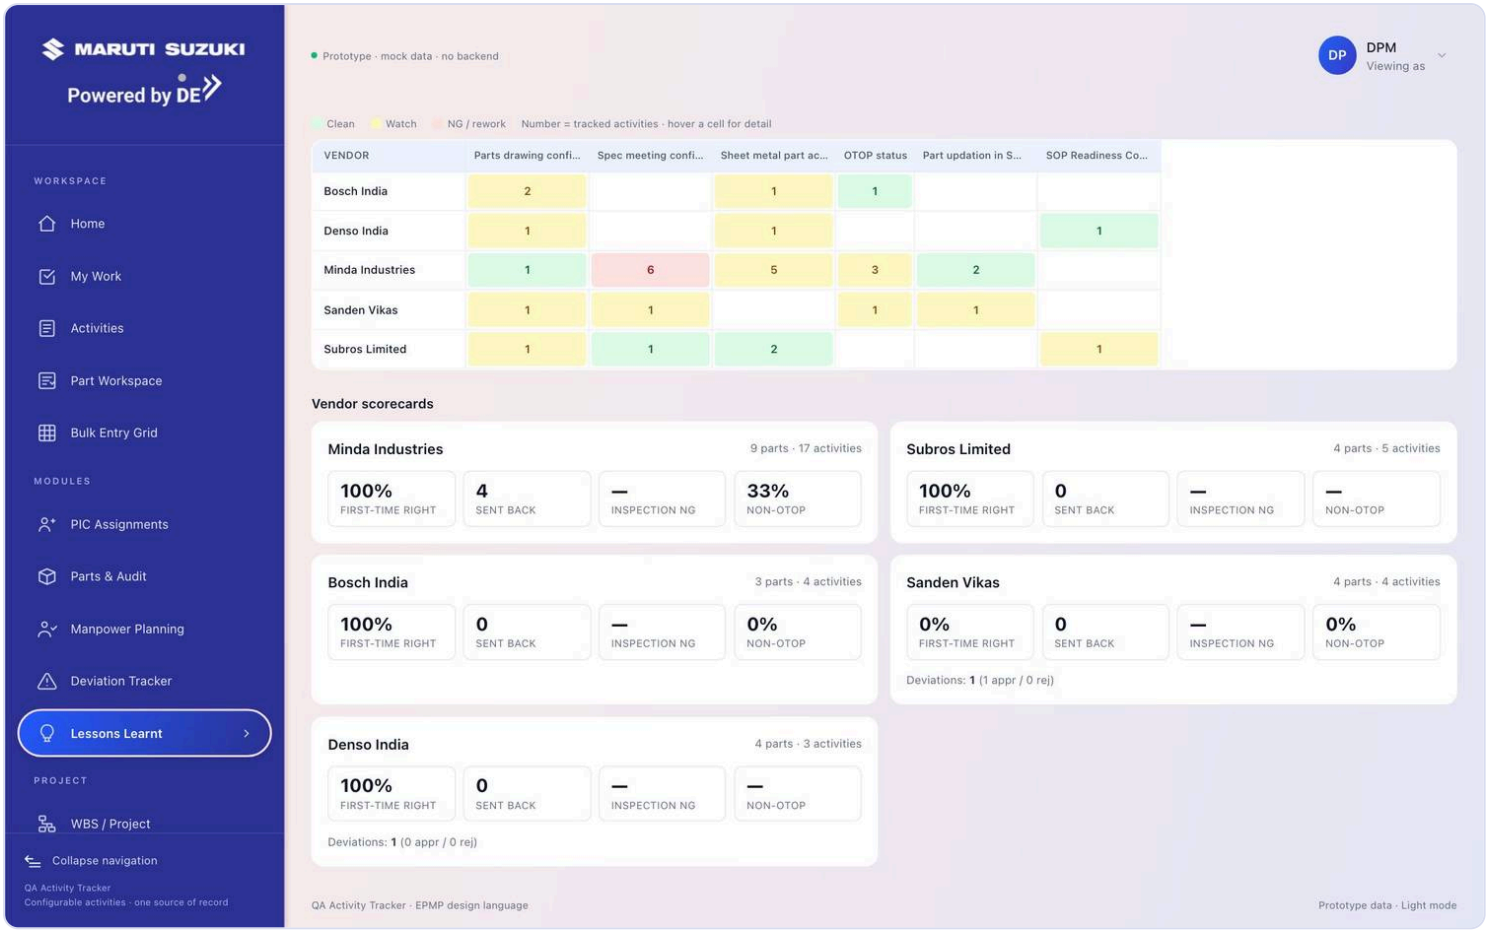

Purpose

A record per vendor built from the same data.

How to use

1. Scroll to Vendor scorecards.
2. Compare vendors on first-time right %, sent back, inspection NG % and non-OTOP %, with the top NG category and top delay reason.

CHAPTER 8 MONITOR

Project view

See the work as a tree and as a chain.

What it does

The WBS shows each model as Milestone → Part → Activity with effort, dates and status. Activity Dependencies define which activity waits for which, per technical category.

What you can do


- WBS / Project: EV weightage, planned effort, planned start and end, dependency and status; Expand all and Collapse all.
- Activity Dependencies: dependent activity, predecessor, type (FS, SS, FF, SF) and lag in days.
- Dependencies are defined per technical category (Engine, Weld, Rubber Assy, Plastic Assy, Other Assy).

Rules you can rely on


- Only DPM and Admin can edit dependencies; others see them read-only.
- Circular and duplicate dependencies are rejected.

Used by


SIC, DPM, Model Coordinator, Admin (WBS); DPM, Model Coordinator, Admin (Dependencies)



WBS / Project · p. 50




Activity Dependencies · p. 51



Set dependency · p. 52

WBS / Project

Used by: SIC, DPM, Model Coordinator, Admin

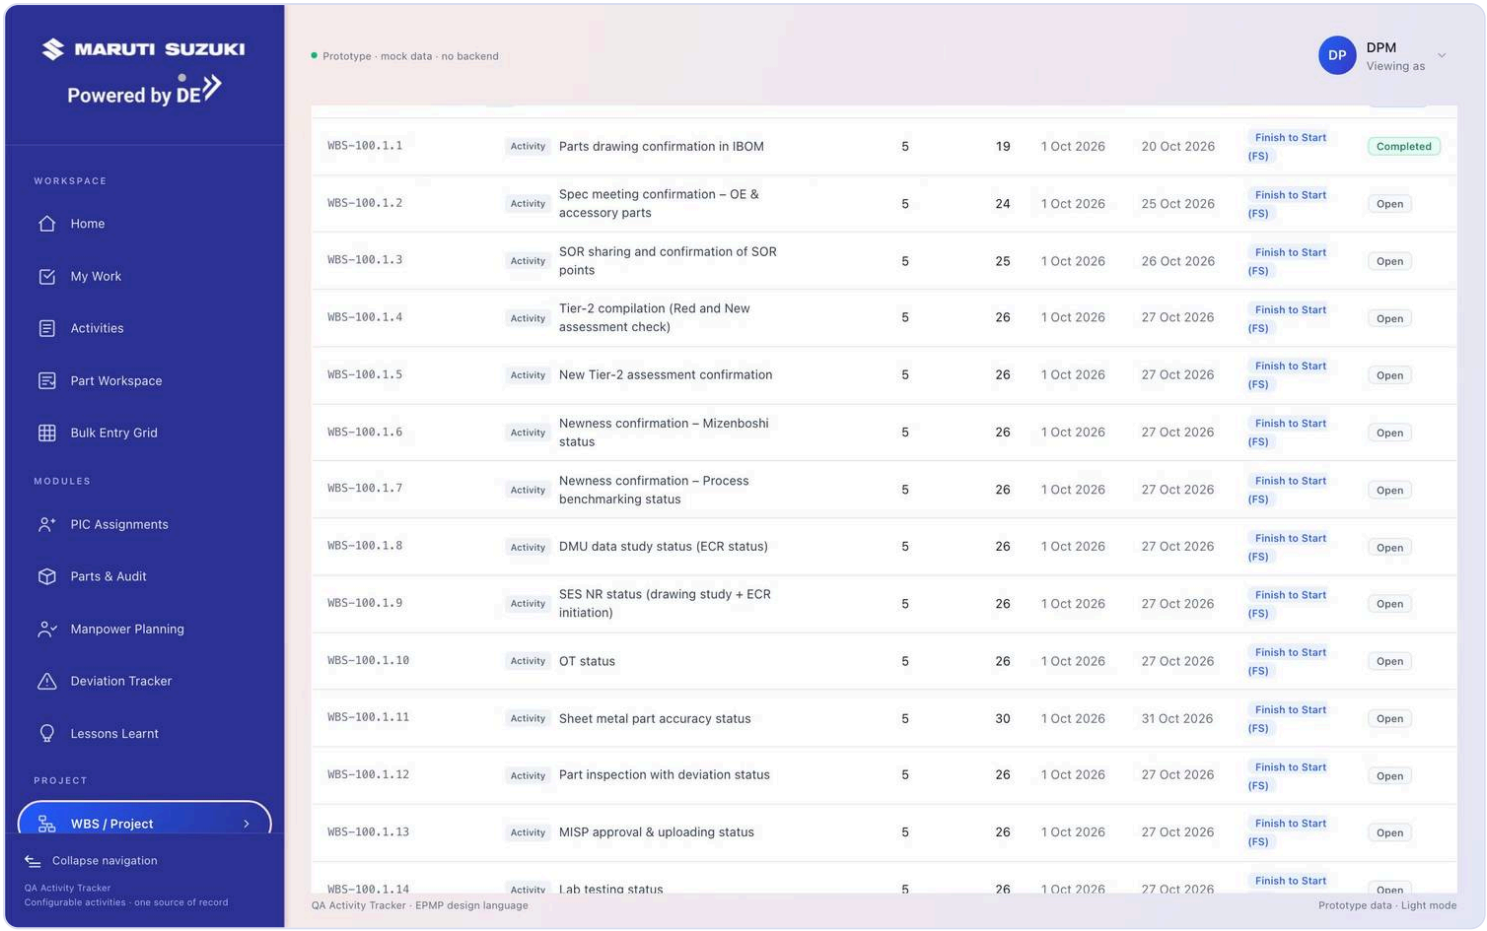

Purpose


The work breakdown per model: Milestone, Part, Activity, with effort, dates, dependency and status.

How to use

1. Choose the model.
2. “Expand all” and “Collapse all” control the tree.

Activity Dependencies

Used by: DPM, Model Coordinator, Admin

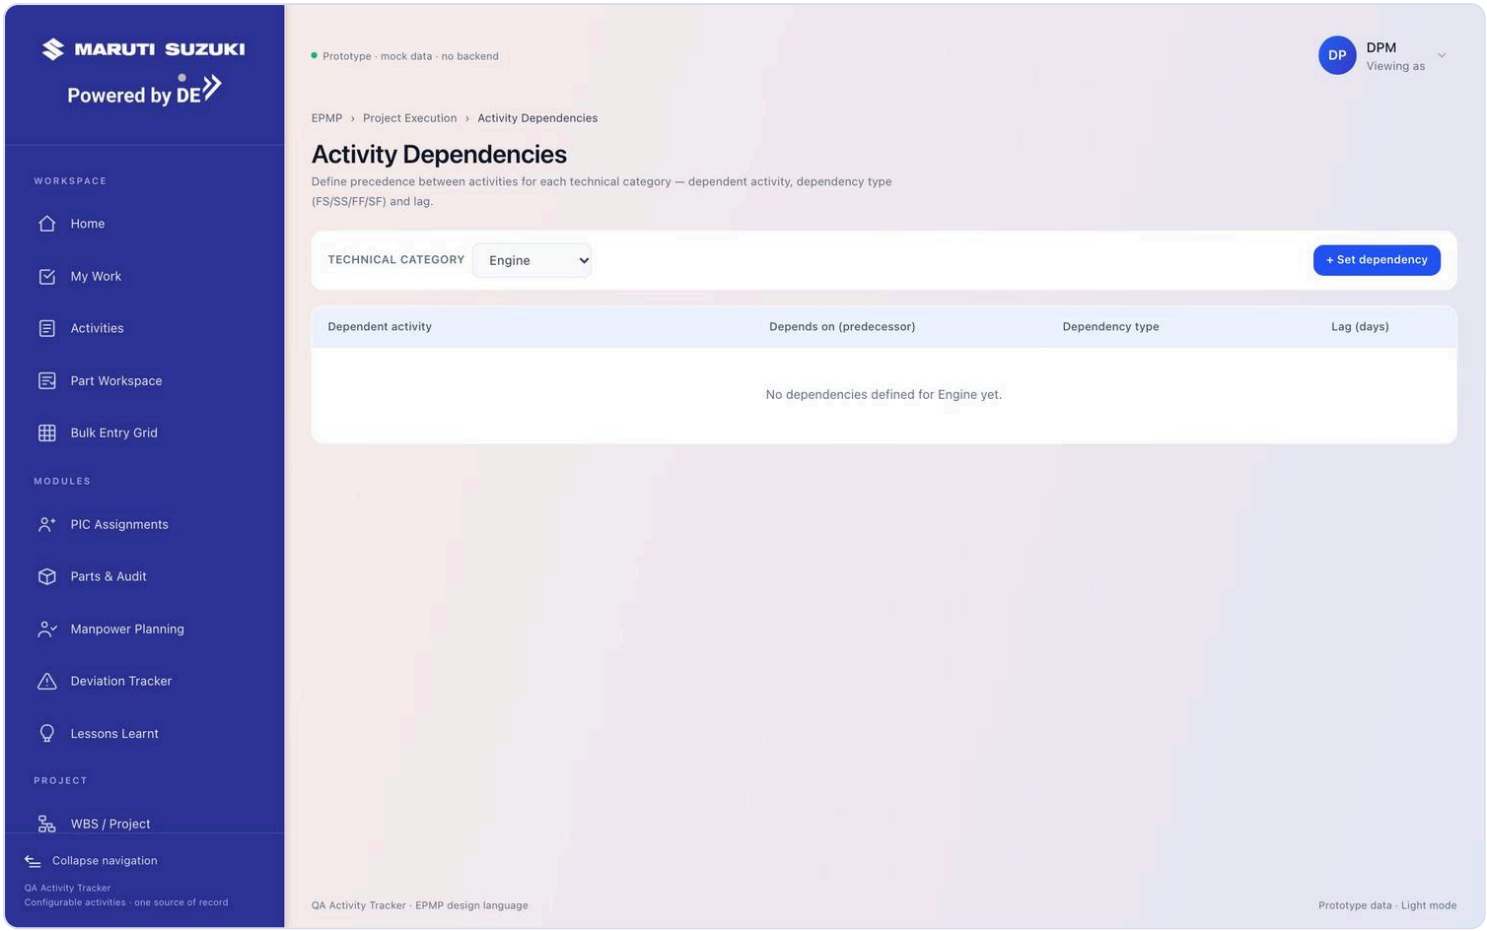

Purpose

Define which activity depends on which for each technical category.


> **Note.** The list is empty until dependencies are set for the chosen category.

How to use

1. Select the technical category.
2. The table lists dependent activity, predecessor, type and lag.
3. “Set dependency” opens the dialog on the next page.

Set dependency

Used by: DPM, Admin

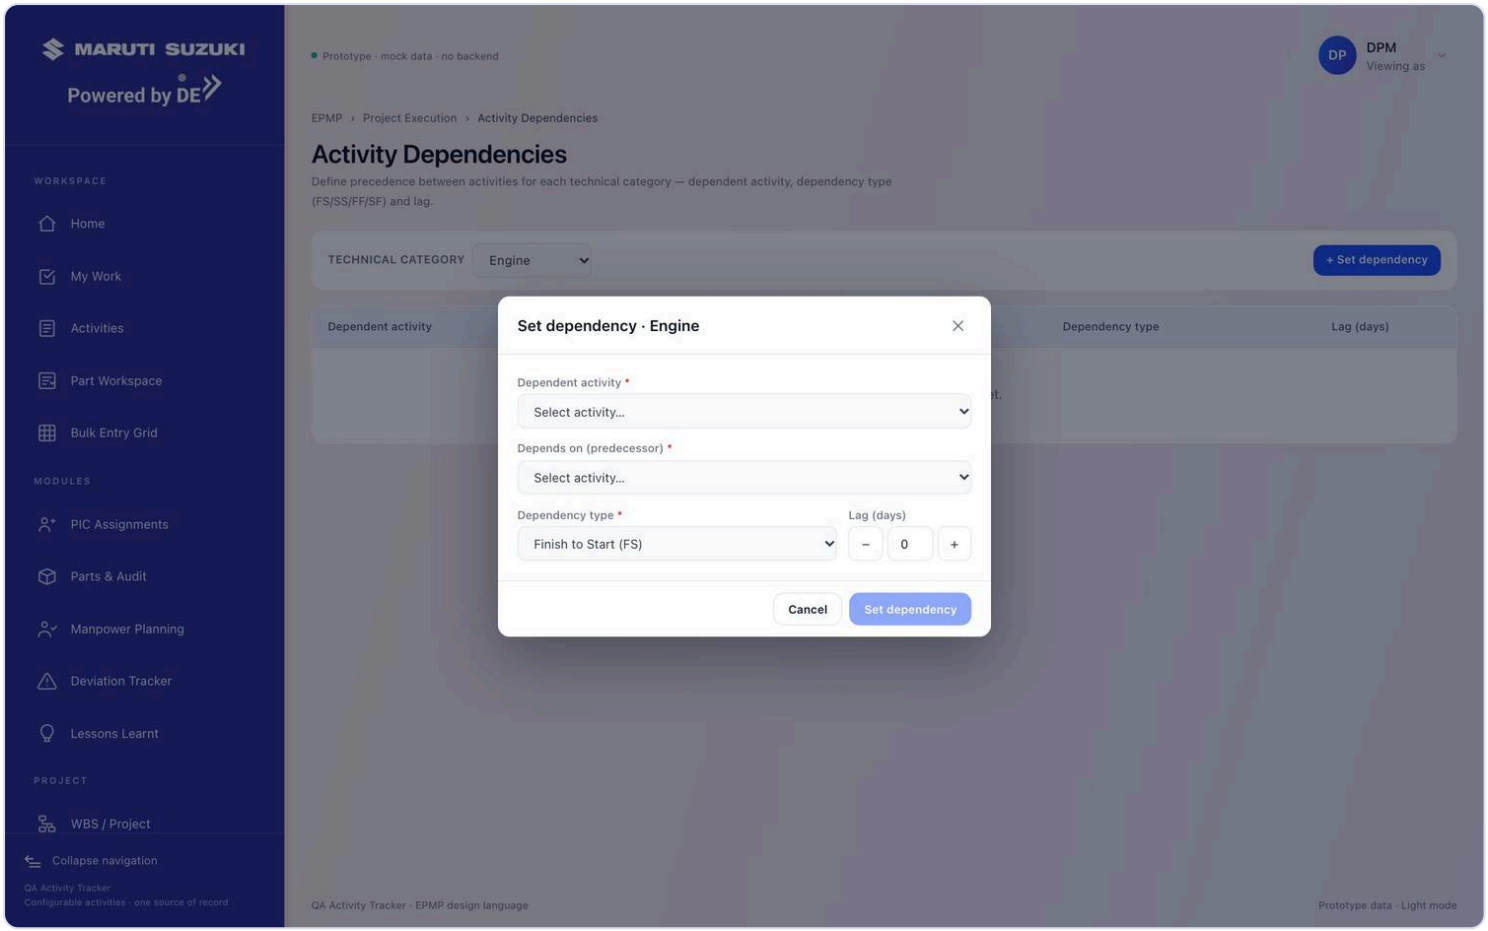

Purpose

Add a dependency between two activities of a technical category.

> **Note.** Circular and duplicate dependencies are rejected.

How to use

1. Pick the dependent activity and the predecessor.
2. Choose the type (Finish to Start by default).
3. Set the lag in days and click “Set dependency”.

CHAPTER 9 MONITOR

Resource & travel planning

Balance PIC workload, and make each vendor trip count.

What it does

Manpower Planning shows how loaded each PIC is and plans vendor visits. A planned visit shows other parts at the same vendor and other vendors in the same location, so one trip covers more.

What you can do


- PIC load: parts, vendors, activities, open, overdue and to-validate per PIC, with a load bar.
- Vendor visits: PIC, vendor, date and purpose, with a status.
- Suggestions of other parts and nearby vendors for a planned visit.

Rules you can rely on


- Load is measured in counts of parts and activities, not hours.

Used by

PIC, SIC, DPM, Admin



Manpower Planning: PIC load · p. 54




Manpower Planning: vendor visits · p. 55

C9A

Manpower Planning: PIC load

Used by: PIC, SIC, DPM, Admin

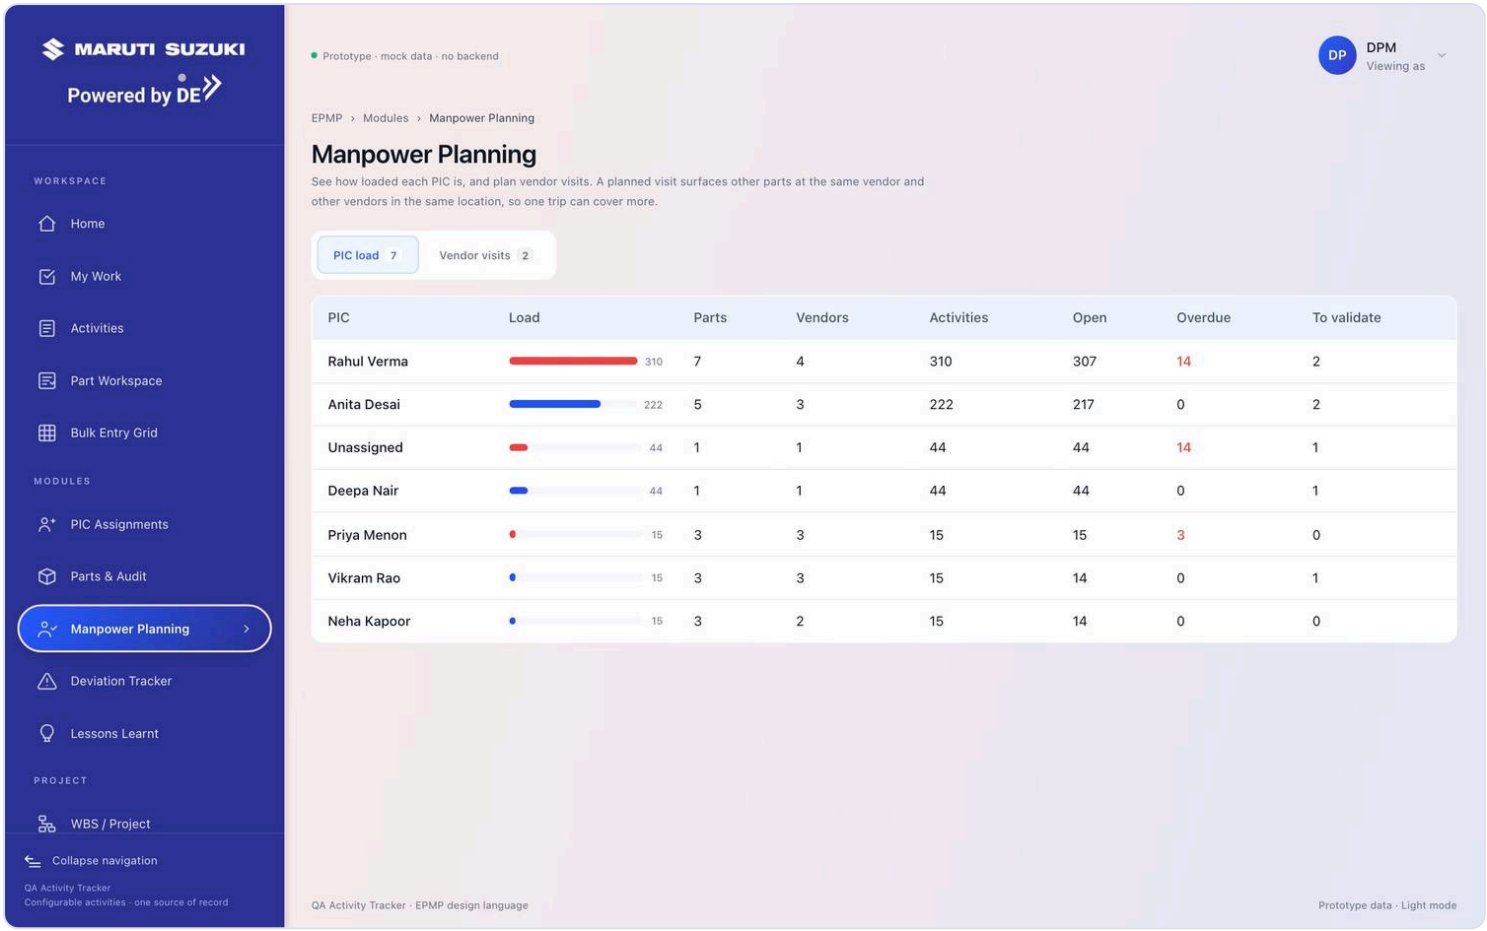

Purpose


How loaded each PIC is.

How to use

1. Read the load bar and the counts per PIC.
2. Spot PICs with many overdue or to-validate items.

Manpower Planning: vendor visits

Used by: PIC, SIC, DPM, Admin

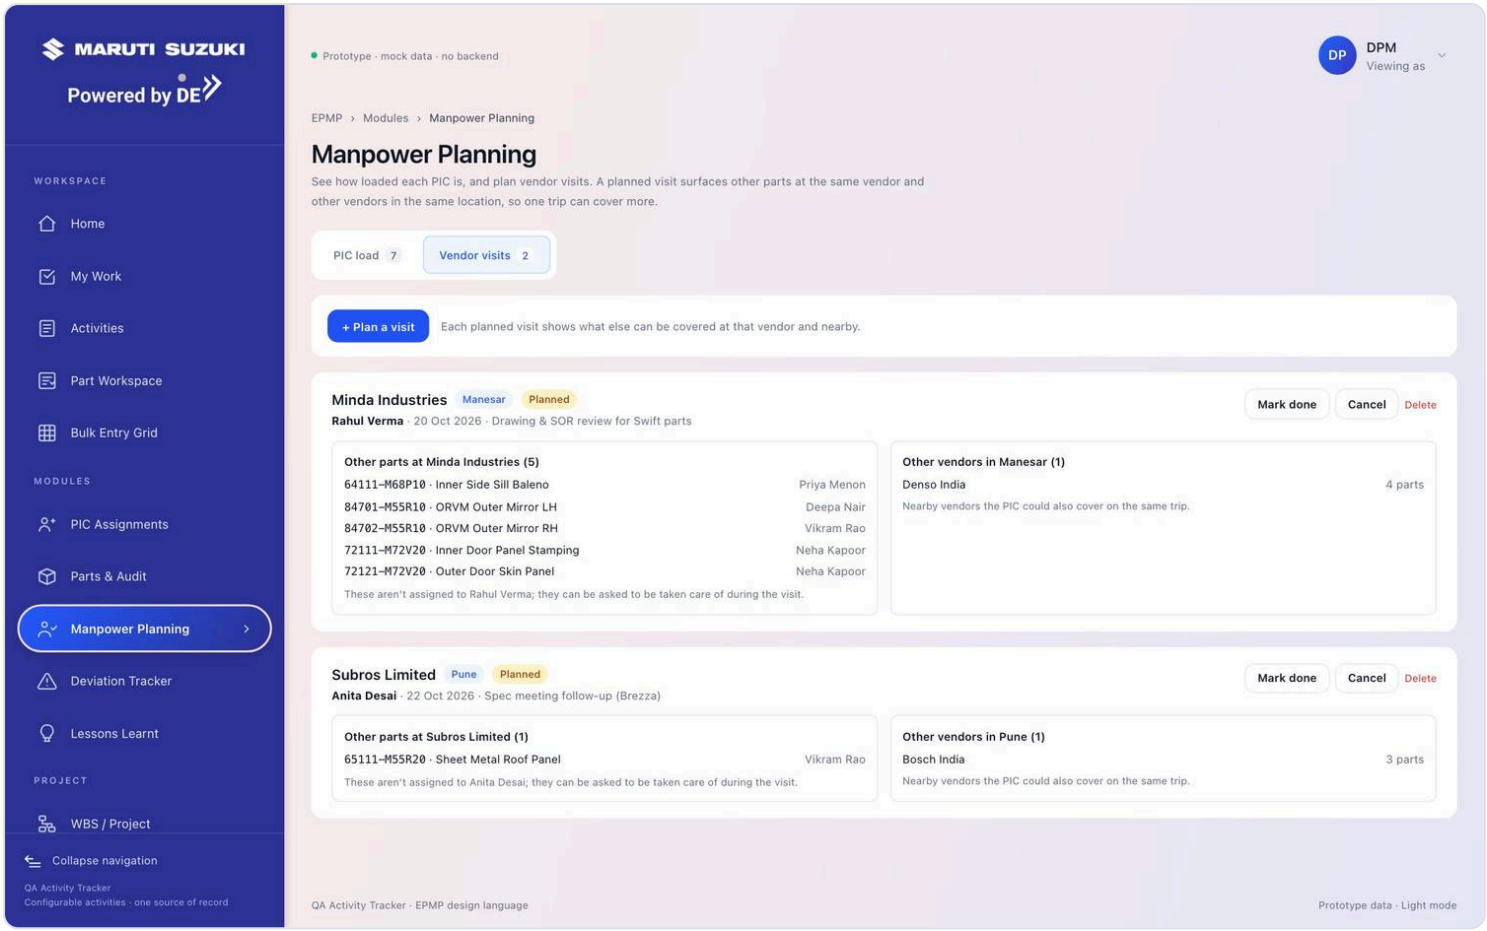

Purpose

Plan vendor visits so one trip covers more.

How to use

1. Add a planned visit with PIC, vendor, date and purpose.
2. See other parts at the same vendor and other vendors nearby.

CHAPTER 10 MONITOR

Monitoring & reporting

Dashboards for every role, down to the part.

What it does

Dashboards are generated from the activity definitions and respect each role's scope. The 46 activity dashboards provided by the client are embedded, and cross-activity dashboards compare activities for one model or part.

What you can do

- Overview dashboard: completion by model and department, filtered by milestone, section, model, vendor and type.
- Activity dashboards: one for each of the 46 client dashboards, embedded in the tracker.
- Cross-activity dashboards and custom charts, with an editable layout.
- Click-through from a chart or tile to the list of parts behind it.
- Download CSV from the entry and validation grids.

Rules you can rely on

- Dashboards are covered in the separate dashboard pack and are not repeated in this manual.
- Export buttons on dashboards are simulated in the prototype; grid CSV downloads are real.

Used by

All roles, scoped to their view

This capability has no screens in this manual. See the separate dashboard pack.

APPENDIX A

Activity reference (46 activities, 467 fields)

One page set per activity: where it sits, the approval flow, its form as the PIC sees it and every field with type, who enters it and who validates it.

#	Activity ID	Activity	Milestone	Fields	Page
1	pp-1	Parts drawing confirmation in IBOM	PP	7	p. 59
2	pp-2	Spec meeting confirmation – OE & accessory parts	PP	11	p. 60
3	pp-3	SOR sharing and confirmation of SOR points	PP	7	p. 62
4	pp-4	Tier-2 compilation (Red and New assessment check)	PP	4	p. 64
5	pp-5	New Tier-2 assessment confirmation	PP	3	p. 66
6	pp-6a	Newness confirmation – Mizenboshi status	PP	11	p. 68
7	pp-6b	Newness confirmation – Process benchmarking status	PP	7	p. 70
8	pp-7	DMU data study status (ECR status)	PP	4	p. 72
9	pp-8	SES NR status (drawing study + ECR initiation)	PP	9	p. 74
10	pp-9	OT status	PP	24	p. 75
11	pp-10	Sheet metal part accuracy status	PP	4	p. 77
12	pp-11	Part inspection with deviation status	PP	14	p. 79
13	pp-12	MISP approval & uploading status	PP	5	p. 81
14	pp-13	Lab testing status	PP	9	p. 82
15	pp-14	BCF status (Body Checking Fixture)	PP	11	p. 83
16	pp-15a	Colour parts check – Testing	PP	8	p. 85
17	pp-15b	Colour parts check – Colour comparison	PP	7	p. 86
18	pp-16	Parts list with deviations & special parts list	PP	8	p. 87
19	mpp-1	OTOP status	MPP	16	p. 88
20	mpp-5	PP Hinkai trial closure status – QAND & Production	MPP	11	p. 90
21	mpp-6	SOR adherence confirmation (Div Head deviation via E-Doc)	MPP	10	p. 92
22	mpp-7	Lab testing status	MPP	12	p. 94
23	mpp-8	Process audit status	MPP	9	p. 96
24	mpp-9	Process capability (critical parameters)	MPP	8	p. 97
25	mpp-10	Homologation marking confirmation	MPP	10	p. 98
26	mpp-11	Set part / semi-finished part status	MPP	4	p. 100
27	mpp-12	MISP revision status	MPP	3	p. 102
28	mpp-13	Spare kit part status	MPP	11	p. 104
29	mpp-14	Parts list with deviations & special parts list	MPP	8	p. 106
30	pilot-1	OTOP status (ECN cases)	SOP	10	p. 107
31	pilot-2	Sheet metal part accuracy status	SOP	12	p. 109
32	pilot-3	Part inspection with deviation status (ECN cases)	SOP	15	p. 111

33	pilot-17	MISP revision status	SOP	3	p. 113
34	pilot-4	MPP Hinkai trial closure status – QAND & Production	SOP	6	p. 115
35	pilot-5	BCF status (Body Checking Fixture)	SOP	11	p. 116
36	pilot-7	PPAP file approval status	SOP	4	p. 118
37	pilot-8	Lab testing status	SOP	9	p. 120
38	pilot-9	Homologation marking confirmation (camera inspection)	SOP	12	p. 121
39	pilot-10	List of limit samples for applicable parts	SOP	7	p. 123
40	pilot-11	IFM mail initiation and checklist completion	SOP	6	p. 124
41	pilot-14	Part updation in Regulatory App	SOP	2	p. 125
42	pilot-15	Part updation in SMIR system	Pilot	3	p. 126
43	pilot-16	Part updation in CPM portal	SOP	4	p. 128
44	pilot-6	PPVT confirmation	SOP	6	p. 130
45	pilot-18	PPVT confirmation – Vendor PPVT details	SOP	29	p. 131
46	pilot-12	SOP Readiness Confirmation from Supplier	SOP	73	p. 133


ACTIVITY · PP-1 · PP MILESTONE


1 Parts drawing confirmation in IBOM

7 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

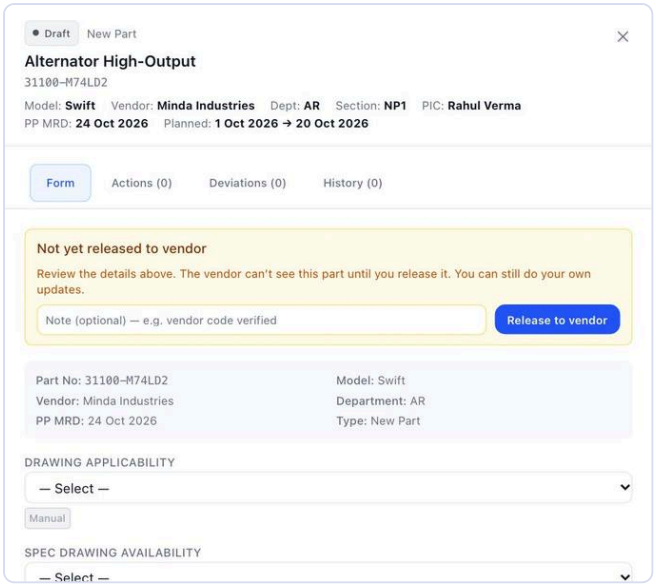

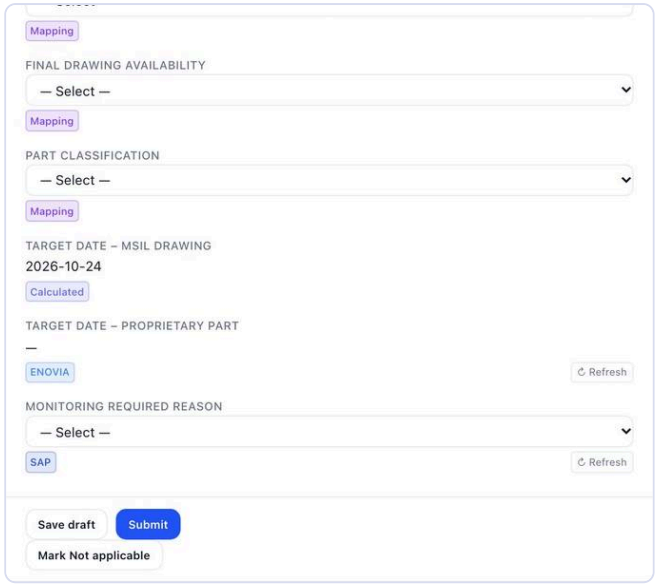

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Drawing applicability	Yes / No	PIC	-	Manual entry	-	-
2	Spec drawing availability	Dropdown	PIC	-	Mapping table	Dashboard, Part list	Available / Not available
3	Final drawing availability	Dropdown	PIC	-	Mapping table	-	Available / Not available
4	Part classification	Dropdown	PIC	-	Mapping table	Dashboard, Part list	MSIL / Proprietary
5	Target date – MSIL drawing	Date	System	-	Calculated	-	-
6	Target date – Proprietary part	Date	System	-	ENOVIA	-	-
7	Monitoring required reason	Dropdown	PIC	-	SAP	-	New Part / ECN Part

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · PP-2 · PP MILESTONE


2 Spec meeting confirmation – OE & accessory parts

11 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** Yes

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

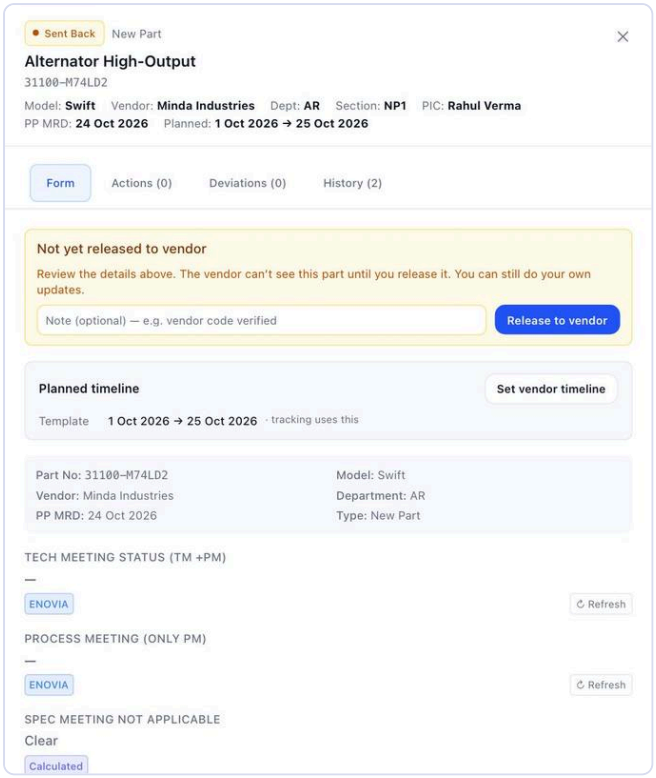

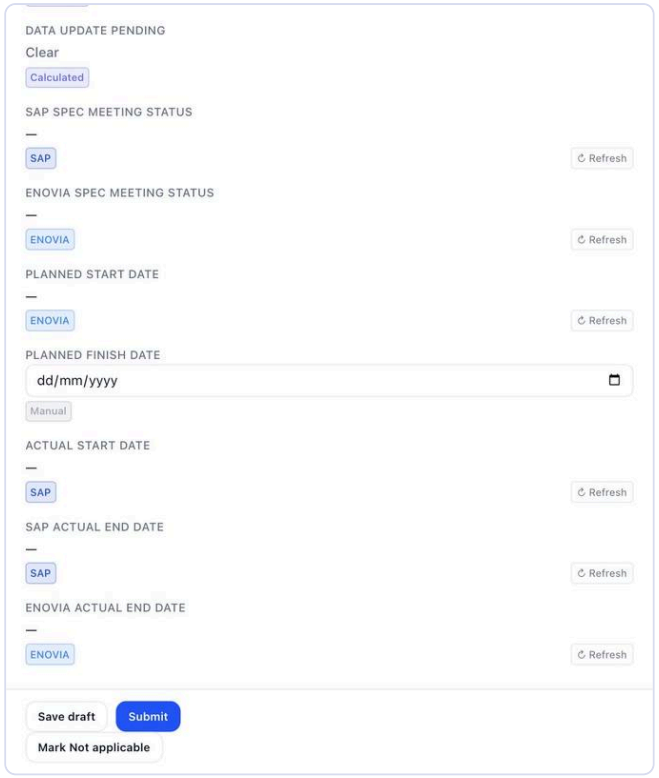

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Tech meeting status (TM +PM)	Yes / No	System	-	ENOVIA	Dashboard, Part list	-
2	Process meeting (only PM)	Yes / No	System	-	ENOVIA	-	-
3	Spec meeting not applicable	Flag	System	-	Calculated	-	-
4	Data update pending	Flag	System	-	Calculated	-	-
5	SAP spec meeting status	Dropdown	System	-	SAP	Dashboard, Part list	Not Initiated / Initiated / Pending For Approval / Approved
6	Enovia spec meeting status	Dropdown	System	-	ENOVIA	-	Initiated / Pending / Approved
7	Planned start date	Date	System	-	ENOVIA	-	-
8	Planned finish date	Date	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
9	Actual start date	Date	System	-	SAP	-	-
10	SAP actual end date	Date	System	-	SAP	-	-
11	Enovia actual end date	Date	System	-	ENOVIA	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-3 · PP MILESTONE


3 SOR sharing and confirmation of SOR points

7 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

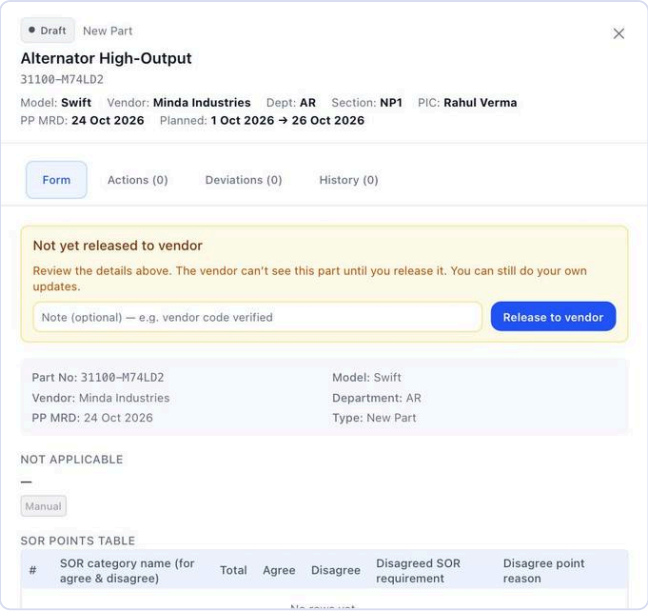

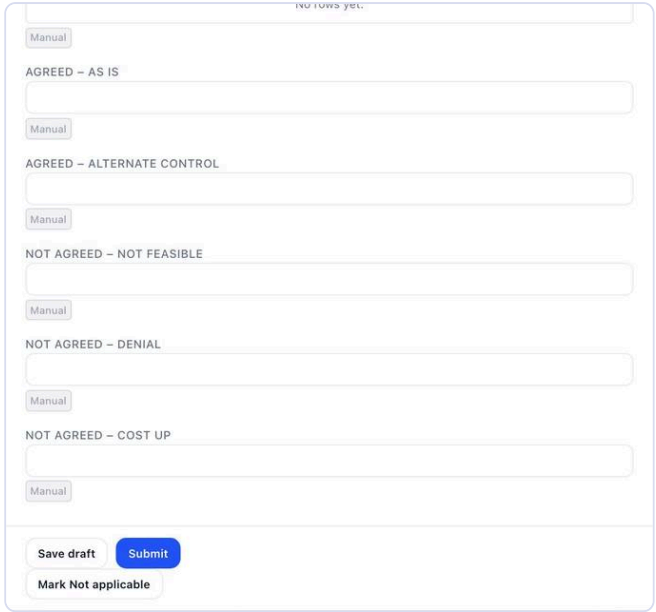

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Not applicable	Number	Vendor	PIC	Manual entry	-	-
2	SOR points table	Table	Vendor	PIC	Manual entry	-	Columns: SOR category name (for agree & disagree), Total, Agree, Disagree, Disagreed SOR requirement, Disagree point reason
3	Agreed – As is	Number	PIC	-	Manual entry	Dashboard	-
4	Agreed – Alternate control	Number	PIC	-	Manual entry	-	-
5	Not agreed – Not feasible	Number	PIC	-	Manual entry	Dashboard	-
6	Not agreed – Denial	Number	PIC	-	Manual entry	-	-
7	Not agreed – Cost up	Number	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-4 · PP MILESTONE

4 Tier-2 compilation (Red and New assessment check)

4 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

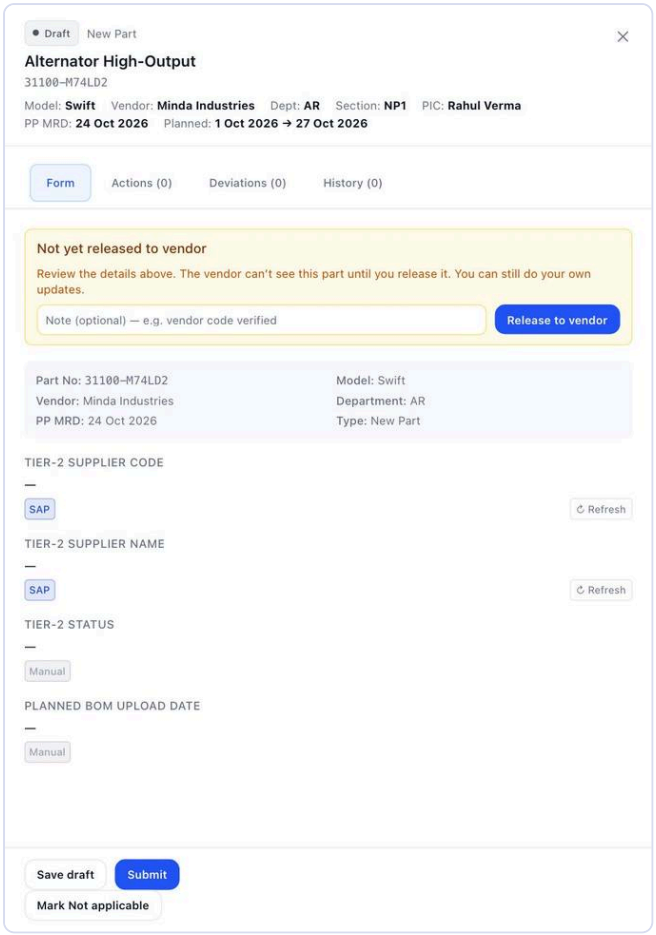

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Tier-2 supplier code	Number	System	-	SAP	-	-
2	Tier-2 supplier name	Text	System	-	SAP	-	-
3	Tier-2 status	Dropdown	System	-	Manual entry	Dashboard	R / Y / G
4	Planned BOM upload date	Date	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-5 · PP MILESTONE

5 New Tier-2 assessment confirmation

3 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

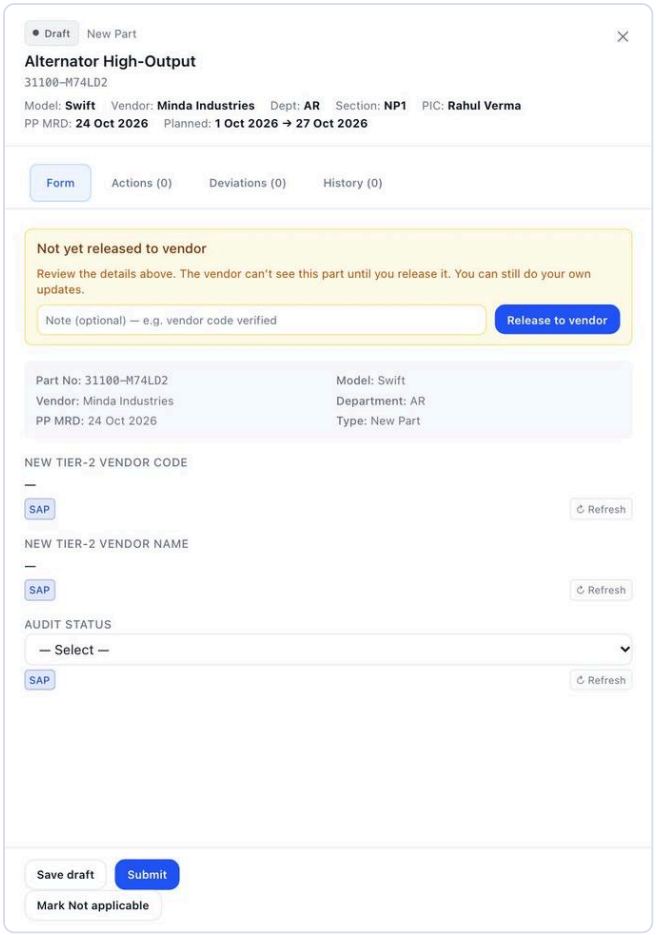

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	New Tier-2 vendor code	Number	System	-	SAP	-	-
2	New Tier-2 vendor name	Text	System	-	SAP	-	-
3	Audit status	Dropdown	PIC	-	SAP	Dashboard, Part list	Done / Not done

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-6A · PP MILESTONE


6 Newness confirmation – Mizenboshi status

11 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

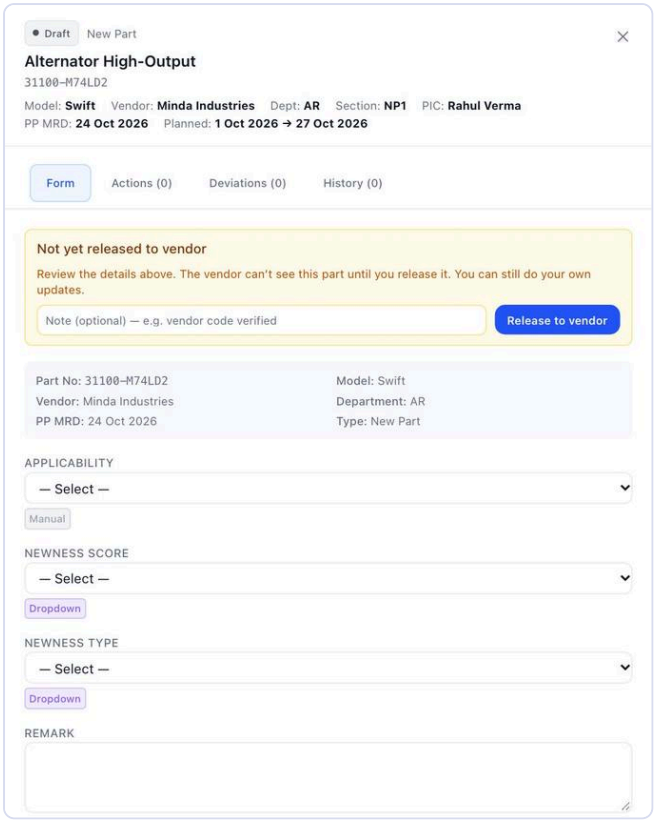

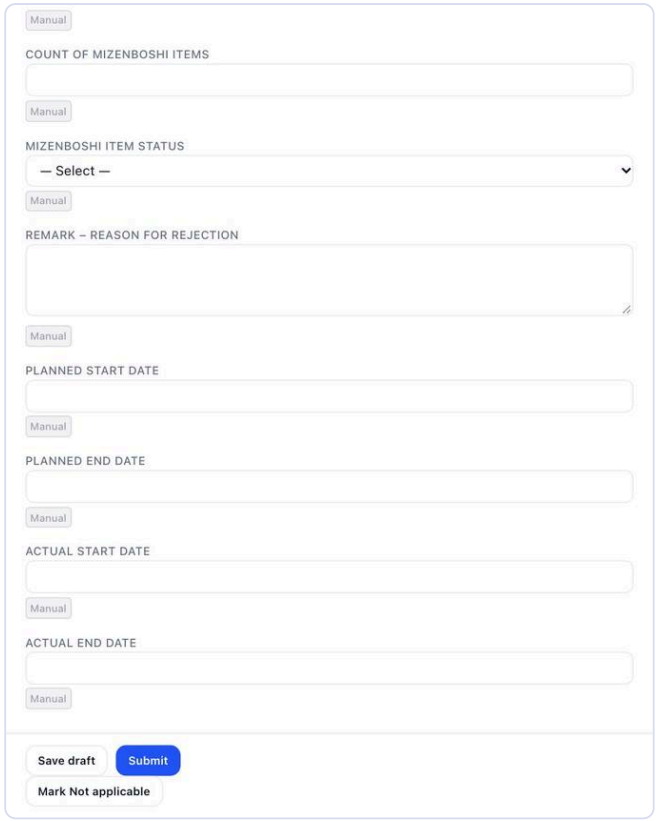

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Newness score	Dropdown	PIC	-	Dropdown list	Dashboard	3 / 4 / 5
3	Newness type	Dropdown	PIC	-	Dropdown list	-	New Technology / New Process
4	Remark	Long text	PIC	-	Manual entry	-	-
5	Count of Mizenboshi items	Number	PIC	-	Manual entry	-	-
6	Mizenboshi item status	Dropdown	PIC	-	Manual entry	-	Accepted / Rejected by Engineering
7	Remark – Reason for rejection	Long text	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
8	Planned start date	Text	PIC	-	Manual entry	-	-
9	Planned end date	Text	PIC	-	Manual entry	-	-
10	Actual start date	Text	PIC	-	Manual entry	-	-
11	Actual end date	Text	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-6B · PP MILESTONE


7 Newness confirmation – Process benchmarking status

7 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

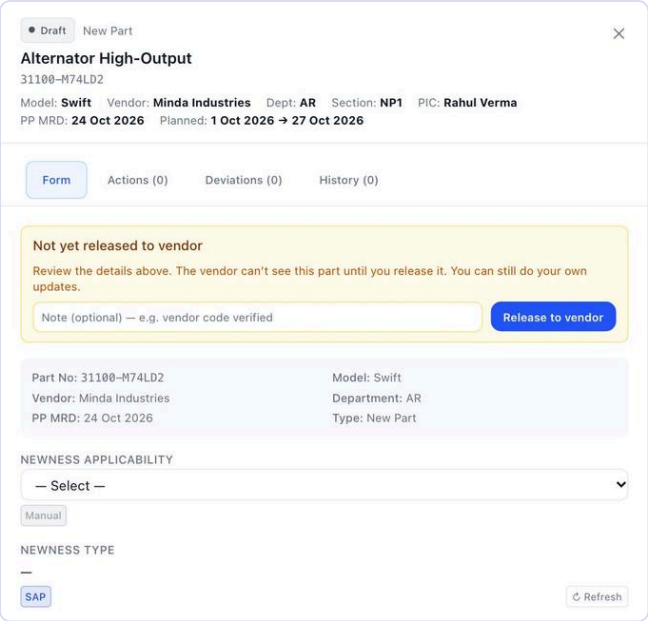

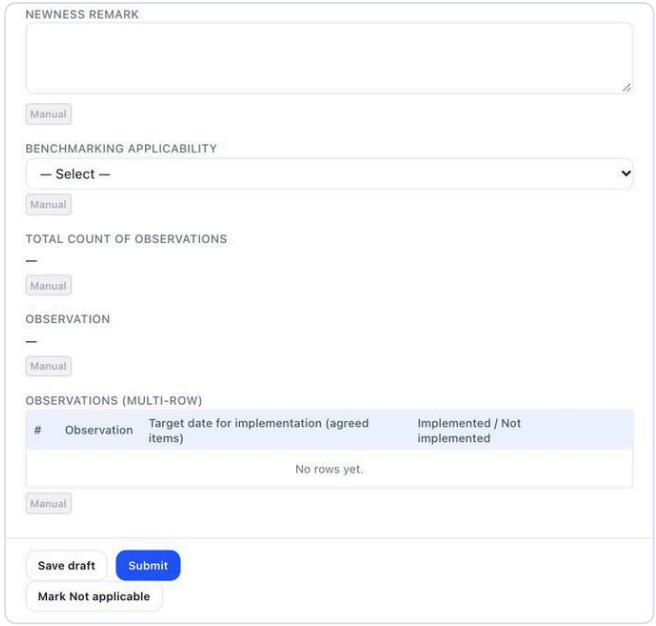

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Newness applicability	Yes / No	PIC	-	Manual entry	-	-
2	Newness type	Dropdown	System	-	SAP	-	New Technology / New Design / New Vendor / Existing vendor New part category / New Process / New Plant / New Material / Localization / Others
3	Newness remark	Long text	PIC	-	Manual entry	-	-
4	Benchmarking applicability	Yes / No	PIC	-	Manual entry	-	-
5	Total count of observations	Number	Vendor	PIC	Manual entry	-	-
6	Observation	Long text	Vendor	PIC	Manual entry	-	-
7	Observations (multi-row)	Table	Vendor	PIC	Manual entry	-	Columns: Observation, Target date for implementation (agreed items), Implemented / Not implemented

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-7 · PP MILESTONE

8 DMU data study status (ECR status)

4 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

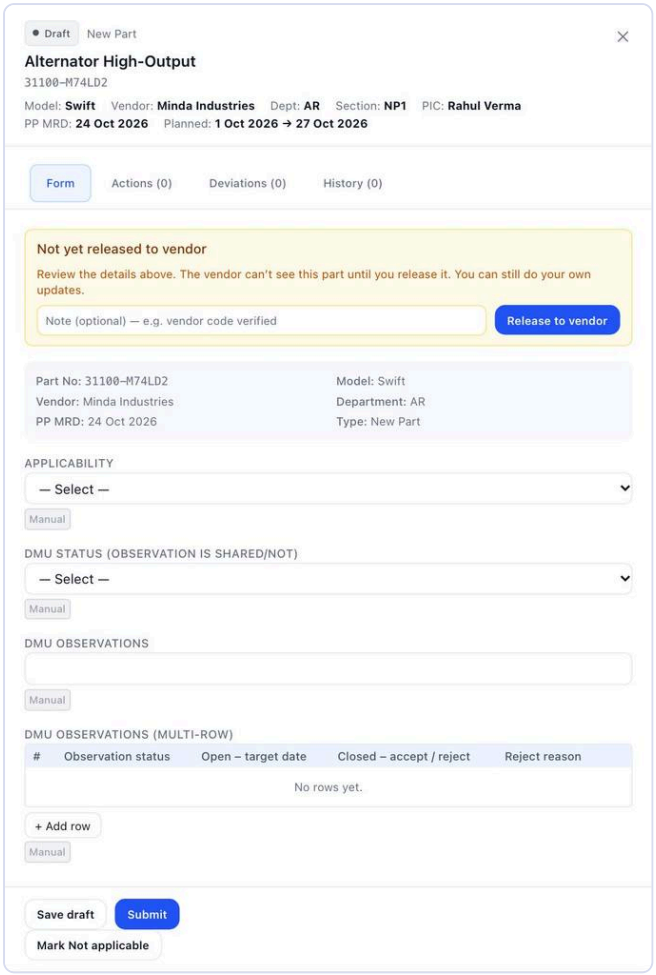

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	DMU status (observation is shared/not)	Dropdown	PIC	-	Manual entry	Dashboard	Completed / Pending
3	DMU observations	Number	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
4	DMU observations (multi-row)	Table	PIC	-	Manual entry	-	Columns: Observation status, Open – target date, Closed – accept / reject, Reject reason

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-8 · PP MILESTONE


9 SES NR status (drawing study + ECR initiation)

9 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

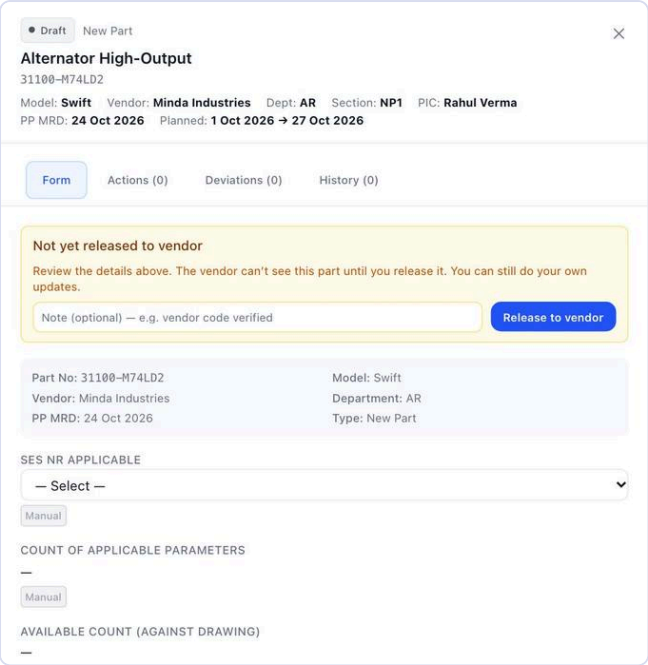

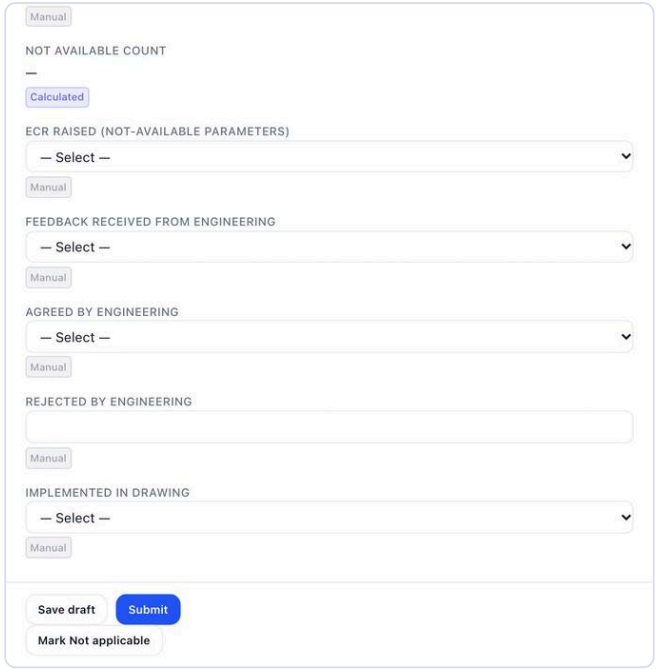

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	SES NR applicable	Yes / No	PIC	-	Manual entry	-	-
2	Count of applicable parameters	Number	Vendor	PIC	Manual entry	-	-
3	Available count (against drawing)	Number	Vendor	PIC	Manual entry	-	-
4	Not available count	Number	System	-	Calculated	-	-
5	ECR raised (not-available parameters)	Yes / No	PIC	-	Manual entry	-	-
6	Feedback received from engineering	Yes / No	PIC	-	Manual entry	-	-
7	Agreed by engineering	Yes / No	PIC	-	Manual entry	-	-
8	Rejected by engineering	Text	PIC	-	Manual entry	-	-
9	Implemented in drawing	Yes / No	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-9 · PP MILESTONE


10 OT status


24 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** Yes

Form screen (PIC view, sample part 31100-M74LD2) · 3 image panels, read left to right

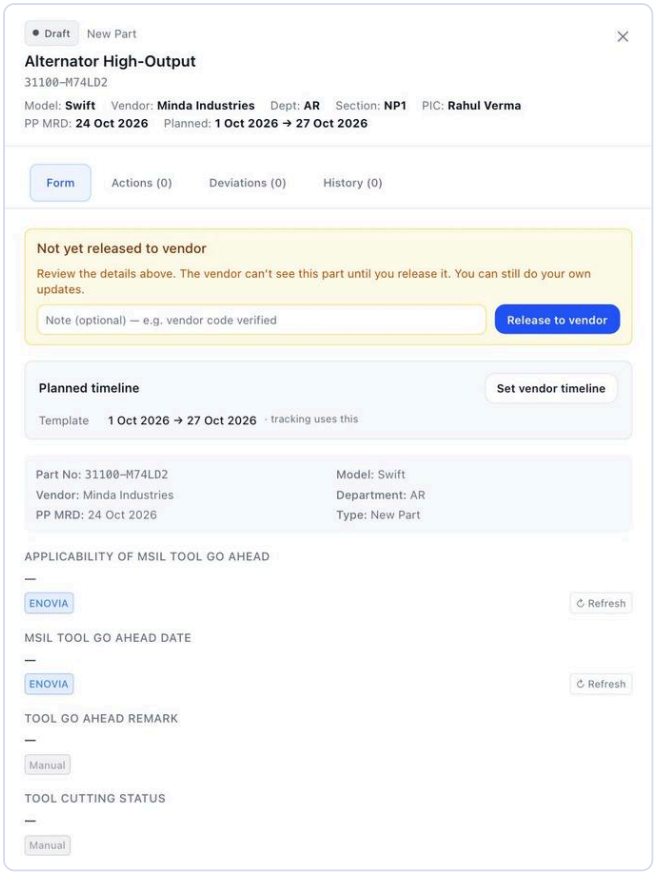

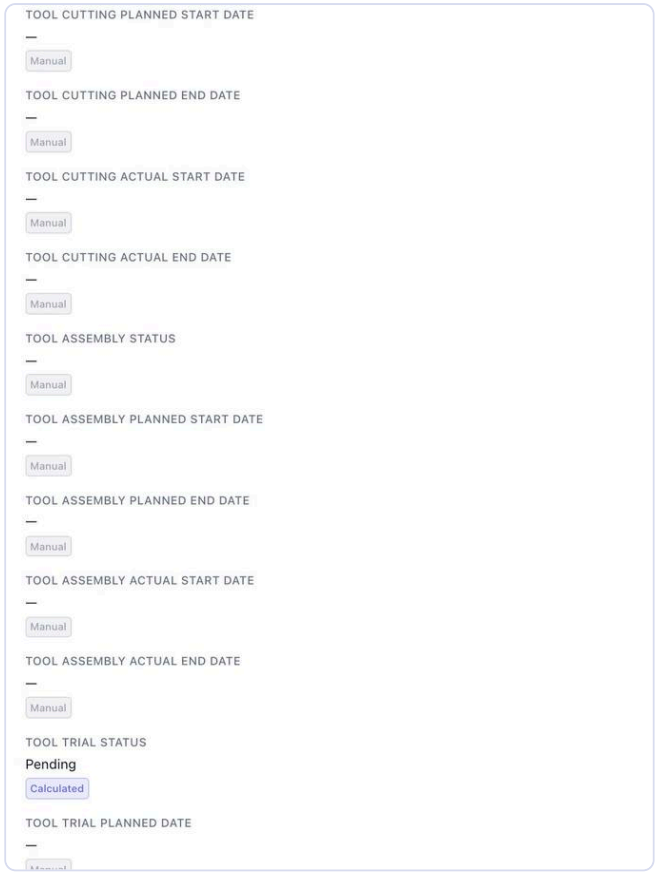

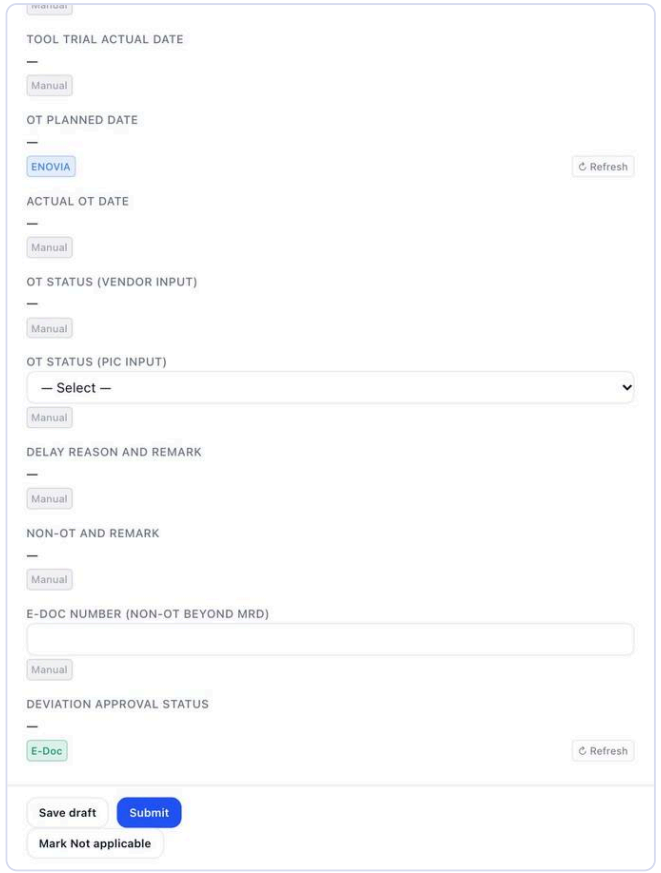

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability of MSIL tool go ahead	Yes / No	System	-	ENOVIA	-	-
2	MSIL tool go ahead date	Date	System	-	ENOVIA	-	-
3	Tool go ahead remark	Long text	Vendor	PIC	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
4	Tool cutting status	Dropdown	Vendor	PIC	Manual entry	-	Started / Completed
5	Tool cutting planned start date	Date	Vendor	PIC	Manual entry	-	-
6	Tool cutting planned end date	Date	Vendor	PIC	Manual entry	-	-
7	Tool cutting actual start date	Date	Vendor	PIC	Manual entry	-	-
8	Tool cutting actual end date	Date	Vendor	PIC	Manual entry	-	-
9	Tool assembly status	Dropdown	Vendor	PIC	Manual entry	-	Started / Completed
10	Tool assembly planned start date	Date	Vendor	PIC	Manual entry	-	-
11	Tool assembly planned end date	Date	Vendor	PIC	Manual entry	-	-
12	Tool assembly actual start date	Date	Vendor	PIC	Manual entry	-	-
13	Tool assembly actual end date	Date	Vendor	PIC	Manual entry	-	-
14	Tool trial status	Dropdown	System	-	Calculated	-	Done / Pending
15	Tool trial planned date	Date	Vendor	PIC	Manual entry	-	-
16	Tool trial actual date	Date	Vendor	PIC	Manual entry	-	-
17	OT planned date	Date	System	-	ENOVIA	-	-
18	Actual OT date	Date	Vendor	PIC	Manual entry	-	-
19	OT status (vendor input)	Dropdown	Vendor	PIC	Manual entry	Dashboard, Part list	OT / Non OT
20	OT status (PIC input)	Dropdown	PIC	-	Manual entry	-	OT / Non OT
21	Delay reason and remark	Dropdown	Vendor	PIC	Manual entry	-	ECN case / Tool maker selection delay / Tool go-ahead delay (MSIL) / Tool go-ahead delay (Vendor) / Design finalization delay (Vendor internal) / Tool maturation delay / Others / OT plan date > system defined target date
22	Non-OT and remark	Dropdown	Vendor	PIC	Manual entry	-	ECN case / Tool maker selection delay / Tool go-ahead delay (MSIL) / Tool go-ahead delay (Vendor) / Design finalization delay (Vendor internal) / Tool maturation delay / Others / OT plan date > system defined target date
23	E-Doc number (Non-OT beyond MRD)	Text	PIC	-	Manual entry	-	-
24	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-10 · PP MILESTONE

11 Sheet metal part accuracy status

4 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

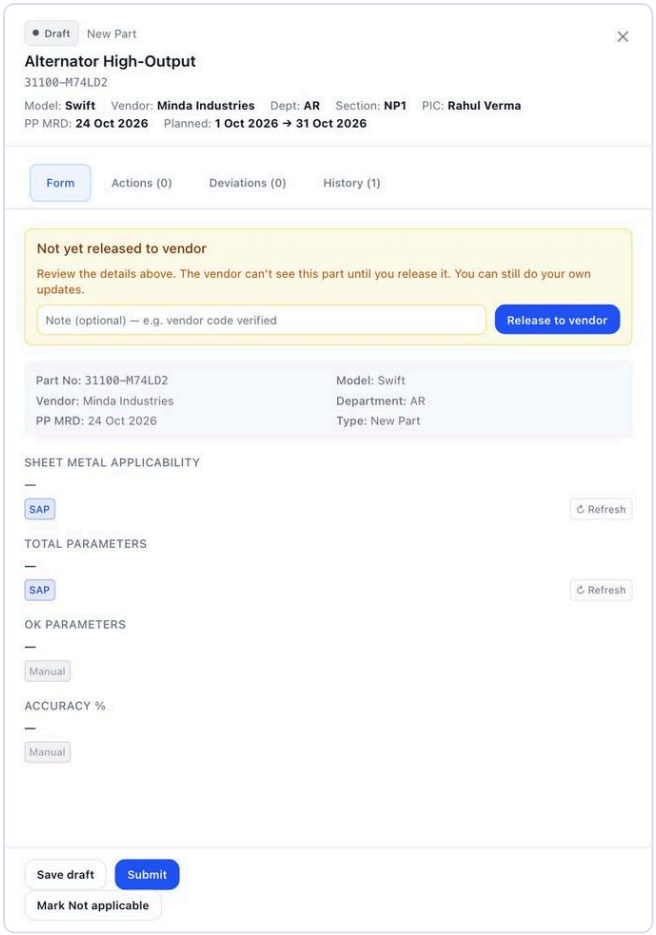

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Sheet metal applicability	Yes / No	System	-	SAP	-	-
2	Total parameters	Number	System	-	SAP	-	-
3	OK parameters	Number	Vendor	PIC	Manual entry	-	-
4	Accuracy %	Percent	Vendor	PIC	Manual entry	Dashboard	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-11 · PP MILESTONE


12 Part inspection with deviation status

14 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

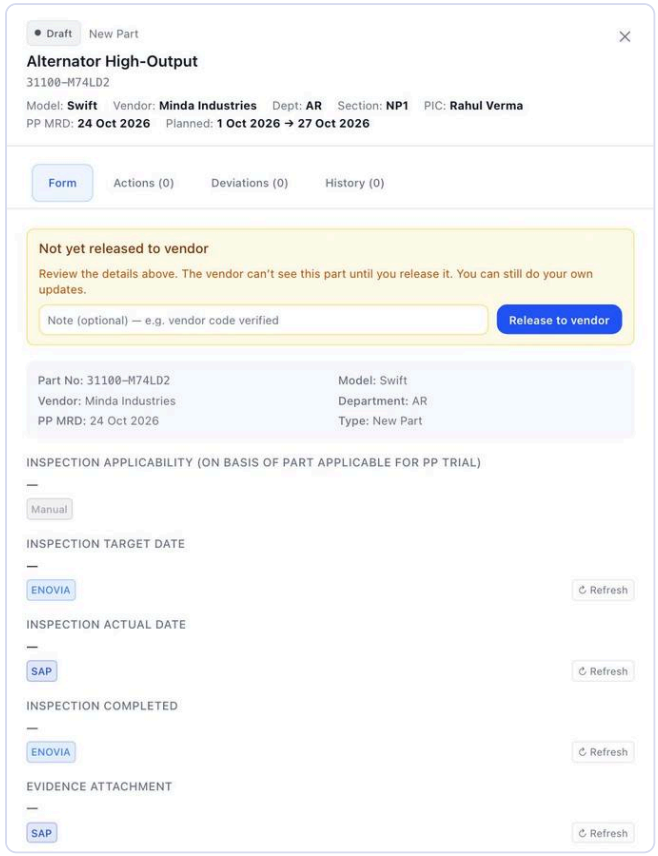

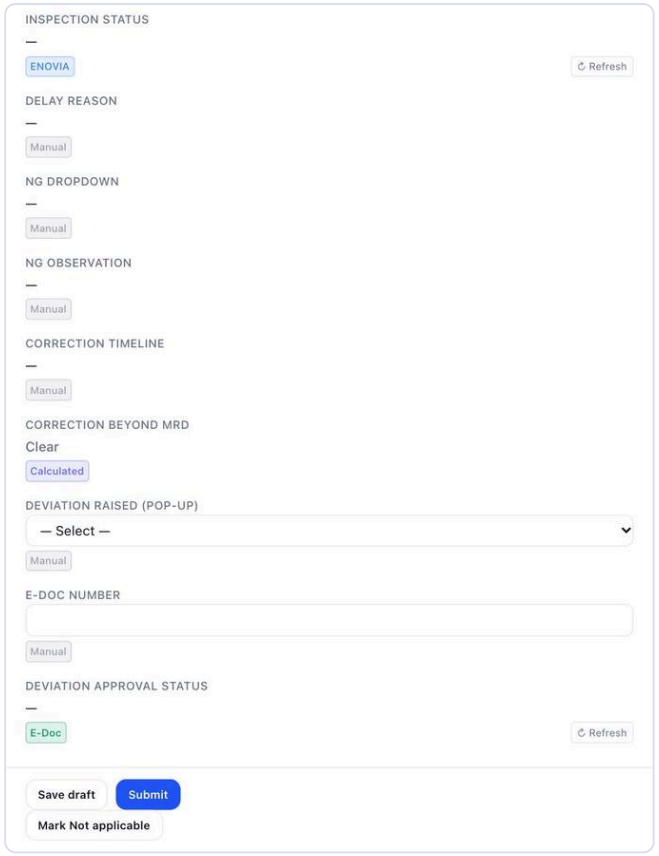

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Inspection applicability (on basis of part applicable for PP trial)	Yes / No	Vendor	PIC	Manual entry	-	-
2	Inspection target date	Date	System	-	ENOVIA	-	-
3	Inspection actual date	Date	System	-	SAP	-	-
4	Inspection completed	Yes / No	System	-	ENOVIA	-	-
5	Evidence attachment	Yes / No	System	-	SAP	-	-
6	Inspection status	Dropdown	System	-	ENOVIA	Dashboard, Part list	OK / NG

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
7	Delay reason	Long text	Vendor	PIC	Manual entry	-	-
8	NG dropdown	Multi-select	Vendor	PIC	Manual entry	-	Appearance / Dimension / Material / Performance / Regulation
9	NG observation	Long text	Vendor	PIC	Manual entry	-	-
10	Correction timeline	Date	Vendor	PIC	Manual entry	-	-
11	Correction beyond MRD	Flag	System	-	Calculated	-	-
12	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
13	E-Doc number	Text	PIC	-	Manual entry	-	-
14	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected / In progress

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-12 · PP MILESTONE


13 MISP approval & uploading status

5 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

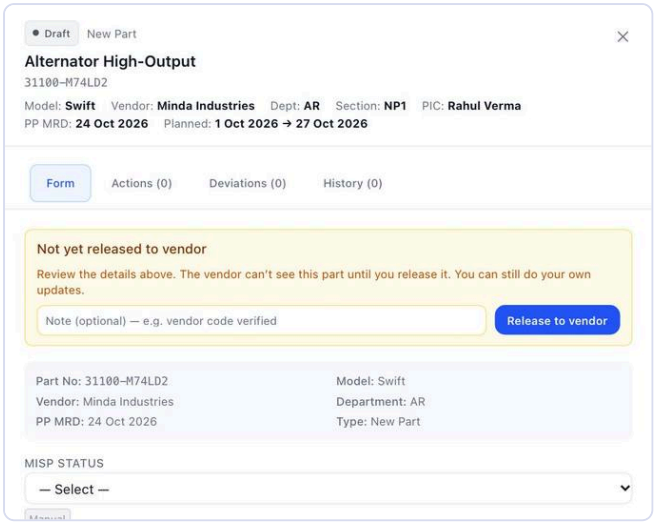

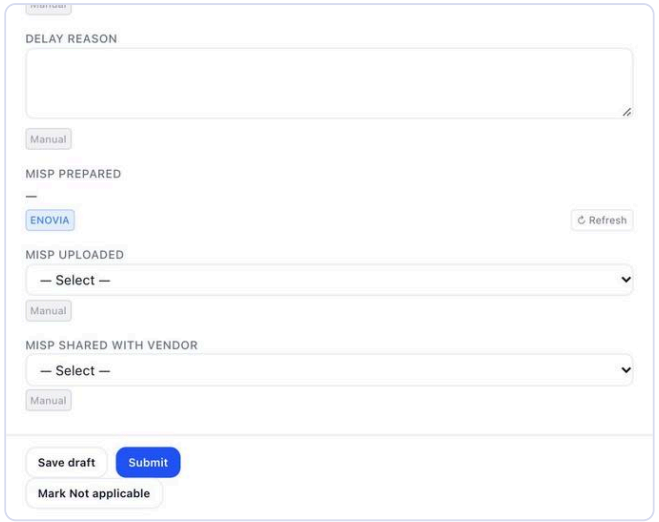

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	MISP status	Dropdown	PIC	-	Manual entry	Dashboard, Part list	Approved / Pending approval
2	Delay reason	Long text	PIC	-	Manual entry	-	-
3	MISP prepared	Yes / No	System	-	ENOVIA	-	-
4	MISP uploaded	Yes / No	PIC	-	Manual entry	-	-
5	MISP shared with vendor	Yes / No	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

14


ACTIVITY · PP-13 · PP MILESTONE


Lab testing status

9 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

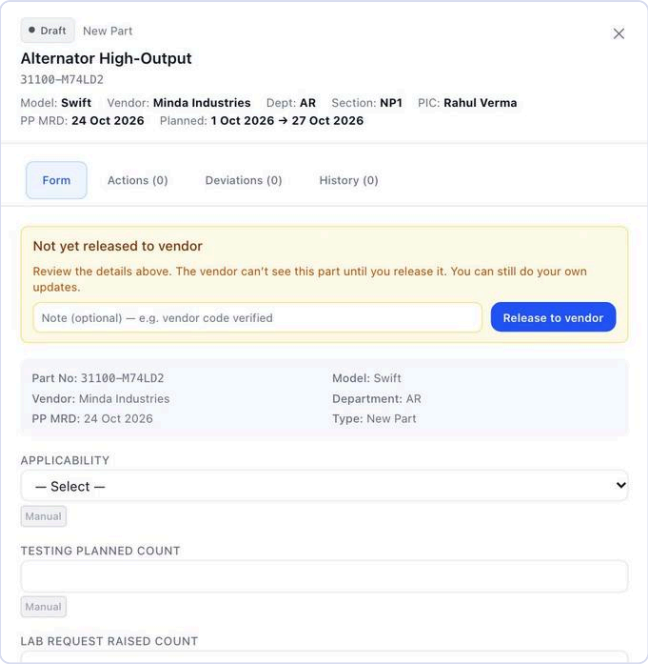

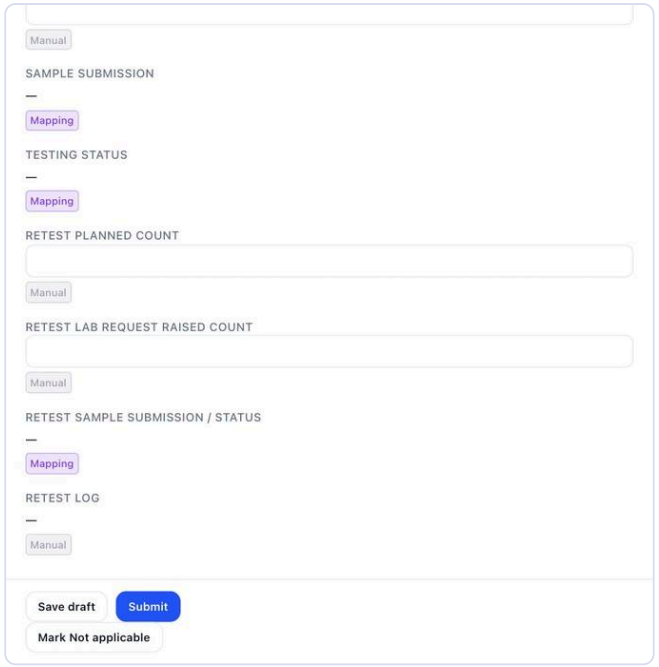

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Testing planned count	Number	PIC	-	Manual entry	-	-
3	Lab request raised count	Number	PIC	-	Manual entry	-	-
4	Sample submission	Dropdown	System	-	Mapping table	-	Submitted / Not submitted
5	Testing status	Dropdown	System	-	Mapping table	Dashboard, Part list	Under testing / OK / NG / Reference / Request rejected
6	Retest planned count	Number	PIC	-	Manual entry	-	-
7	Retest lab request raised count	Number	PIC	-	Manual entry	-	-
8	Retest sample submission / status	Text	System	-	Mapping table	-	-
9	Retest log	Long text	System	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-14 · PP MILESTONE


15 BCF status (Body Checking Fixture)

11 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

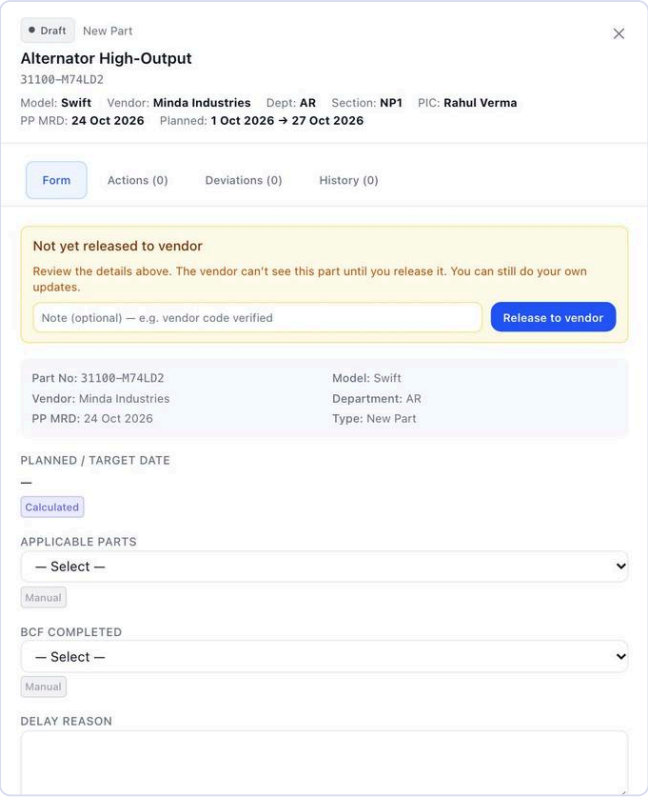

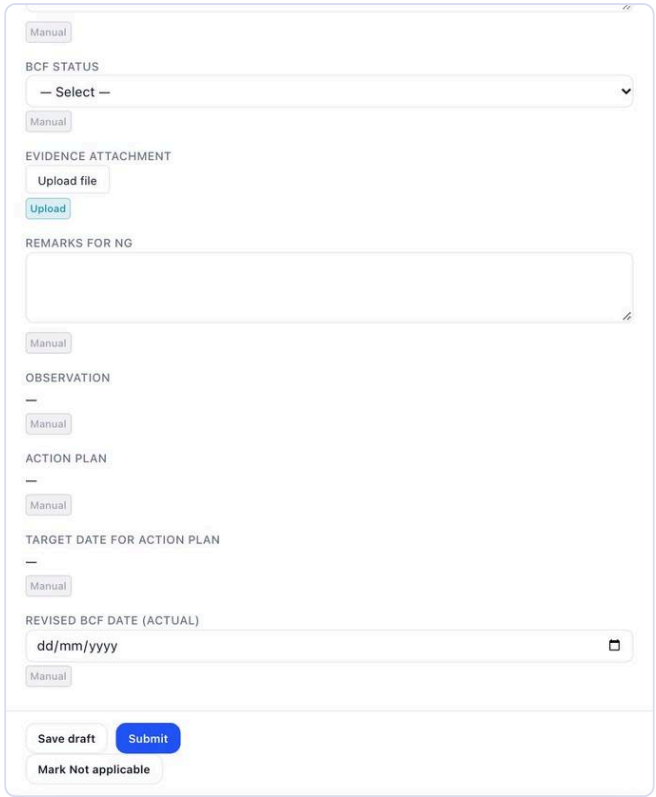

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Planned / target date	Date	System	-	Calculated	-	-
2	Applicable parts	Yes / No	PIC	-	Manual entry	-	-
3	BCF completed	Yes / No	PIC	-	Manual entry	-	-
4	Delay reason	Long text	PIC	-	Manual entry	-	-
5	BCF status	Dropdown	PIC	-	Manual entry	Dashboard, Part list	OK / NG
6	Evidence attachment	Attachment	PIC	-	Upload	-	-
7	Remarks for NG	Long text	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
8	Observation	Long text	Vendor	PIC	Manual entry	-	-
9	Action plan	Long text	Vendor	PIC	Manual entry	-	-
10	Target date for action plan	Date	Vendor	PIC	Manual entry	-	-
11	Revised BCF date (actual)	Date	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-15A · PP MILESTONE


16 Colour parts check – Testing

8 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

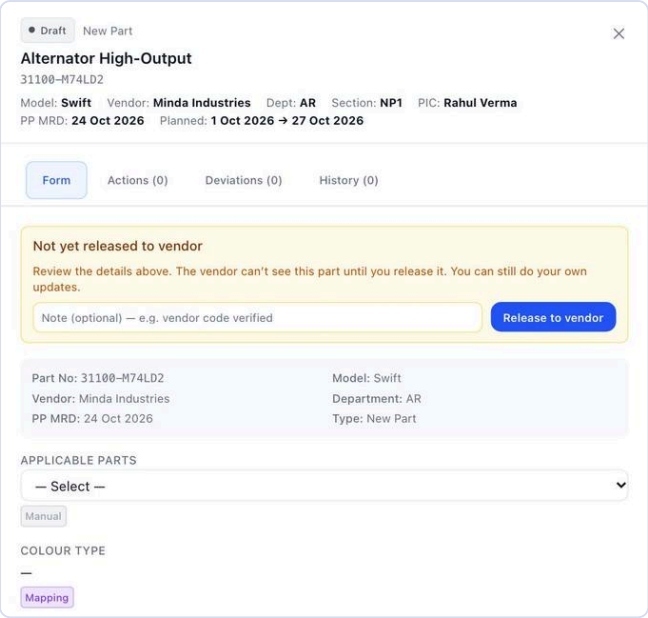

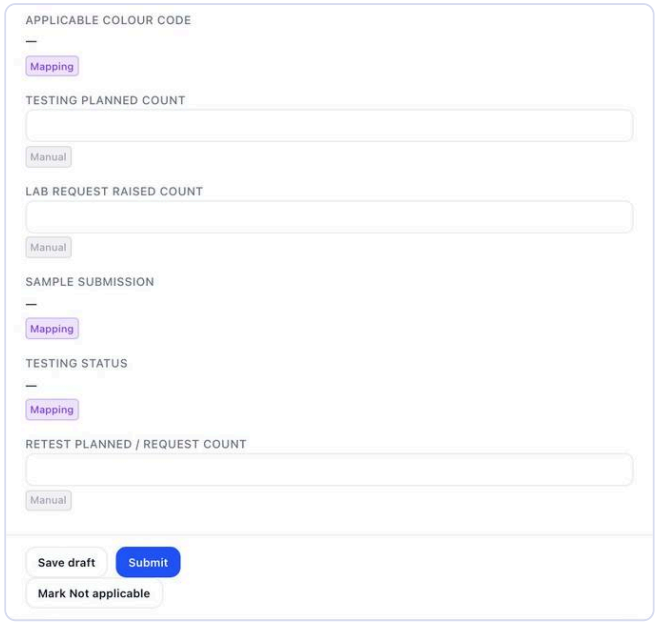

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicable parts	Yes / No	PIC	-	Manual entry	-	-
2	Colour type	Dropdown	System	-	Mapping table	-	Old / New
3	Applicable colour code	Text	System	-	Mapping table	-	-
4	Testing planned count	Number	PIC	-	Manual entry	-	-
5	Lab request raised count	Number	PIC	-	Manual entry	-	-
6	Sample submission	Dropdown	System	-	Mapping table	-	Submitted / Not submitted
7	Testing status	Dropdown	System	-	Mapping table	Dashboard	Under testing / OK / NG / Reference / Request rejected
8	Retest planned / request count	Number	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · PP-15B · PP MILESTONE


17 Colour parts check – Colour comparison

7 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

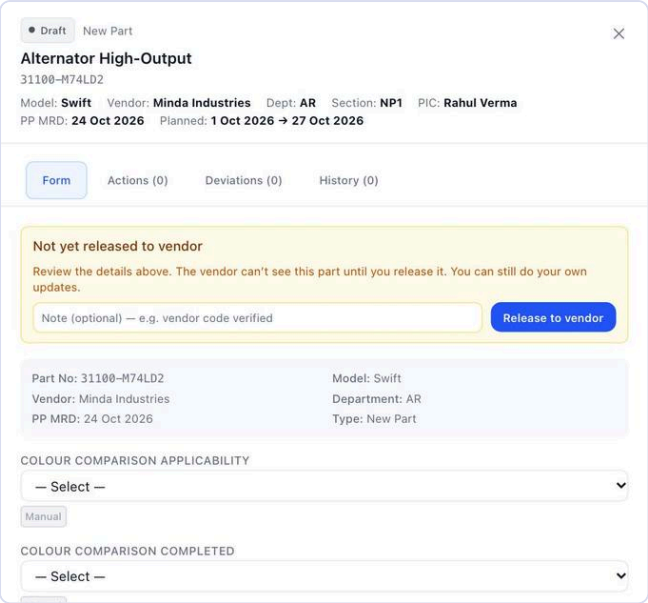

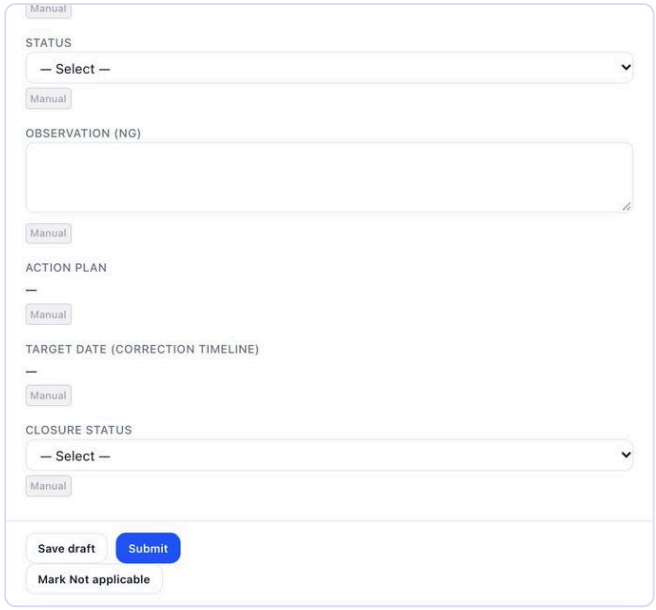

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Colour comparison applicability	Yes / No	PIC	-	Manual entry	-	-
2	Colour comparison completed	Yes / No	PIC	-	Manual entry	-	-
3	Status	Dropdown	PIC	-	Manual entry	Dashboard, Part list	OK / NG
4	Observation (NG)	Long text	PIC	-	Manual entry	-	-
5	Action plan	Long text	Vendor	PIC	Manual entry	-	-
6	Target date (correction timeline)	Date	Vendor	PIC	Manual entry	-	-
7	Closure status	Dropdown	PIC	-	Manual entry	-	Open / Closed

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PP-16 · PP MILESTONE


18 Parts list with deviations & special parts list

8 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

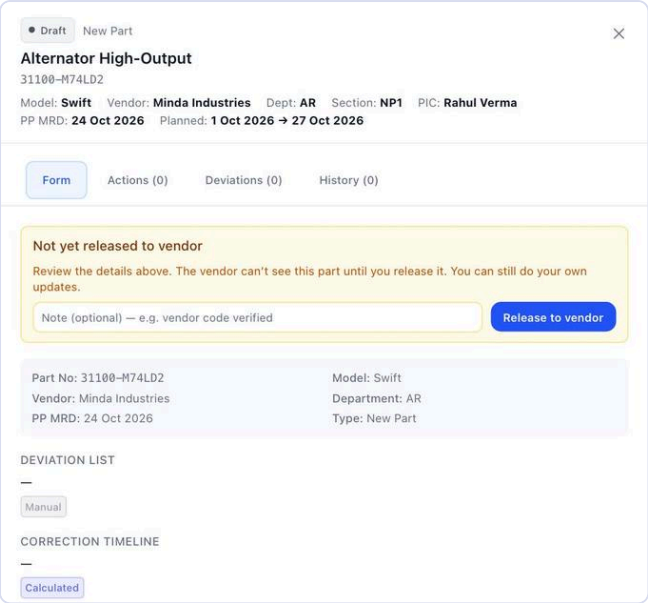

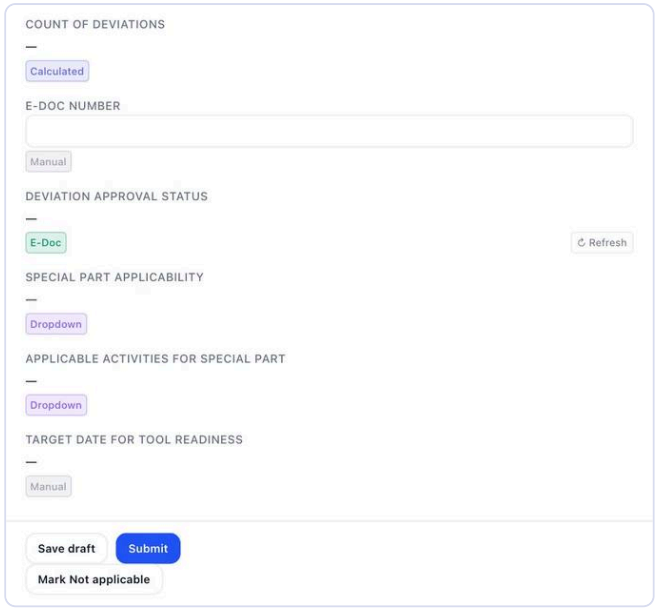

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Deviation list	Long text	System	-	Manual entry	-	-
2	Correction timeline	Date	System	-	Calculated	-	-
3	Count of deviations	Number	System	-	Calculated	Dashboard	-
4	E-Doc number	Text	PIC	-	Manual entry	-	-
5	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected
6	Special part applicability	Yes / No	Admin	-	Dropdown list	-	-
7	Applicable activities for special part	Text	Admin	-	Dropdown list	-	-
8	Target date for tool readiness	Date	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-1 · MPP MILESTONE


19 OTOP status

16 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** Yes

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

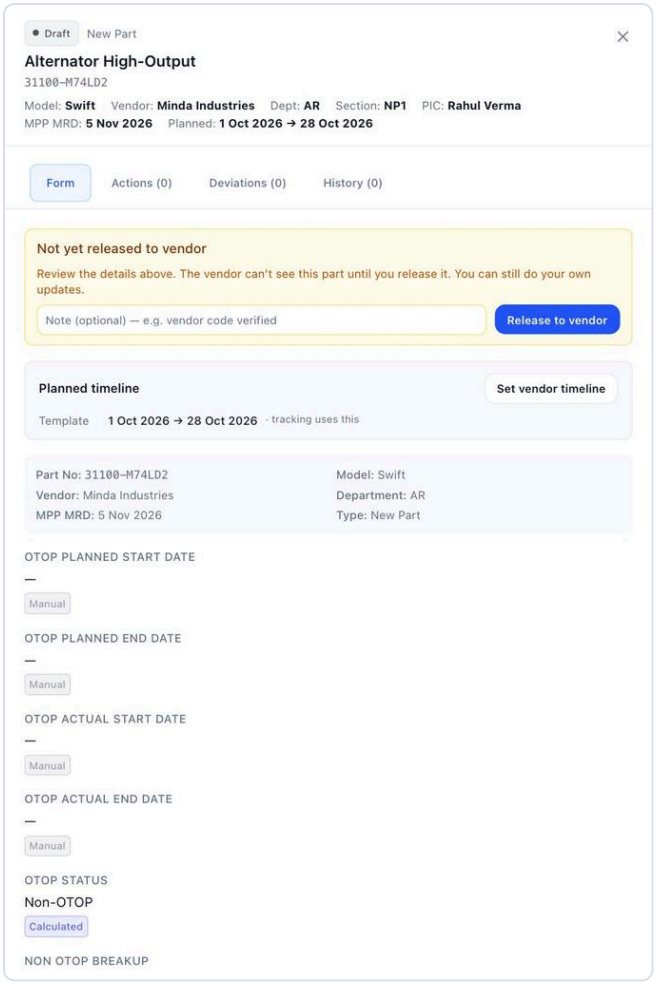

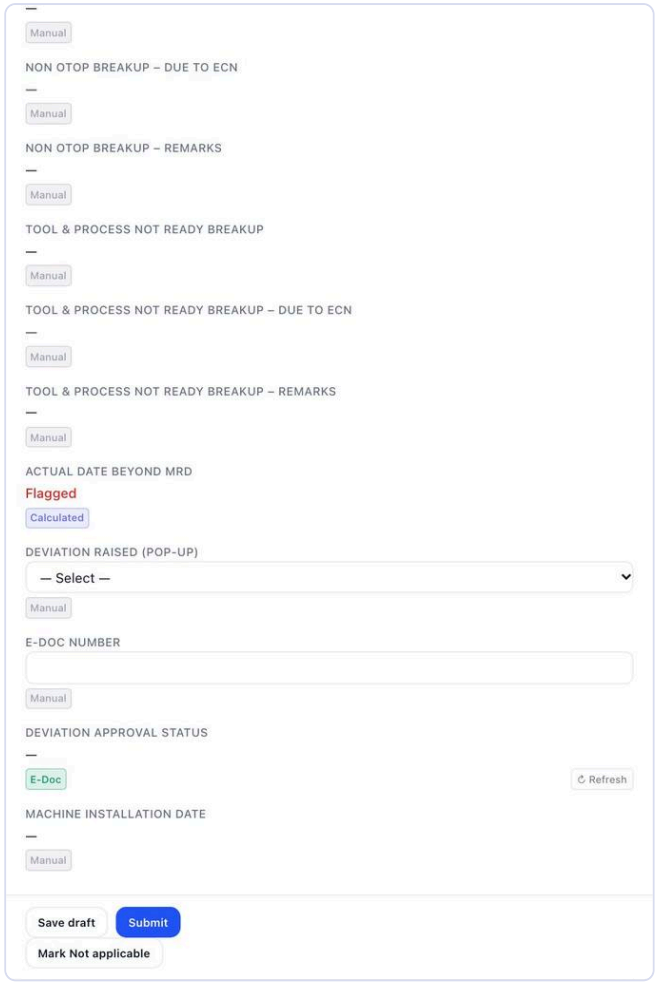

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	OTOP planned start date	Date	Vendor	PIC	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
2	OTOP planned end date	Date	Vendor	PIC	Manual entry	-	-
3	OTOP actual start date	Date	Vendor	PIC	Manual entry	-	-
4	OTOP actual end date	Date	Vendor	PIC	Manual entry	-	-
5	OTOP status	Dropdown	System	-	Calculated	Dashboard, Part list	OTOP / Non-OTOP
6	Non OTOP breakup	Dropdown	Vendor	PIC	Manual entry	-	Tool Not Ready / Process Not Ready / Tool & Process Not Ready
7	Non OTOP breakup – Due to ECN	Yes / No	Vendor	PIC	Manual entry	-	-
8	Non OTOP breakup – Remarks	Long text	Vendor	PIC	Manual entry	-	-
9	Tool & process not ready breakup	Dropdown	Vendor	PIC	Manual entry	-	Process Maturation Delay / Software Readiness / Machine/Facility Delay / Source Selection Delay
10	Tool & process not ready breakup – Due to ECN	Yes / No	Vendor	PIC	Manual entry	-	-
11	Tool & process not ready breakup – Remarks	Long text	Vendor	PIC	Manual entry	-	-
12	Actual date beyond MRD	Flag	System	-	Calculated	-	-
13	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
14	E-Doc number	Number	PIC	-	Manual entry	-	-
15	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected
16	Machine installation date	Date	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-5 · MPP MILESTONE


20 PP Hinkai trial closure status – QAND & Production

11 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

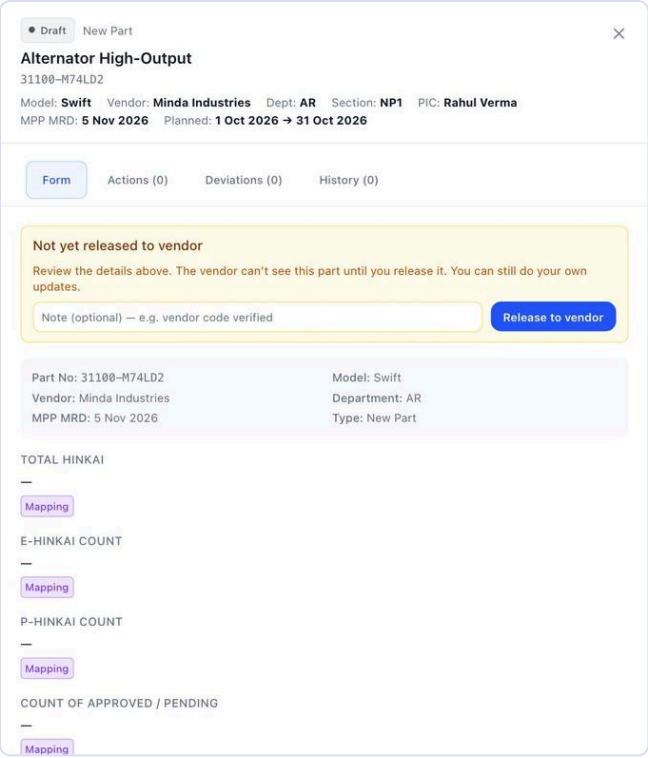

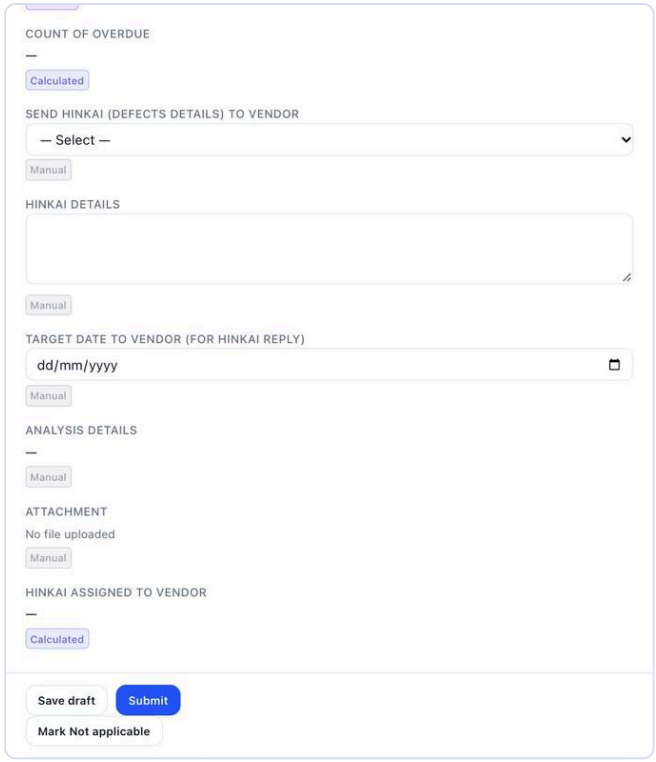

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Total Hinkai	Number	System	-	Mapping table	Dashboard	-
2	E-Hinkai count	Number	System	-	Mapping table	-	-
3	P-Hinkai count	Number	System	-	Mapping table	-	-
4	Count of approved / pending	Number	System	-	Mapping table	-	-
5	Count of overdue	Number	System	-	Calculated	-	-
6	Send Hinkai (defects details) to vendor	Yes / No	PIC	-	Manual entry	-	-
7	Hinkai details	Long text	PIC	-	Manual entry	-	-
8	Target date to vendor (for Hinkai reply)	Date	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
9	Analysis details	Long text	Vendor	PIC	Manual entry	-	-
10	Attachment	Attachment	Vendor	PIC	Manual entry	-	-
11	Hinkai assigned to vendor	Dropdown	System	-	Calculated	-	Replied by vendor / Pending for reply by vendor

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-6 · MPP MILESTONE


21 SOR adherence confirmation (Div Head deviation via E-Doc)

10 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

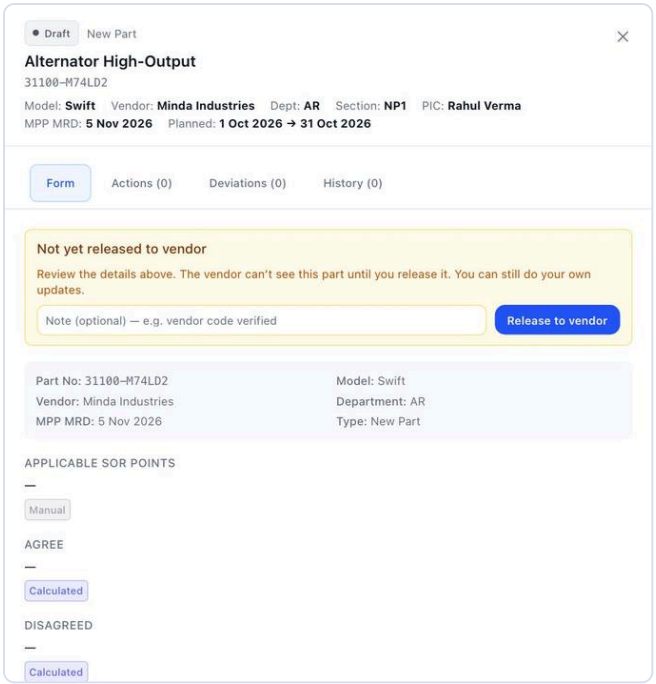

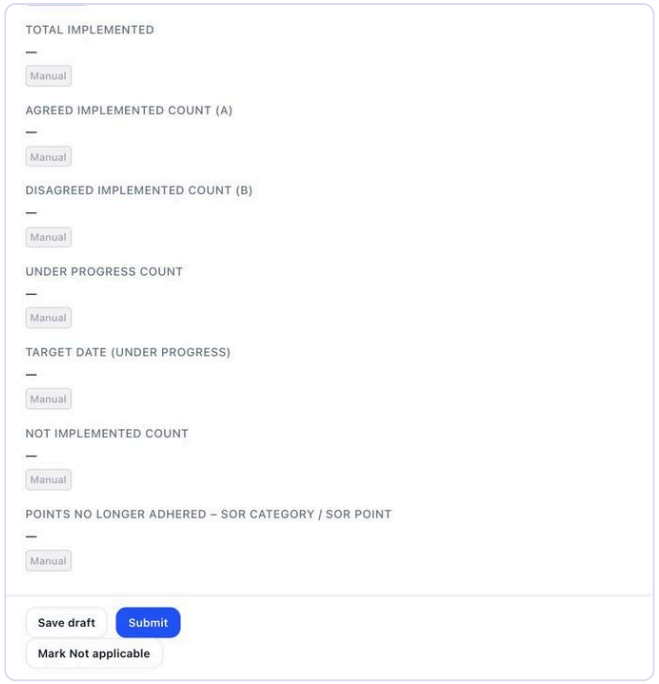

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicable SOR points	Text	System	-	Manual entry	-	-
2	Agree	Number	System	-	Calculated	-	-
3	Disagreed	Number	System	-	Calculated	-	-
4	Total implemented	Number	Vendor	PIC	Manual entry	Dashboard	-
5	Agreed implemented count (A)	Number	Vendor	PIC	Manual entry	-	-
6	Disagreed implemented count (B)	Number	Vendor	PIC	Manual entry	-	-
7	Under progress count	Number	Vendor	PIC	Manual entry	-	-
8	Target date (under progress)	Date	Vendor	PIC	Manual entry	-	-
9	Not implemented count	Number	Vendor	PIC	Manual entry	-	-
10	Points no longer adhered – SOR category / SOR point	Text	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

22


ACTIVITY · MPP-7 · MPP MILESTONE


Lab testing status

12 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

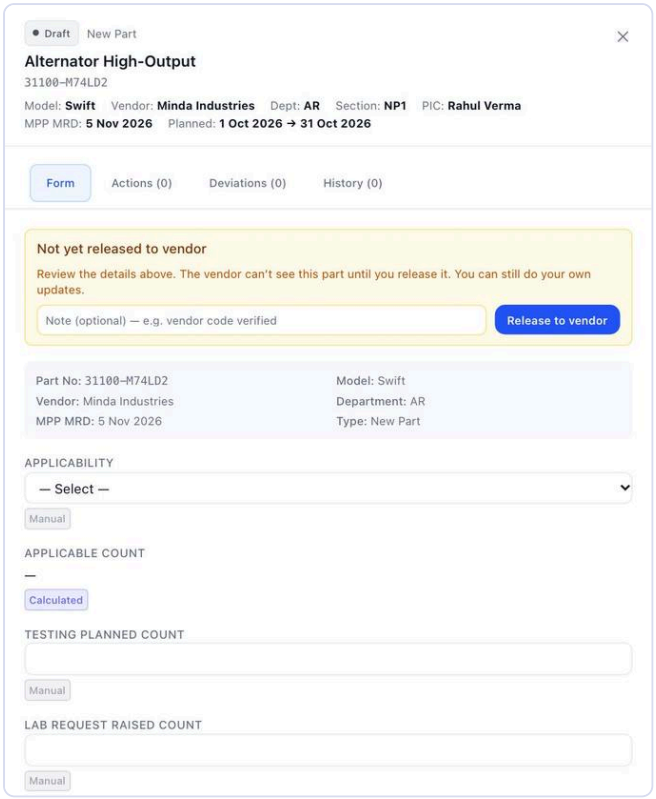

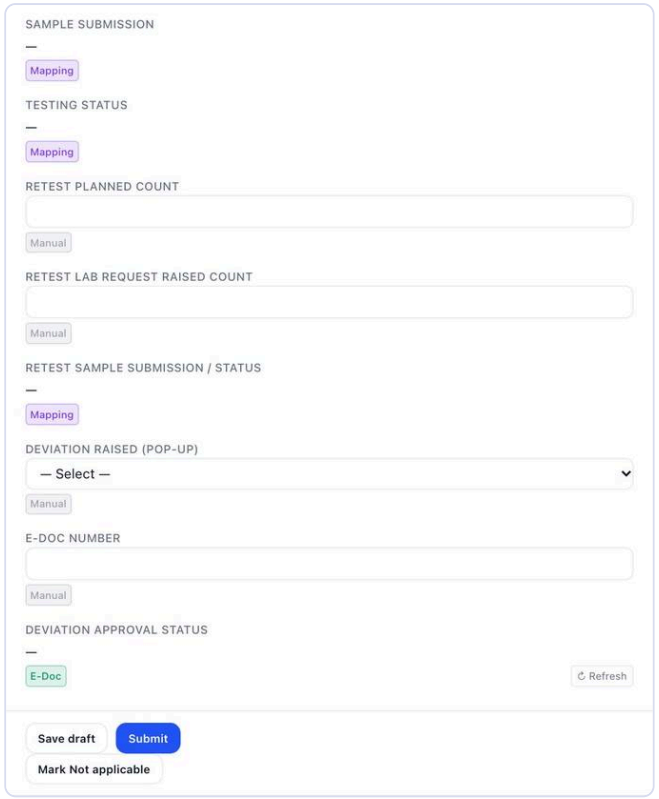

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Applicable count	Number	System	-	Calculated	-	-
3	Testing planned count	Number	PIC	-	Manual entry	-	-
4	Lab request raised count	Number	PIC	-	Manual entry	-	-
5	Sample submission	Dropdown	System	-	Mapping table	-	Submitted / Not submitted
6	Testing status	Dropdown	System	-	Mapping table	Dashboard, Part list	Under testing / OK / NG / Reference / Request rejected
7	Retest planned count	Number	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
8	Retest lab request raised count	Number	PIC	-	Manual entry	-	-
9	Retest sample submission / status	Text	System	-	Mapping table	-	-
10	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
11	E-Doc number	Text	PIC	-	Manual entry	-	-
12	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

23


ACTIVITY · MPP-8 · MPP MILESTONE


Process audit status

9 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

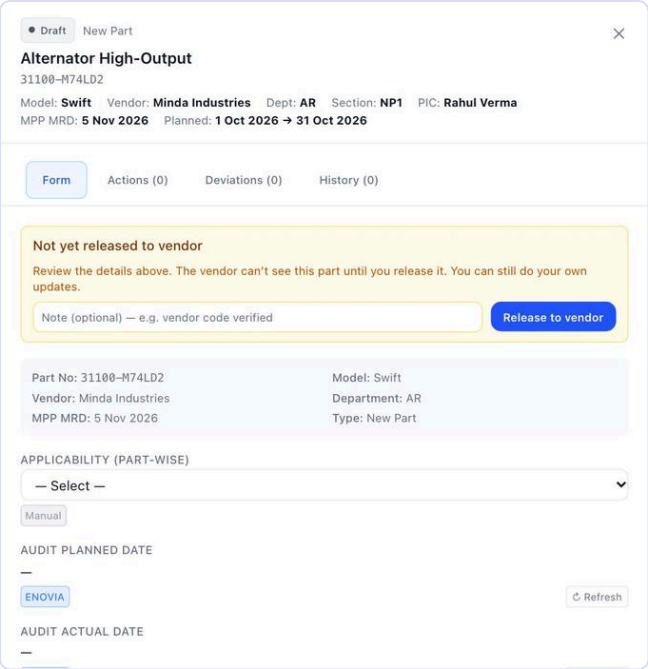

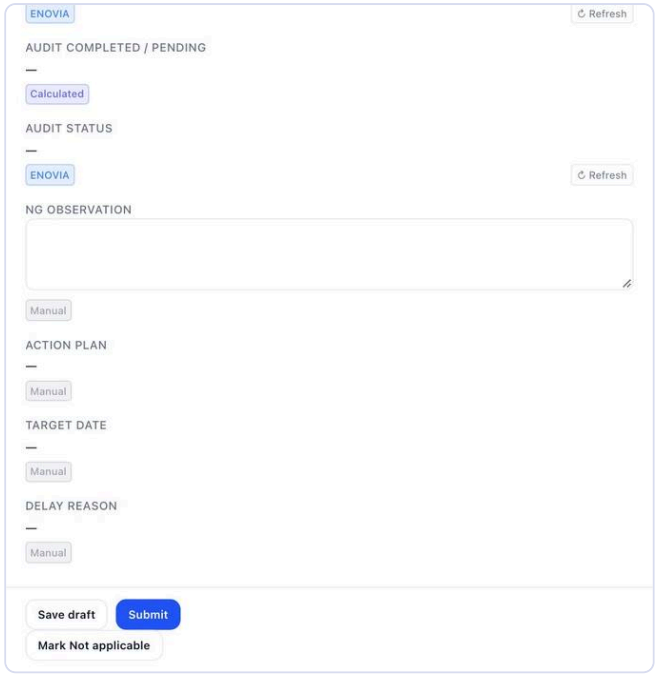

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability (part-wise)	Yes / No	PIC	-	Manual entry	-	-
2	Audit planned date	Date	System	-	ENOVIA	-	-
3	Audit actual date	Date	System	-	ENOVIA	-	-
4	Audit completed / pending	Dropdown	System	-	Calculated	-	Completed / Pending
5	Audit status	Dropdown	System	-	ENOVIA	Dashboard, Part list	OK / NG
6	NG observation	Long text	PIC	-	Manual entry	-	-
7	Action plan	Long text	Vendor	PIC	Manual entry	-	-
8	Target date	Date	Vendor	PIC	Manual entry	-	-
9	Delay reason	Long text	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · MPP-9 · MPP MILESTONE


24 Process capability (critical parameters)

8 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

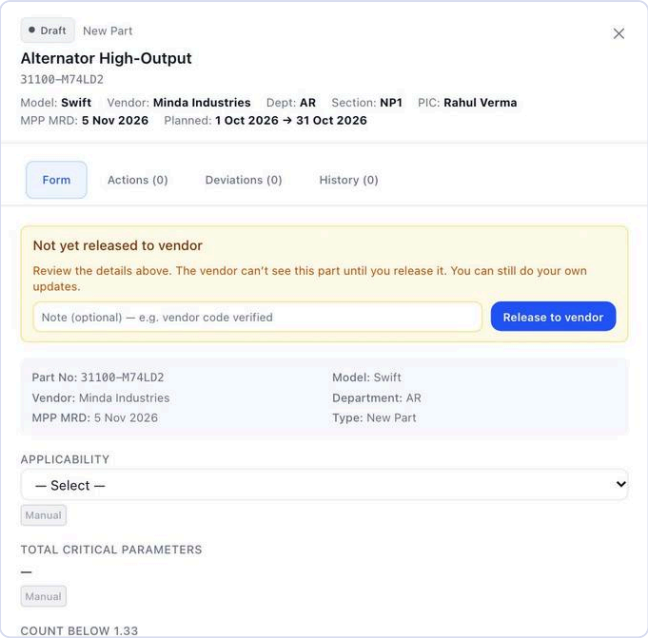

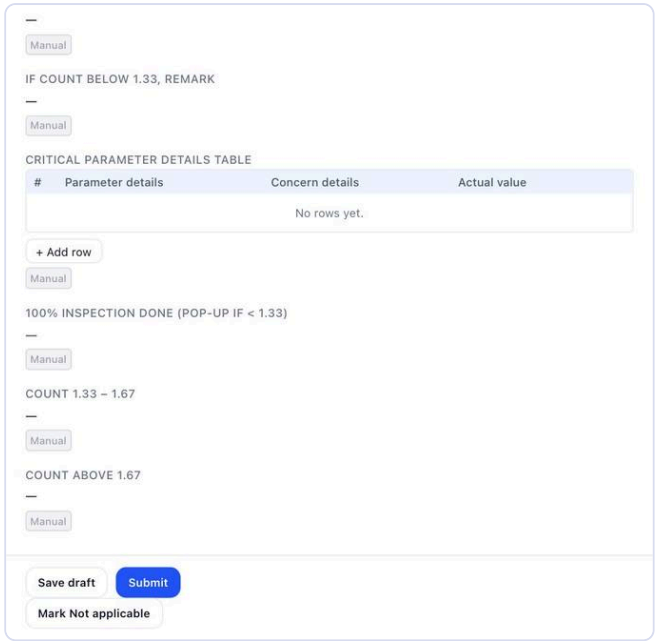

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Total critical parameters	Number	Vendor	PIC	Manual entry	-	-
3	Count below 1.33	Number	Vendor	PIC	Manual entry	Dashboard	-
4	If count below 1.33, remark	Long text	Vendor	PIC	Manual entry	-	-
5	Critical parameter details table	Table	PIC	-	Manual entry	-	Columns: Parameter details, Concern details, Actual value
6	100% inspection done (pop-up if < 1.33)	Yes / No	Vendor	PIC	Manual entry	-	-
7	Count 1.33 – 1.67	Number	Vendor	PIC	Manual entry	-	-
8	Count above 1.67	Number	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-10 · MPP MILESTONE


25 Homologation marking confirmation

10 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

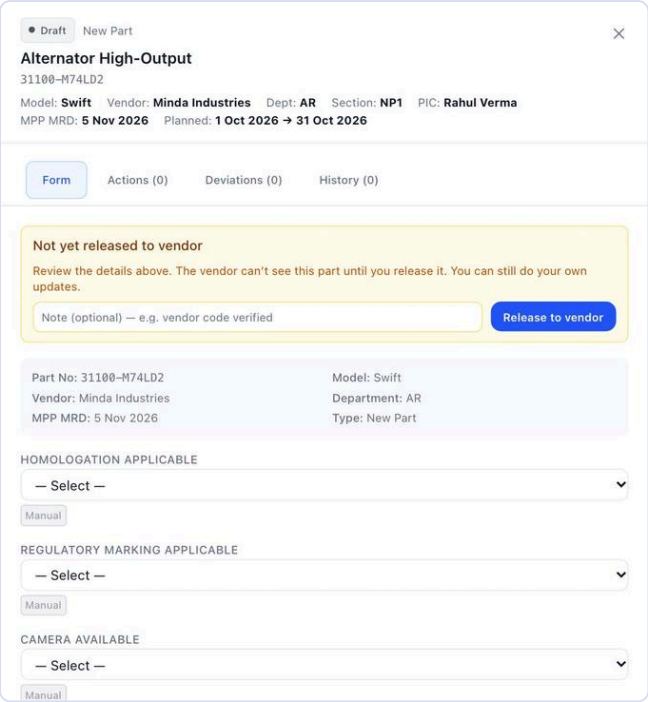

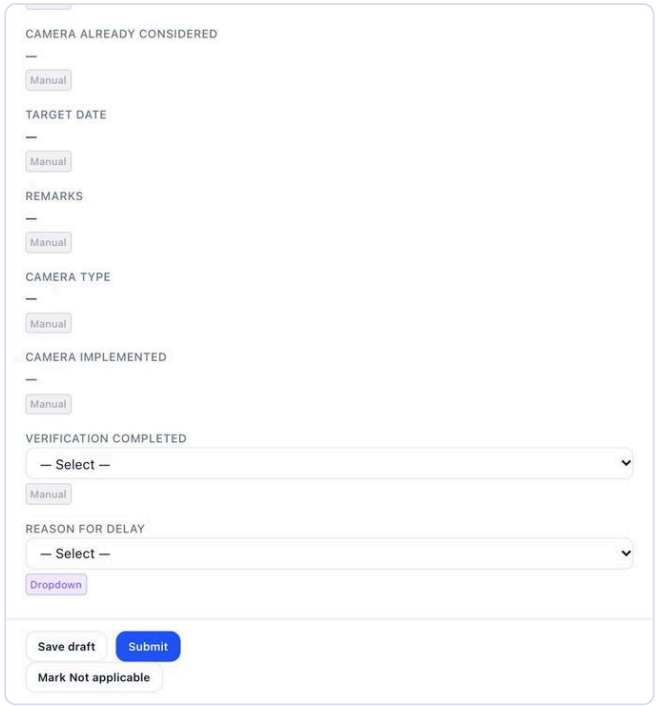

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Homologation applicable	Yes / No	PIC	-	Manual entry	-	-
2	Regulatory marking applicable	Yes / No	PIC	-	Manual entry	-	-
3	Camera available	Yes / No	PIC	-	Manual entry	-	-
4	Camera already considered	Yes / No	Vendor	PIC	Manual entry	-	-
5	Target date	Date	Vendor	PIC	Manual entry	-	-
6	Remarks	Long text	Vendor	PIC	Manual entry	-	-
7	Camera type	Dropdown	Vendor	PIC	Manual entry	-	OCR / Image
8	Camera implemented	Yes / No	Vendor	PIC	Manual entry	-	-
9	Verification completed	Yes / No	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
10	Reason for delay	Dropdown	PIC	-	Dropdown list	-	SC approval pending / SC approved, vendor implementation pending / All approvals in, delay by vendor

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-11 · MPP MILESTONE

26 Set part / semi-finished part status

4 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

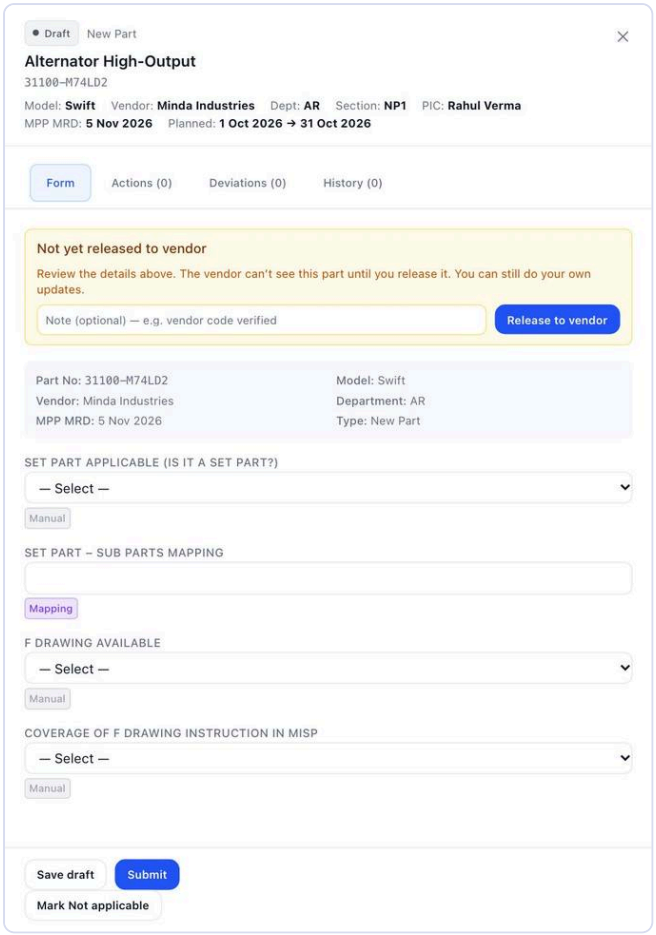

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Set part applicable (is it a set part?)	Yes / No	PIC	-	Manual entry	-	-
2	Set part – Sub parts mapping	Text	PIC	-	Mapping table	-	-
3	F drawing available	Yes / No	PIC	-	Manual entry	-	-
4	Coverage of F drawing instruction in MISP	Yes / No	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

27


ACTIVITY · MPP-12 · MPP MILESTONE

MISP revision status

3 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

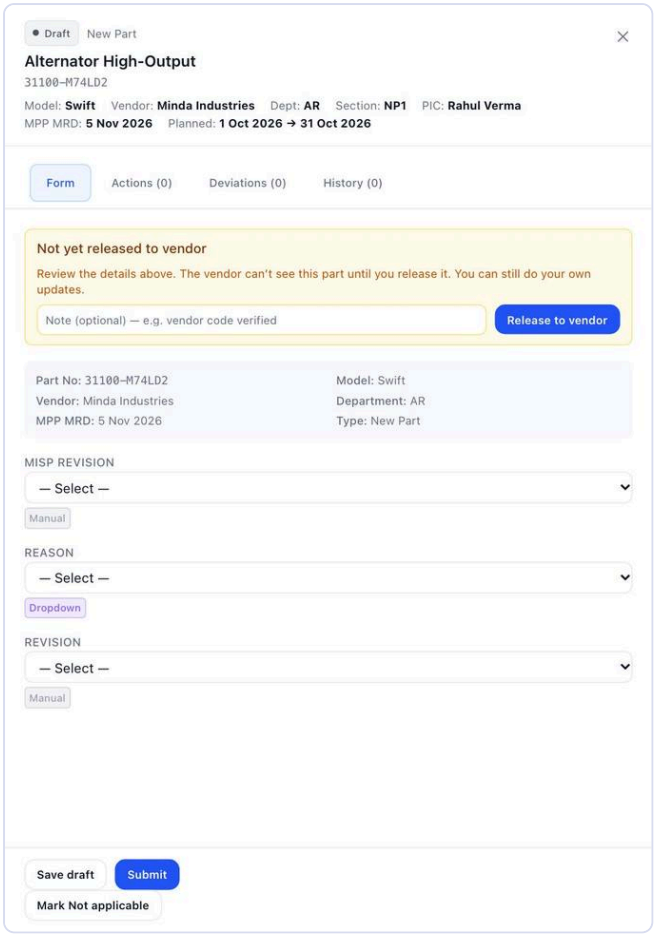

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	MISP revision	Dropdown	PIC	-	Manual entry	Dashboard, Part list	Required / Not required
2	Reason	Dropdown	PIC	-	Dropdown list	-	ECN / Learning / Both / Others
3	Revision	Dropdown	PIC	-	Manual entry	-	Done / Not done

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

28


ACTIVITY · MPP-13 · MPP MILESTONE


Spare kit part status

11 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

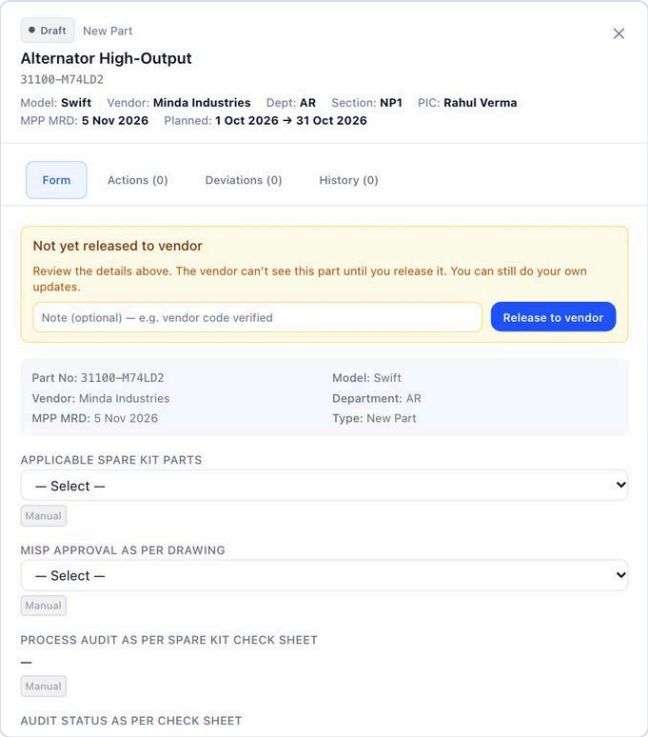

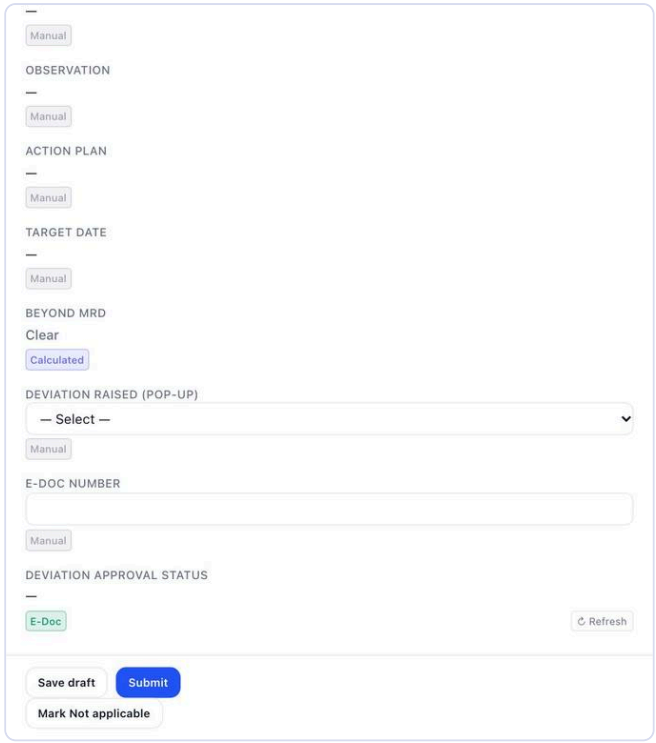

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicable spare kit parts	Yes / No	PIC	-	Manual entry	-	-
2	MISP approval as per drawing	Dropdown	PIC	-	Manual entry	-	Done / Pending
3	Process audit as per spare kit check sheet	Dropdown	Vendor	PIC	Manual entry	-	Done / Pending
4	Audit status as per check sheet	Dropdown	Vendor	PIC	Manual entry	Dashboard	OK / NG
5	Observation	Long text	Vendor	PIC	Manual entry	-	-
6	Action plan	Long text	Vendor	PIC	Manual entry	-	-
7	Target date	Date	Vendor	PIC	Manual entry	-	-
8	Beyond MRD	Flag	System	-	Calculated	-	-
9	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
10	E-Doc number	Text	PIC	-	Manual entry	-	-
11	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · MPP-14 · MPP MILESTONE


29 Parts list with deviations & special parts list

8 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

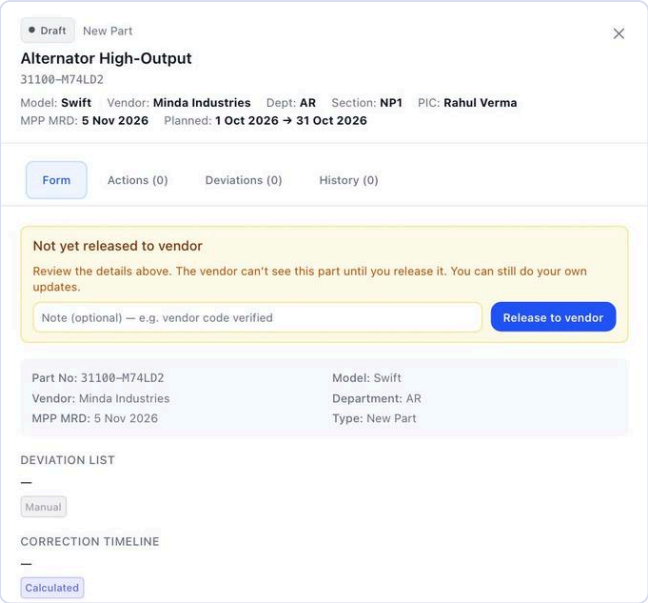

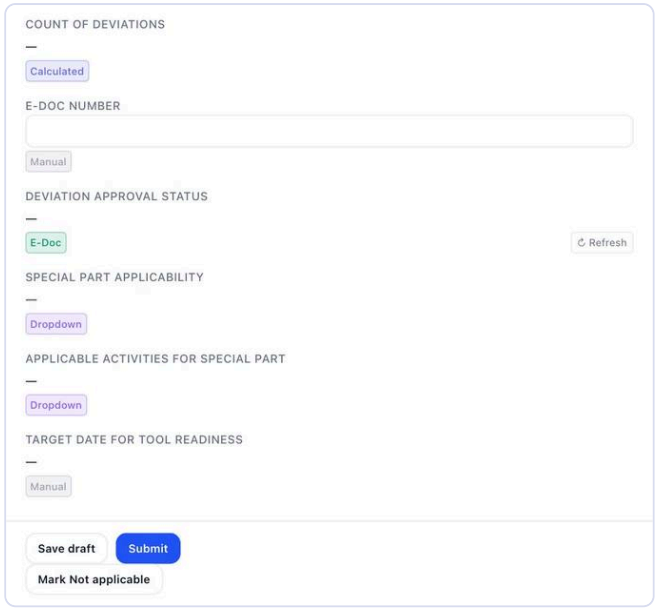

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Deviation list	Long text	System	-	Manual entry	-	-
2	Correction timeline	Date	System	-	Calculated	-	-
3	Count of deviations	Number	System	-	Calculated	Dashboard	-
4	E-Doc number	Text	PIC	-	Manual entry	-	-
5	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected
6	Special part applicability	Yes / No	Admin	-	Dropdown list	-	-
7	Applicable activities for special part	Text	Admin	-	Dropdown list	-	-
8	Target date for tool readiness	Date	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-1 · SOP MILESTONE


30 OTOP status (ECN cases)

10 fields

Owner: PIC **Scope:** ECN **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** Yes

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

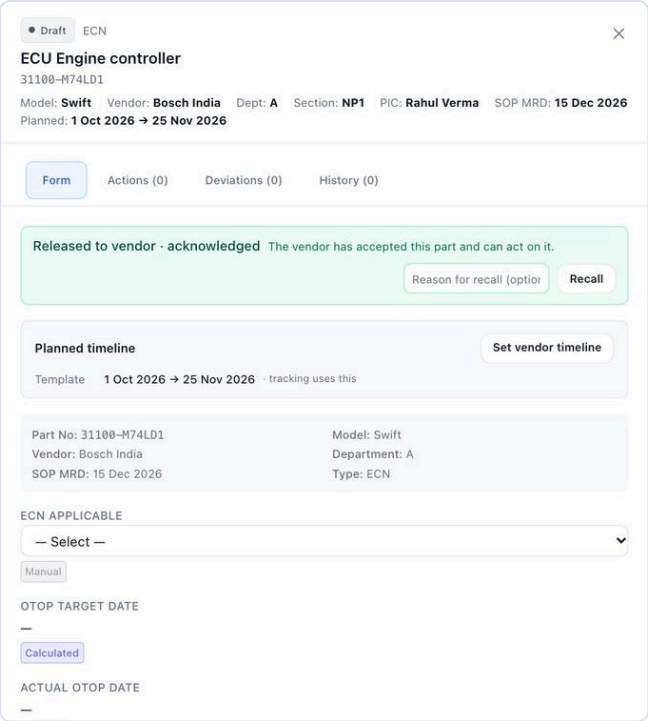

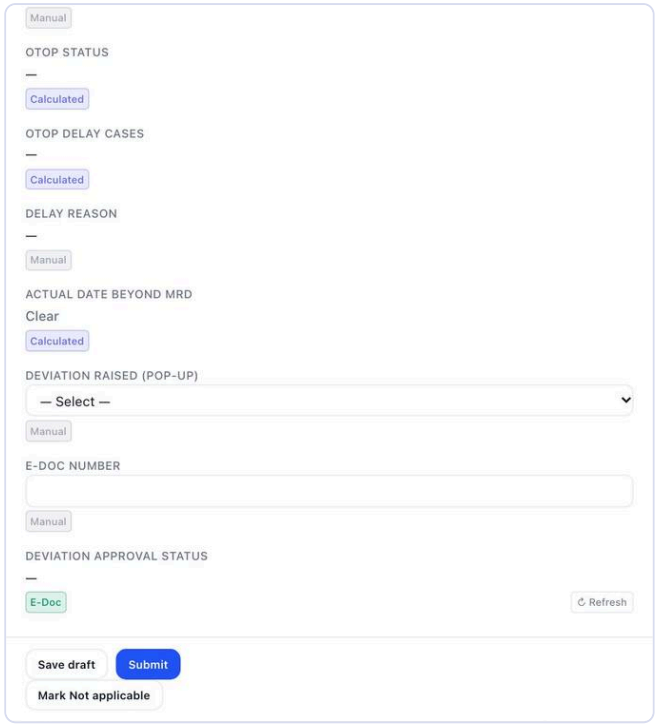

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	ECN applicable	Yes / No	PIC	-	Manual entry	-	-
2	OTOP target date	Date	System	-	Calculated	-	-
3	Actual OTOP date	Date	Vendor	PIC	Manual entry	-	-
4	OTOP status	Dropdown	System	-	Calculated	Dashboard, Part list	OTOP / Non-OTOP
5	OTOP delay cases	Number	System	-	Calculated	-	-
6	Delay reason	Long text	Vendor	PIC	Manual entry	-	-
7	Actual date beyond MRD	Flag	System	-	Calculated	-	-
8	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
9	E-Doc number	Text	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
10	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-2 · SOP MILESTONE


31 Sheet metal part accuracy status

12 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

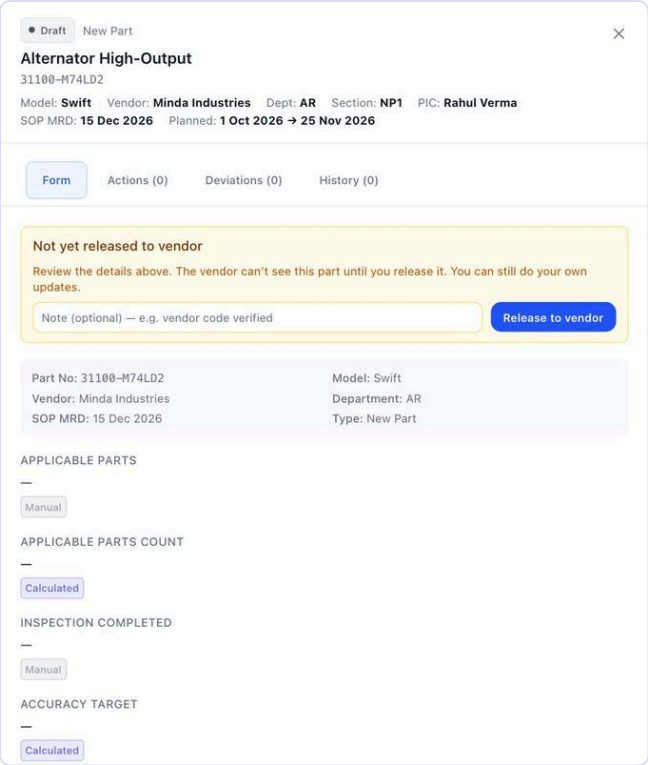

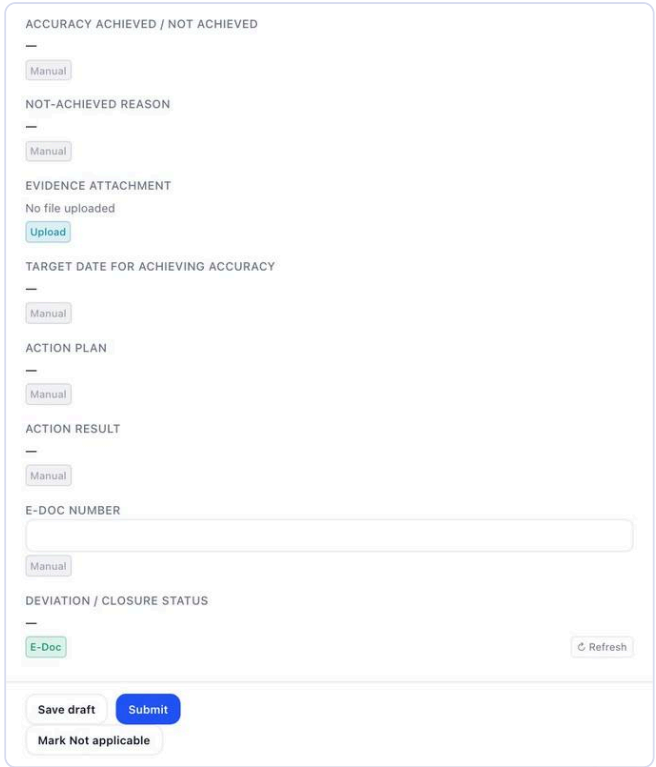

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicable parts	Yes / No	Vendor	PIC	Manual entry	-	-
2	Applicable parts count	Number	System	-	Calculated	-	-
3	Inspection completed	Yes / No	Vendor	PIC	Manual entry	-	-
4	Accuracy target	Percent	System	-	Calculated	-	-
5	Accuracy achieved / not achieved	Percent	Vendor	PIC	Manual entry	Dashboard	-
6	Not-achieved reason	Long text	Vendor	PIC	Manual entry	-	-
7	Evidence attachment	Attachment	Vendor	PIC	Upload	-	-
8	Target date for achieving accuracy	Date	Vendor	PIC	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
9	Action plan	Long text	Vendor	PIC	Manual entry	-	-
10	Action result	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Deviation
11	E-Doc number	Text	PIC	-	Manual entry	-	-
12	Deviation / closure status	Dropdown	System	-	E-Doc	-	Accept / Pending / Reject / Open / Closed

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-3 · SOP MILESTONE


32 Part inspection with deviation status (ECN cases)

15 fields

Owner: PIC **Scope:** ECN **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

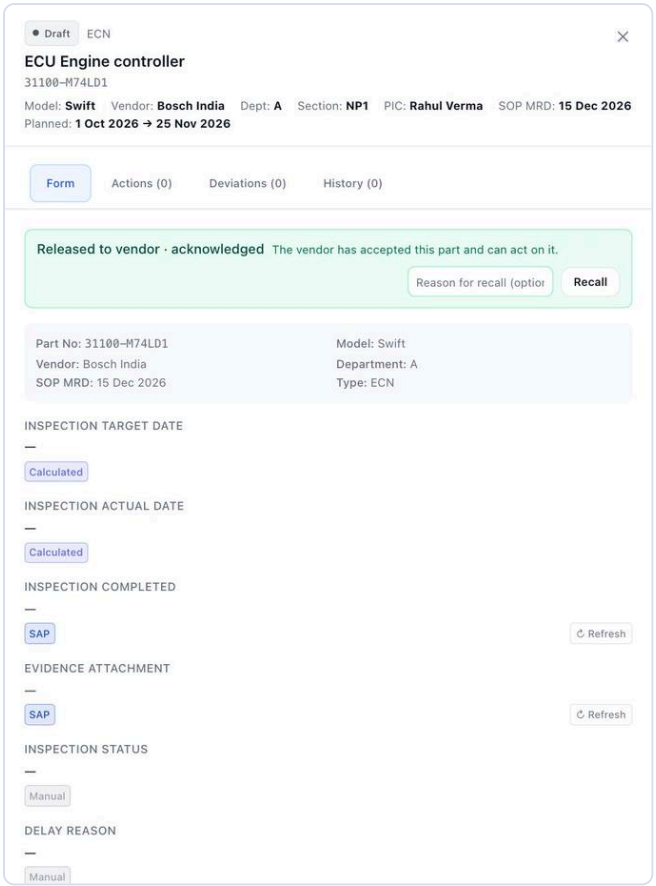

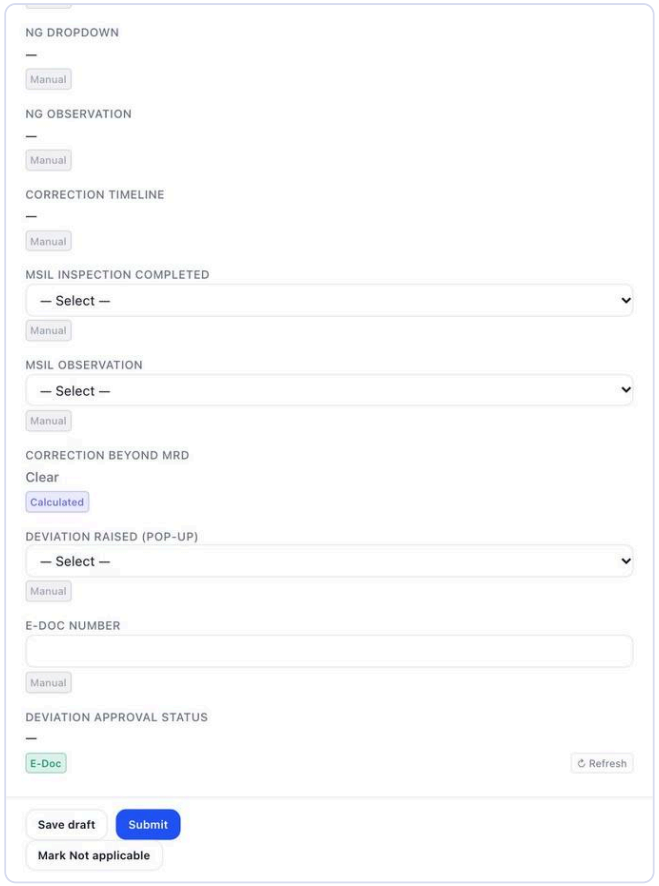

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Inspection target date	Date	System	-	Calculated	-	-
2	Inspection actual date	Date	System	-	Calculated	-	-
3	Inspection completed	Yes / No	System	-	SAP	-	-
4	Evidence attachment	Yes / No	System	-	SAP	-	-
5	Inspection status	Dropdown	Vendor	PIC	Manual entry	Dashboard, Part list	OK / NG

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
6	Delay reason	Long text	Vendor	PIC	Manual entry	-	-
7	NG dropdown	Multi-select	Vendor	PIC	Manual entry	-	Appearance / Dimension / Material / Performance / Regulation
8	NG observation	Long text	Vendor	PIC	Manual entry	-	-
9	Correction timeline	Date	Vendor	PIC	Manual entry	-	-
10	MSIL inspection completed	Yes / No	PIC	-	Manual entry	-	-
11	MSIL observation	Dropdown	PIC	-	Manual entry	-	OK / NG
12	Correction beyond MRD	Flag	System	-	Calculated	-	-
13	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
14	E-Doc number	Text	PIC	-	Manual entry	-	-
15	Deviation approval status	Dropdown	System	-	E-Doc	-	Approved / Pending / Rejected / In progress

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-17 · SOP MILESTONE

33 MISP revision status

3 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

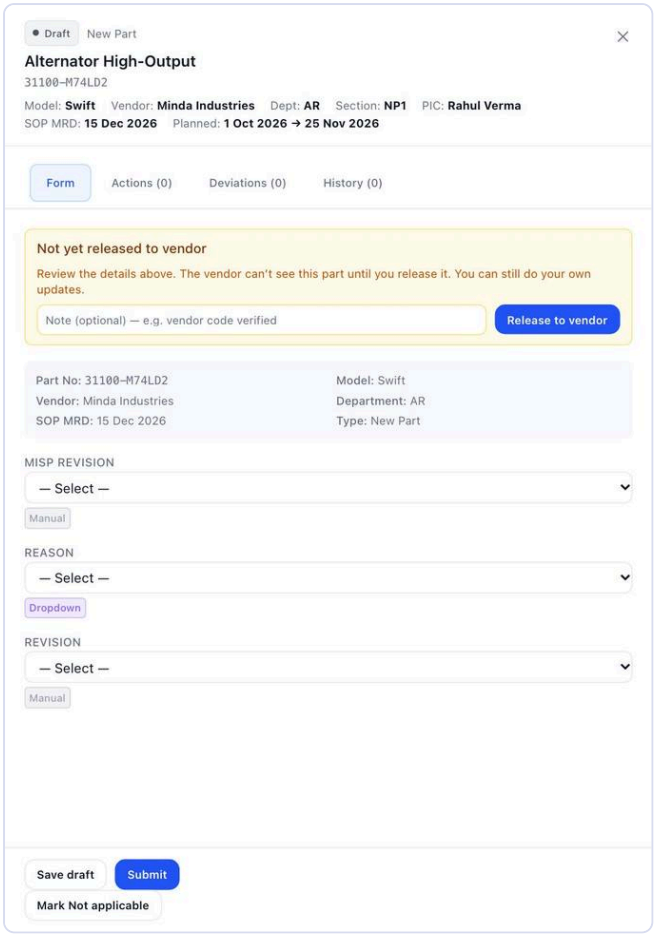

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	MISP revision	Dropdown	PIC	-	Manual entry	-	Required / Not required
2	Reason	Dropdown	PIC	-	Dropdown list	-	ECN / Learning / Both
3	Revision	Dropdown	PIC	-	Manual entry	-	Done / Not done

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-4 · SOP MILESTONE


34 MPP Hinkai trial closure status – QAND & Production

6 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

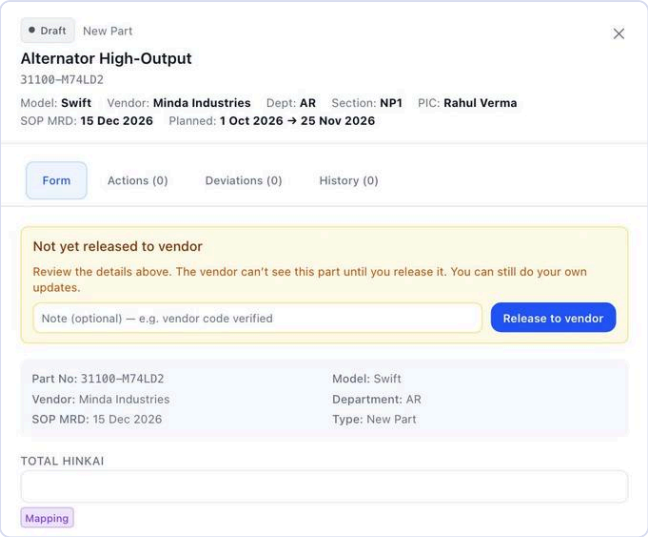

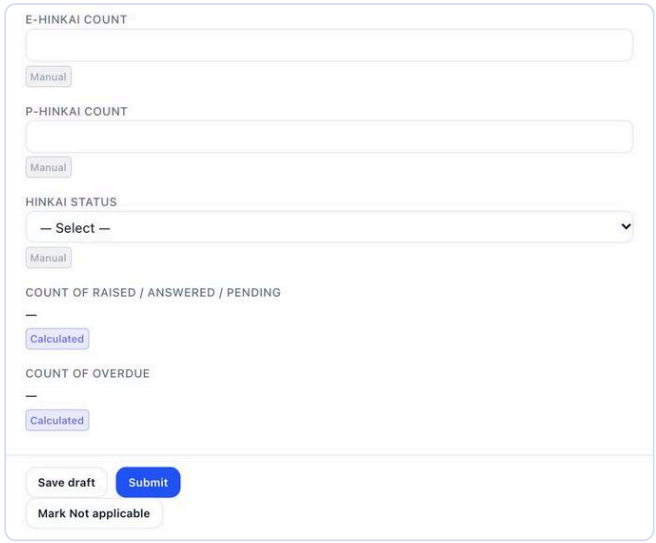

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Total Hinkai	Number	PIC	-	Mapping table	Dashboard	-
2	E-Hinkai count	Number	PIC	-	Manual entry	-	-
3	P-Hinkai count	Number	PIC	-	Manual entry	-	-
4	Hinkai status	Dropdown	PIC	-	Manual entry	Part list	Raised / Answered / Pending
5	Count of raised / answered / pending	Number	System	-	Calculated	-	-
6	Count of overdue	Number	System	-	Calculated	-	-

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · PILOT-5 · SOP MILESTONE


35 BCF status (Body Checking Fixture)

11 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

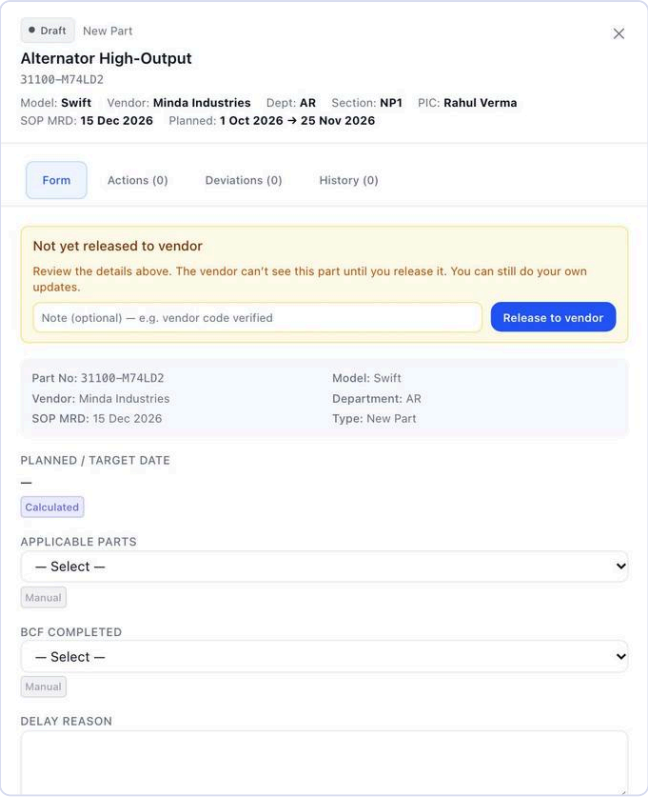

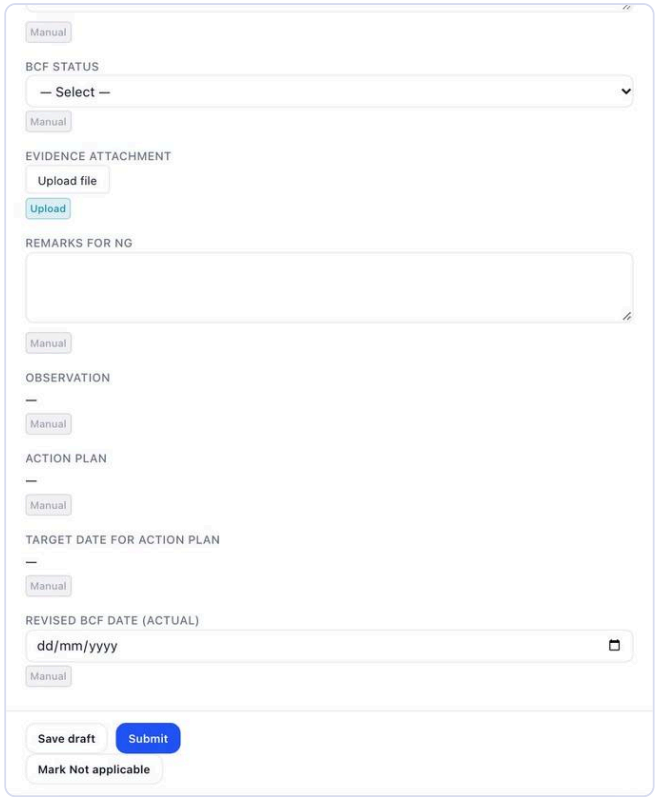

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Planned / target date	Date	System	-	Calculated	-	-
2	Applicable parts	Yes / No	PIC	-	Manual entry	-	-
3	BCF completed	Yes / No	PIC	-	Manual entry	-	-
4	Delay reason	Long text	PIC	-	Manual entry	-	-
5	BCF status	Dropdown	PIC	-	Manual entry	Dashboard, Part list	OK / NG
6	Evidence attachment	Attachment	PIC	-	Upload	-	-
7	Remarks for NG	Long text	PIC	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
8	Observation	Long text	Vendor	PIC	Manual entry	-	-
9	Action plan	Long text	Vendor	PIC	Manual entry	-	-
10	Target date for action plan	Date	Vendor	PIC	Manual entry	-	-
11	Revised BCF date (actual)	Date	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-7 · SOP MILESTONE

36 PPAP file approval status

4 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

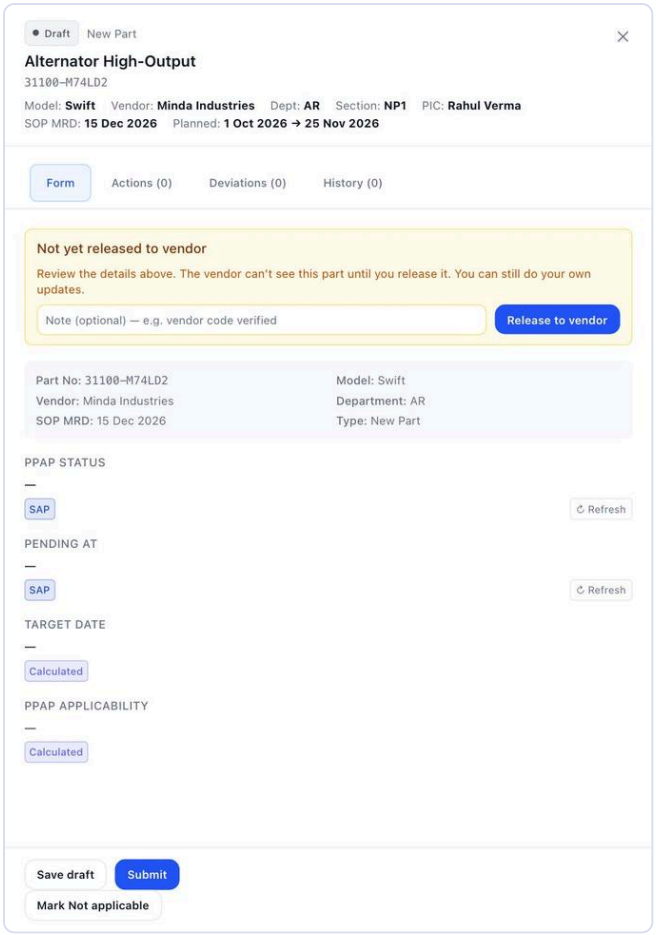

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	PPAP status	Dropdown	System	-	SAP	Dashboard, Part list	Approved / Pending
2	Pending at	Dropdown	System	-	SAP	-	PIC / SIC / DPM / DDVM / DVM / DVM-SMC
3	Target date	Date	System	-	Calculated	-	-
4	PPAP applicability	Yes / No	System	-	Calculated	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

37


ACTIVITY · PILOT-8 · SOP MILESTONE


Lab testing status

9 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

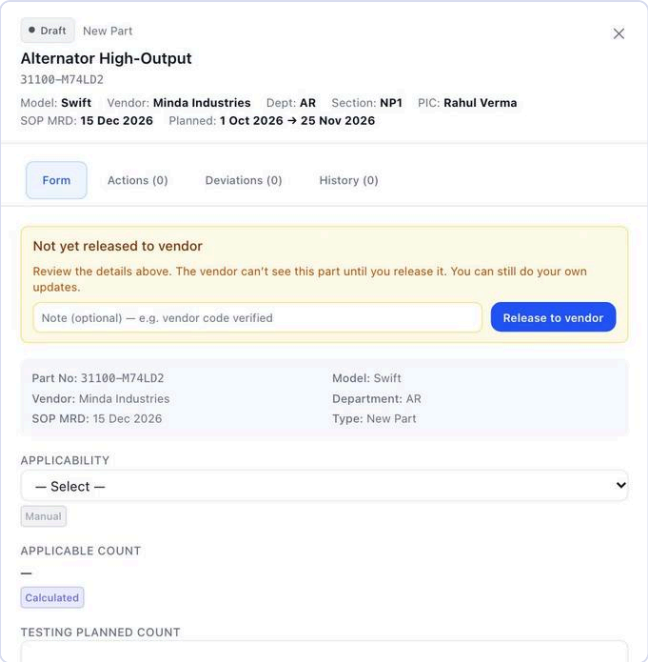

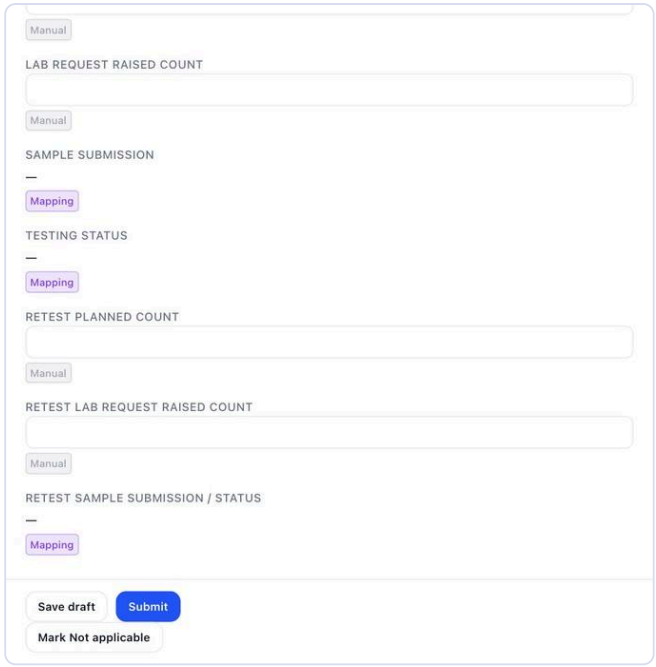

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Applicable count	Number	System	-	Calculated	-	-
3	Testing planned count	Number	PIC	-	Manual entry	-	-
4	Lab request raised count	Number	PIC	-	Manual entry	-	-
5	Sample submission	Dropdown	System	-	Mapping table	-	Submitted / Not submitted
6	Testing status	Dropdown	System	-	Mapping table	Dashboard, Part list	Under testing / OK / NG / Reference / Request rejected
7	Retest planned count	Number	PIC	-	Manual entry	-	-
8	Retest lab request raised count	Number	PIC	-	Manual entry	-	-
9	Retest sample submission / status	Text	System	-	Mapping table	-	-

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · PILOT-9 · SOP MILESTONE


38 Homologation marking confirmation (camera inspection)

12 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

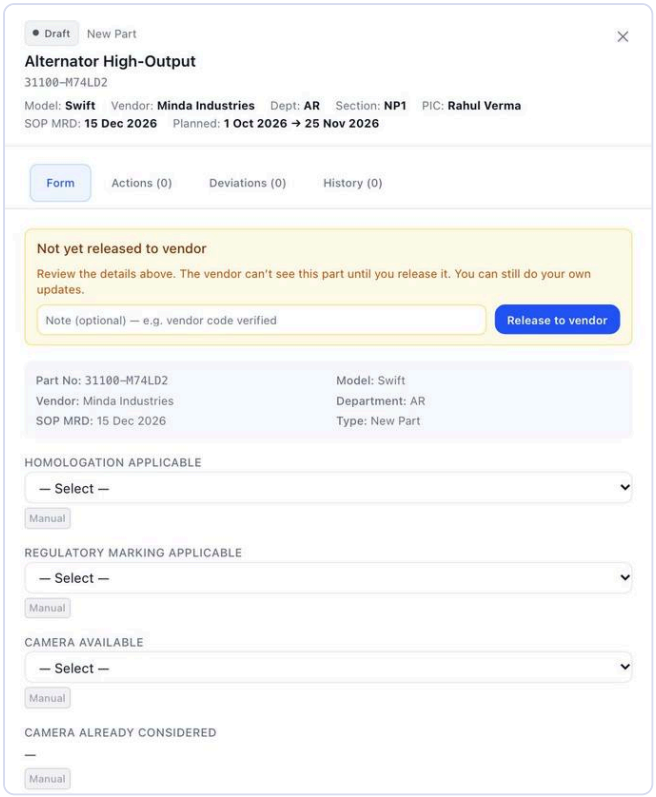

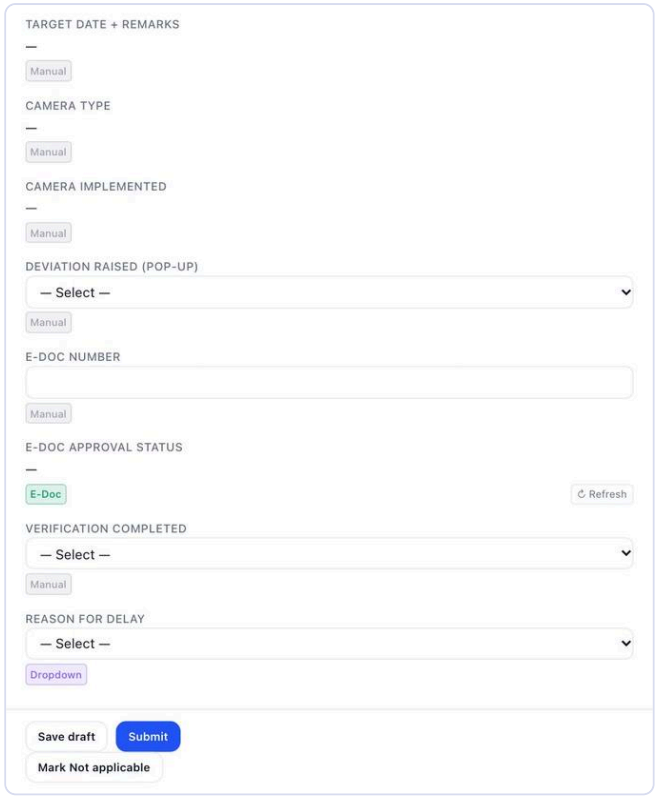

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Homologation applicable	Yes / No	PIC	-	Manual entry	-	-
2	Regulatory marking applicable	Yes / No	PIC	-	Manual entry	-	-
3	Camera available	Yes / No	PIC	-	Manual entry	-	-
4	Camera already considered	Yes / No	Vendor	PIC	Manual entry	-	-
5	Target date + remarks	Date	Vendor	PIC	Manual entry	-	-
6	Camera type	Dropdown	Vendor	PIC	Manual entry	-	OCR / Image
7	Camera implemented	Yes / No	Vendor	PIC	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
8	Deviation raised (pop-up)	Yes / No	PIC	-	Manual entry	-	-
9	E-Doc number	Text	PIC	-	Manual entry	-	-
10	E-Doc approval status	Dropdown	System	-	E-Doc	-	Approved / Under approval / Rejected
11	Verification completed	Yes / No	PIC	-	Manual entry	-	-
12	Reason for delay	Dropdown	PIC	-	Dropdown list	-	SC approval pending / SC approved, vendor implementation pending / All approvals in, delay by vendor

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-10 · SOP MILESTONE


39 List of limit samples for applicable parts

7 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

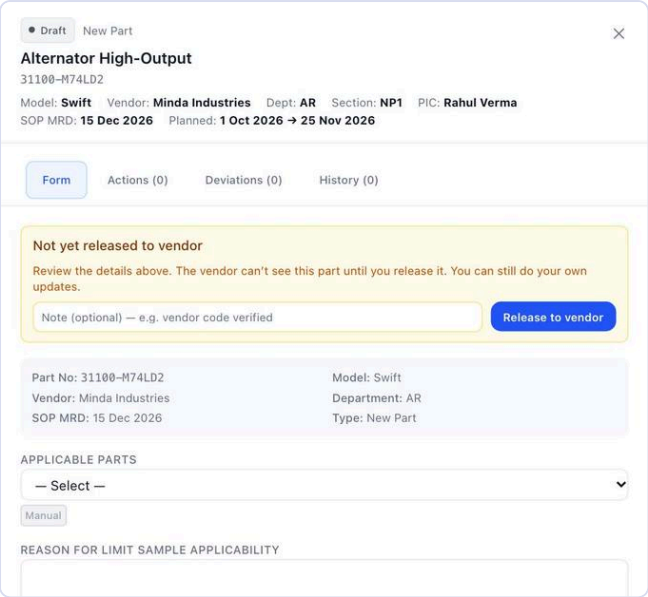

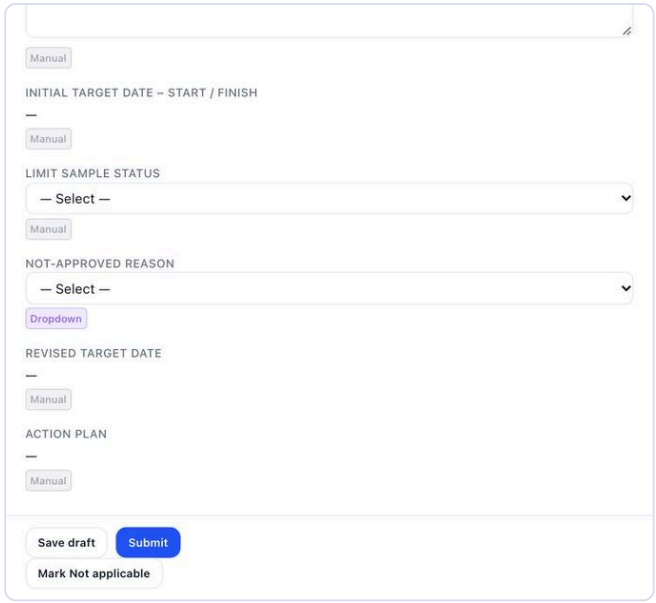

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicable parts	Yes / No	PIC	-	Manual entry	-	-
2	Reason for limit sample applicability	Long text	PIC	-	Manual entry	-	-
3	Initial target date – Start / finish	Date	Vendor	PIC	Manual entry	-	-
4	Limit sample status	Dropdown	PIC	-	Manual entry	Dashboard, Part list	Approved / Not approved
5	Not-approved reason	Dropdown	PIC	-	Dropdown list	-	Delay in preparation / Under preparation / Under correction
6	Revised target date	Date	Vendor	PIC	Manual entry	-	-
7	Action plan	Long text	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-11 · SOP MILESTONE


40 IFM mail initiation and checklist completion

6 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

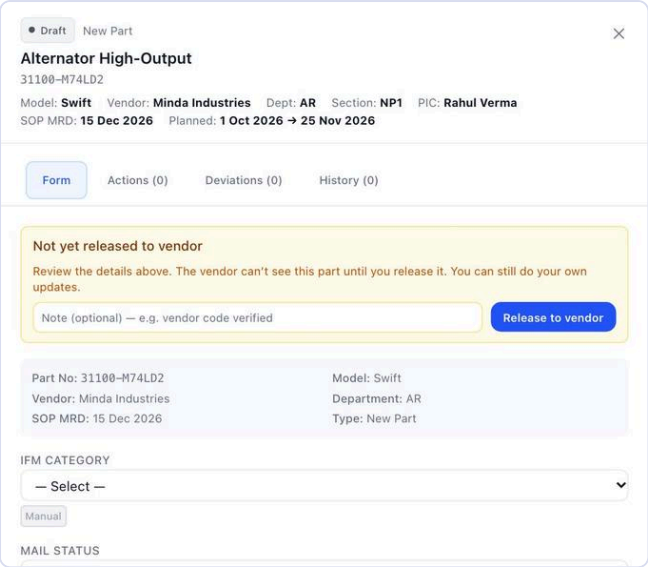

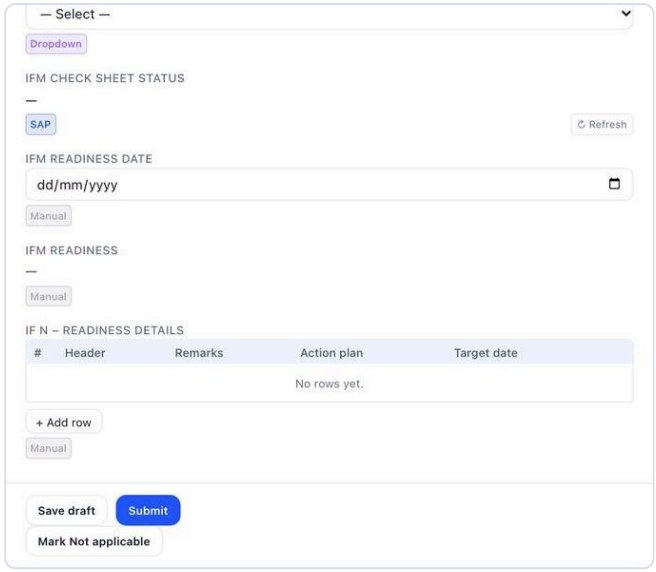

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	IFM category	Dropdown	PIC	-	Manual entry	Dashboard	A / B / C / D
2	Mail status	Dropdown	PIC	-	Dropdown list	-	Mail drafted / Mail sent from DVM-san desk
3	IFM check sheet status	Dropdown	System	-	SAP	-	Submitted by vendor / Approved by MSIL
4	IFM readiness date	Date	PIC	-	Manual entry	-	-
5	IFM readiness	Yes / No	Vendor	PIC	Manual entry	Part list	-
6	If N – readiness details	Table	Vendor	PIC	Manual entry	-	Columns: Header, Remarks, Action plan, Target date

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-14 · SOP MILESTONE

41 Part updation in Regulatory App

2 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

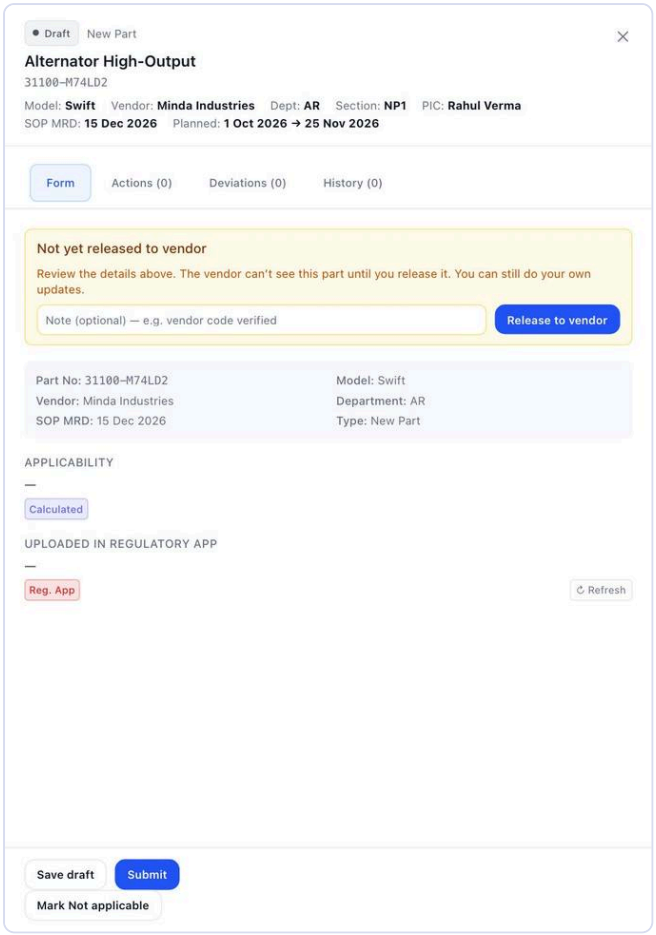

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	System	-	Calculated	-	-
2	Uploaded in regulatory app	Yes / No	System	-	Regulatory app	Dashboard, Part list	-

Reviewer: _____ Accepted ☐ Accepted with comments ☐ Rejected ☐


ACTIVITY · PILOT-15 · PILOT MILESTONE

42 Part updation in SMIR system

3 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

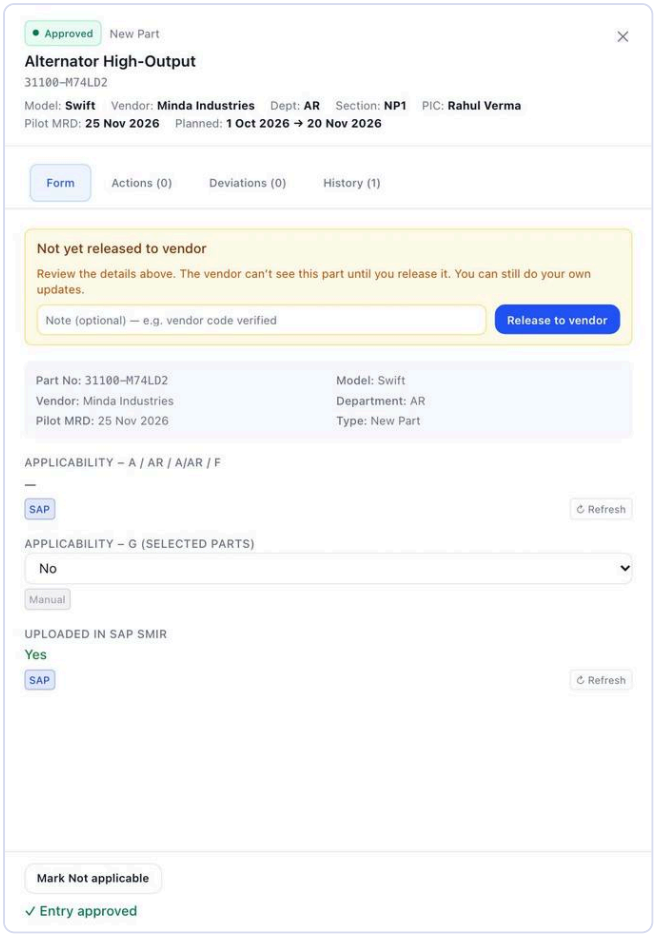

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability – A / AR / A/AR / F	Yes / No	System	-	SAP	-	-
2	Applicability – G (selected parts)	Yes / No	PIC	-	Manual entry	-	-
3	Uploaded in SAP SMIR	Yes / No	System	-	SAP	Dashboard, Part list	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-16 · SOP MILESTONE

43 Part updation in CPM portal

4 fields

Owner: PIC **Scope:** Both **Approval flow:** PIC Confirmation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2)

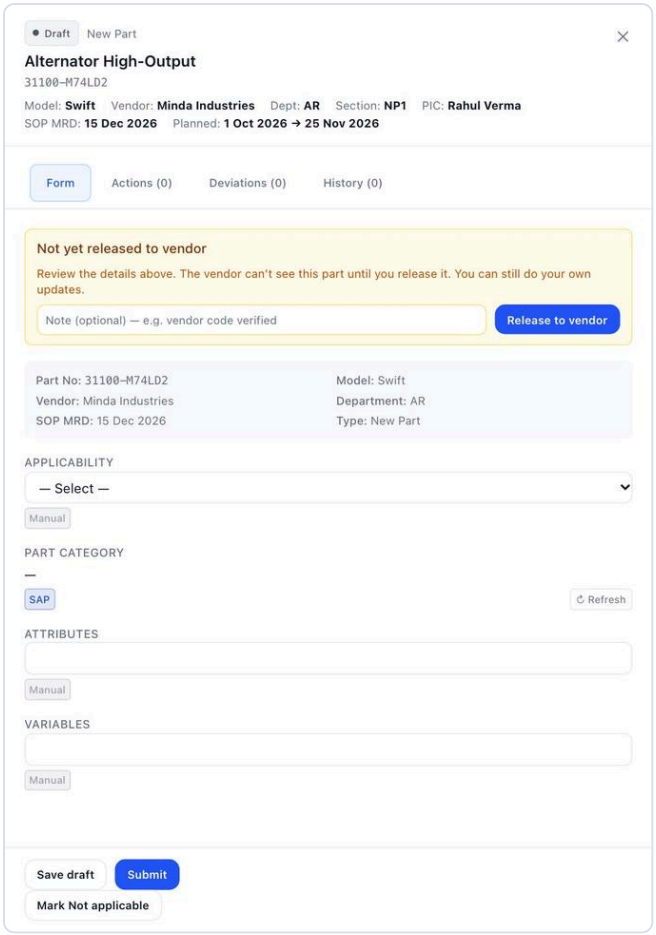

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Applicability	Yes / No	PIC	-	Manual entry	-	-
2	Part category	Text	System	-	SAP	-	-
3	Attributes	Number	PIC	-	Manual entry	-	-
4	Variables	Number	PIC	-	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-6 · SOP MILESTONE


44 PPVT confirmation

6 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 2 image panels, read left to right

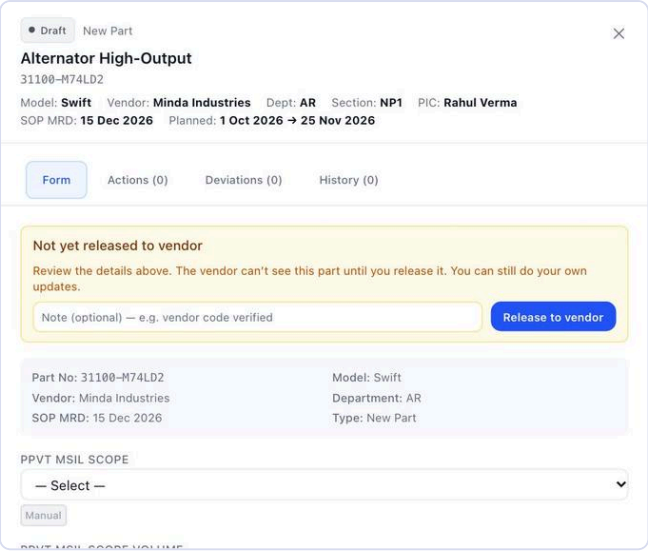

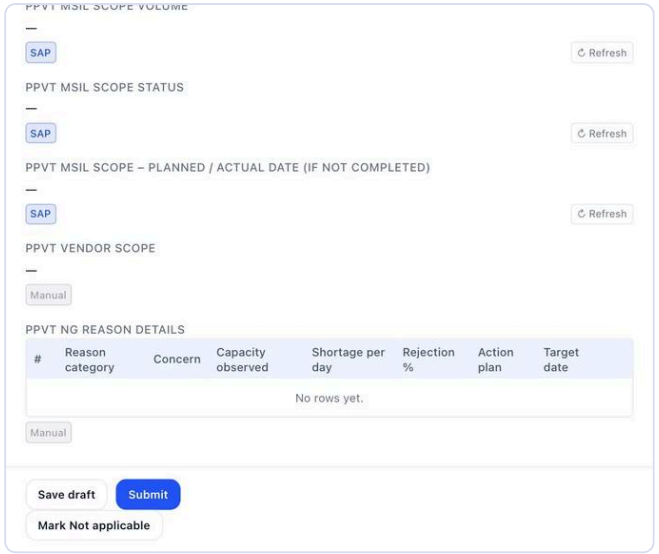

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	PPVT MSIL scope	Yes / No	PIC	-	Manual entry	-	-
2	PPVT MSIL scope volume	Number	System	-	SAP	-	-
3	PPVT MSIL scope status	Dropdown	System	-	SAP	Dashboard	OK / NG
4	PPVT MSIL scope – planned / actual date (if not completed)	Text	System	-	SAP	-	-
5	PPVT vendor scope	Text	Vendor	PIC	Manual entry	-	-
6	PPVT NG reason details	Table	Vendor	PIC	Manual entry	-	Columns: Reason category, Concern, Capacity observed, Shortage per day, Rejection %, Action plan, Target date

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □


ACTIVITY · PILOT-18 · SOP MILESTONE


45 PPVT confirmation – Vendor PPVT details


29 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 3 image panels, read left to right

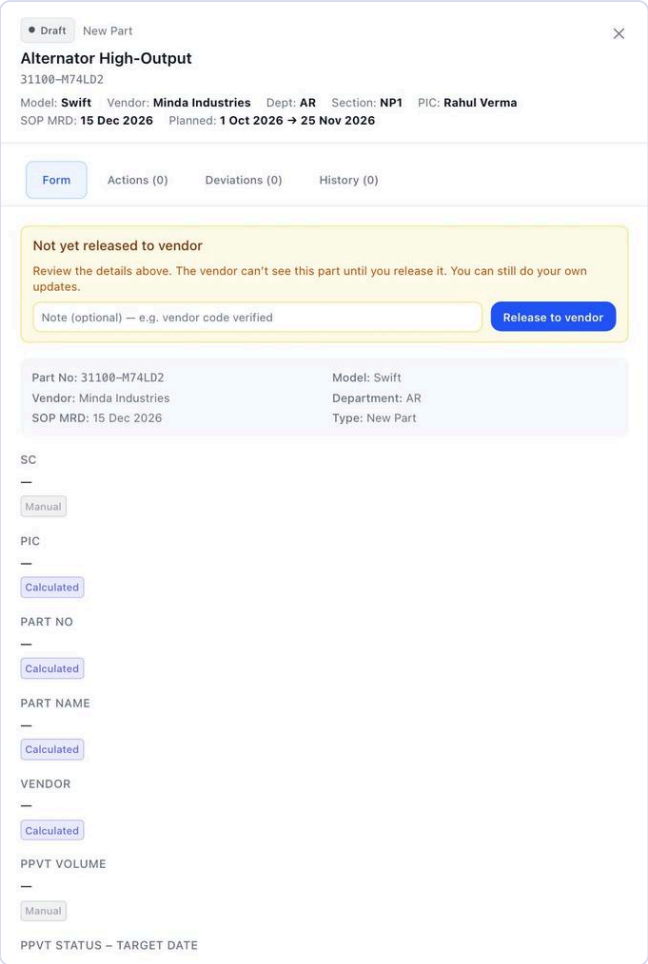

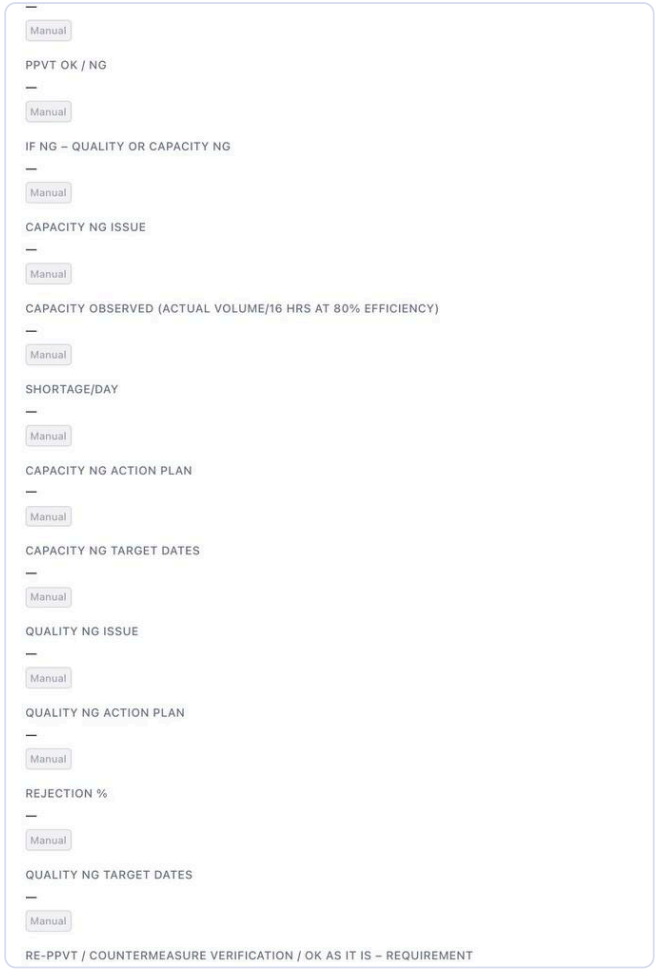

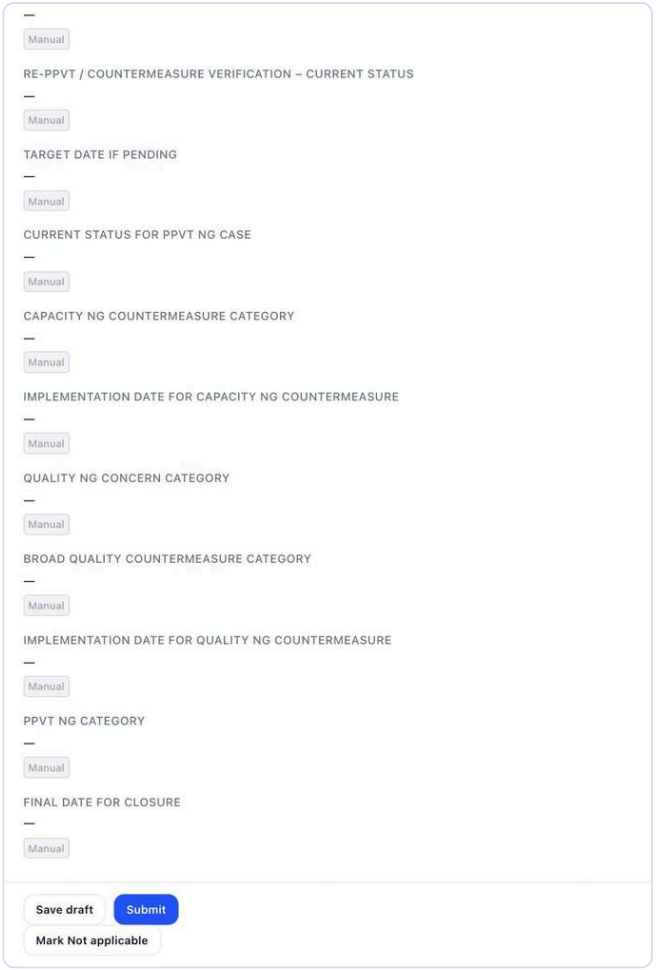

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	SC	Text	Vendor	PIC	Manual entry	-	-
2	PIC	Text	System	-	Calculated	-	-
3	Part No	Text	System	-	Calculated	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
4	Part name	Text	System	-	Calculated	-	-
5	Vendor	Text	System	-	Calculated	-	-
6	PPVT volume	Number	Vendor	PIC	Manual entry	-	-
7	PPVT status – Target date	Date	Vendor	PIC	Manual entry	-	-
8	PPVT OK / NG	Dropdown	Vendor	PIC	Manual entry	-	OK / NG
9	If NG – Quality or capacity NG	Dropdown	Vendor	PIC	Manual entry	-	Quality NG / Capacity NG / Both
10	Capacity NG issue	Long text	Vendor	PIC	Manual entry	-	-
11	Capacity observed (actual Volume/16 hrs at 80% efficiency)	Number	Vendor	PIC	Manual entry	-	-
12	Shortage/Day	Number	Vendor	PIC	Manual entry	-	-
13	Capacity NG action plan	Long text	Vendor	PIC	Manual entry	-	-
14	Capacity NG target dates	Date	Vendor	PIC	Manual entry	-	-
15	Quality NG issue	Long text	Vendor	PIC	Manual entry	-	-
16	Quality NG action plan	Long text	Vendor	PIC	Manual entry	-	-
17	Rejection %	Percent	Vendor	PIC	Manual entry	-	-
18	Quality NG target dates	Date	Vendor	PIC	Manual entry	-	-
19	Re-PPVT / countermeasure verification / OK as it is – Requirement	Dropdown	Vendor	PIC	Manual entry	-	Re-PPVT / Countermeasure Verification / OK As It Is
20	Re-PPVT / countermeasure verification – Current status	Long text	Vendor	PIC	Manual entry	-	-
21	Target date if pending	Date	Vendor	PIC	Manual entry	-	-
22	Current status for PPVT NG case	Long text	Vendor	PIC	Manual entry	-	-
23	Capacity NG countermeasure category	Text	Vendor	PIC	Manual entry	-	-
24	Implementation date for capacity NG countermeasure	Date	Vendor	PIC	Manual entry	-	-
25	Quality NG concern category	Text	Vendor	PIC	Manual entry	-	-
26	Broad quality countermeasure category	Text	Vendor	PIC	Manual entry	-	-
27	Implementation date for quality NG countermeasure	Date	Vendor	PIC	Manual entry	-	-
28	PPVT NG category	Dropdown	Vendor	PIC	Manual entry	-	Red / Yellow / Green
29	Final date for closure	Date	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

46


ACTIVITY · PILOT-12 · SOP MILESTONE

SOP Readiness Confirmation from Supplier


73 fields

Owner: PIC **Scope:** Both **Approval flow:** Vendor Entry (Vendor) → PIC Validation (PIC) **PIC can mark Not applicable:** Yes **Vendor sets planned timeline:** No

Form screen (PIC view, sample part 31100-M74LD2) · 7 image panels, read left to right

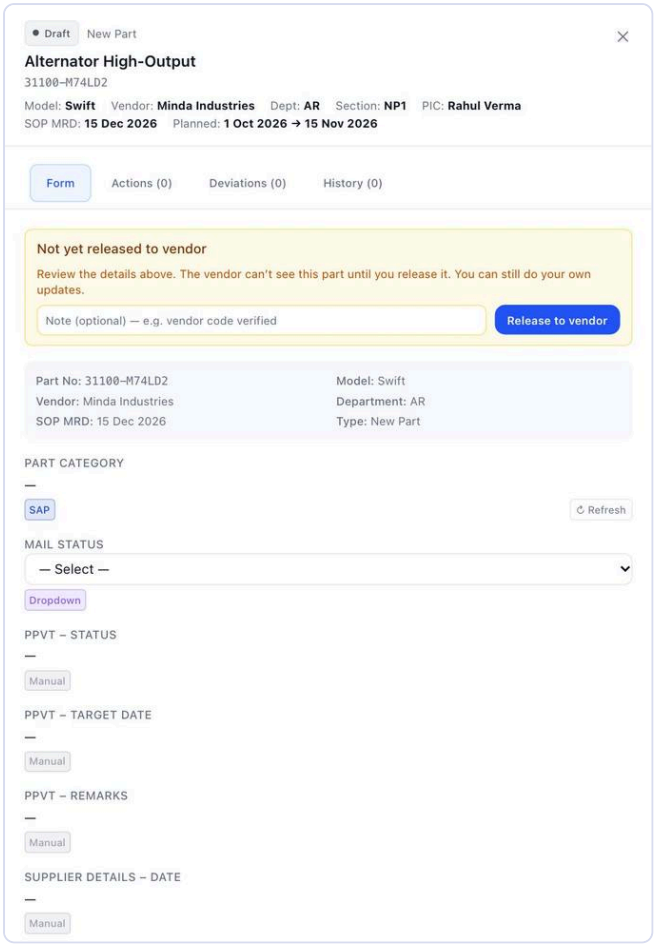



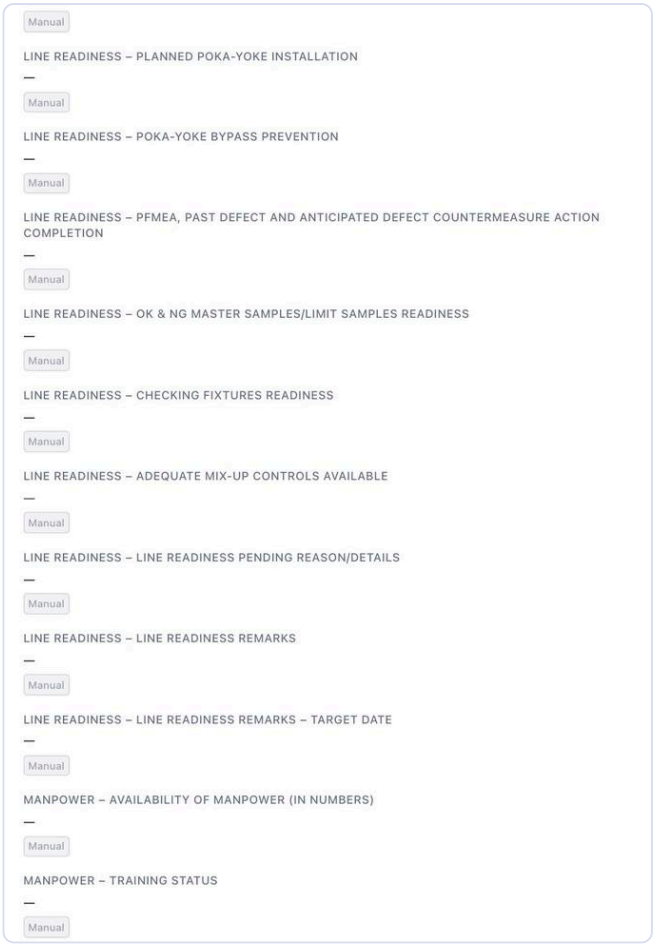

MANPOWER – MANPOWER REMARKS

—

Manual

MANPOWER – MANPOWER REMARKS – TARGET DATE

—

Manual

TIER-2 PREPAREDNESS – PARTS CONFIRMATION (AS PER DRAWING)

—

Manual

TIER-2 PREPAREDNESS – CAPACITY CONFIRMATION

—

Manual

TIER-2 PREPAREDNESS – IFM READINESS

—

Manual

TIER-2 PREPAREDNESS – TIER-2 PENDING/NG DETAILS

—

Manual

TIER-2 PREPAREDNESS – TIER-2 PENDING/NG DETAILS – TARGET DATE

—

Manual

PART EVALUATION – APPEARANCE, DIMENSIONS, MATERIAL & PERFORMANCE

—

Manual

PART EVALUATION – PART EVALUATION PENDING/NG DETAILS

—

Manual

PART EVALUATION – PART EVALUATION PENDING/NG DETAILS – TARGET DATE

—

Manual

PART EVALUATION – DURABILITY AND REGULATORY TESTING – STATUS

—

Manual

PART EVALUATION – DURABILITY AND REGULATORY TESTING – DETAILS

—

Manual

PART EVALUATION – DURABILITY AND REGULATORY TESTING – TARGET DATE

—

Manual

CLOSURE OF PENDING POINTS – PROCESS AUDIT/PPVT: ALL POINTS CLOSED

—

Manual

CLOSURE OF PENDING POINTS – PENDING POINTS DETAILS

—

Manual

CLOSURE OF PENDING POINTS – PENDING POINTS DETAILS – TARGET DATE

—

Manual

ECN CONFIRMATION – ALL ECNS IMPLEMENTED, INCLUDING VENDOR PROPRIETARY DESIGN CHANGES (INCLUDING TIER 2)

—

Manual

ECN CONFIRMATION – ECN IMPLEMENTATION DETAILS IF NO

—

Manual

ECN CONFIRMATION – ECN IMPLEMENTATION TARGET DATE

—

Manual

ECN CONFIRMATION – PRE-ECN PARTS DISPOSAL/SCRAP DETAILS (ANNEXURE-A)

—

Manual

ECN CONFIRMATION – PRE-ECN PARTS AVAILABLE IN PLANT/WAREHOUSE

—

Manual

PACKAGING READINESS – SUFFICIENT NUMBER OF TROLLEYS/BINS AVAILABLE (INCLUDING WIP PACKAGING)

—

Manual

PACKAGING READINESS – PACKAGING READINESS REMARKS

—

Manual

4M CHANGE – ANY 4M CHANGE (PROCESS/METHOD/MATERIAL AFTER MPT TRIAL) – CHANGE DETAILS

—

Manual

4M CHANGE – ANY 4M CHANGE (PROCESS/METHOD/MATERIAL AFTER MPT TRIAL) – REASON

—

Manual

IFM STATION READINESS – SEPARATE IFM STATION AVAILABLE WITH REQUIRED MANPOWER

—

Manual

IFM STATION READINESS – IFM STATION READINESS REMARKS

—

Manual

OLD PARTS CONFIRMATION – OLD PARTS AVAILABLE IN PLANT (INCLUDING TIER 2)

—

Manual

OLD PARTS CONFIRMATION – BATCH CODE DETAILS (IF OLD PARTS AVAILABLE)

—

Manual

OLD PARTS CONFIRMATION – SHELF LIFE DETAILS

—

Manual

OLD PARTS CONFIRMATION – NON-USABLE PARTS DISPOSAL/SCRAP DETAILS (ANNEXURE-A)

—

Manual

OLD PARTS CONFIRMATION – OLD PARTS CAN BE USED FOR SOP SUPPLY

—

Manual

OLD PARTS CONFIRMATION – REASON FOR OLD PART USAGE/NON-USAGE


—

Manual

SET PARTS – SET PARTS F-DRAWING & WIS AVAILABLE

—

Manual

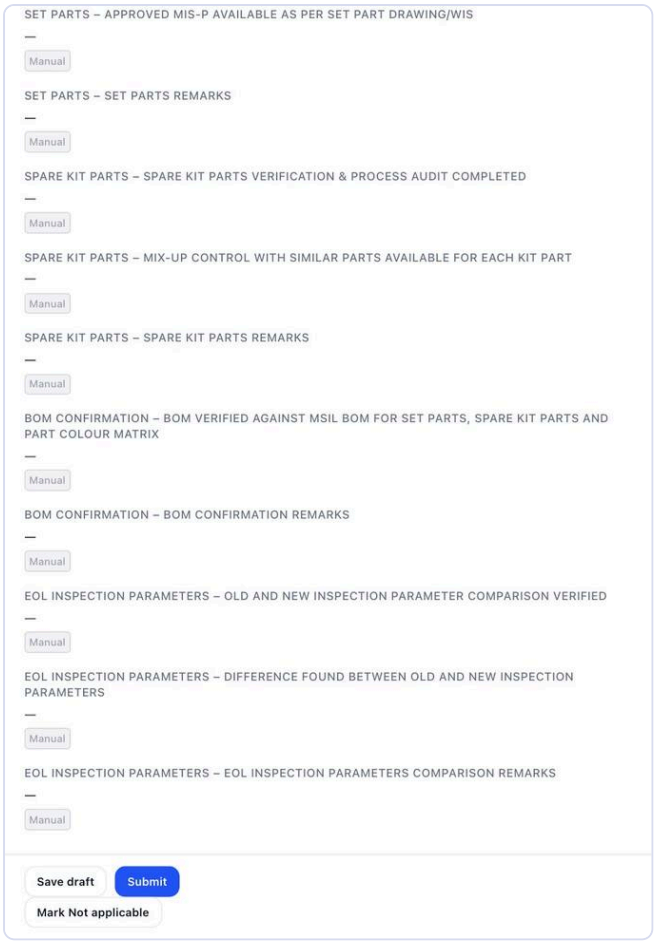

Field definitions

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
1	Part category	Dropdown	System	-	SAP	Part list	A / AR / A/AR / G / F
2	Mail status	Dropdown	PIC	-	Dropdown list	-	Mail sent / Pending / Reply received
3	PPVT – status	Dropdown	System	-	Manual entry	-	Closed / Pending
4	PPVT – target date	Date	System	-	Manual entry	-	-
5	PPVT – remarks	Long text	System	-	Manual entry	-	-
6	Supplier details – Date	Date	Vendor	PIC	Manual entry	-	-
7	Supplier details – Vendor name	Text	System	-	Manual entry	-	-
8	Supplier details – Vendor code	Text	System	-	Manual entry	-	-
9	Supplier details – Model	Text	System	-	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
10	Supplier details – No. of parts supplied by vendor	Number	Vendor	PIC	Manual entry	-	-
11	Supplier details – Part family	Text	Vendor	PIC	Manual entry	-	-
12	Supplier details – SOP	Date	System	-	Manual entry	-	-
13	Tool readiness – Parts with permanent tool	Yes / No	Vendor	PIC	Manual entry	-	-
14	Tool readiness – Parts with temporary tool or tool under modification	Yes / No	Vendor	PIC	Manual entry	-	-
15	Tool readiness – Tool readiness remarks with target date	Long text	Vendor	PIC	Manual entry	-	-
16	Line readiness – Operating Standards/WIS display on line	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
17	Line readiness – Trained manpower availability including supervisors	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
18	Line readiness – Production equipment and EOL installation (if applicable)	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending / N/A
19	Line readiness – Planned Poka-yoke installation	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending / N/A
20	Line readiness – Poka-yoke bypass prevention	Dropdown	Vendor	PIC	Manual entry	-	Confirmed / Not confirmed
21	Line readiness – PFMEA, past defect and anticipated defect countermeasure action completion	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
22	Line readiness – OK & NG master samples/limit samples readiness	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
23	Line readiness – Checking fixtures readiness	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
24	Line readiness – Adequate mix-up controls available	Yes / No	Vendor	PIC	Manual entry	-	-
25	Line readiness – Line readiness pending Reason/Details	Long text	Vendor	PIC	Manual entry	-	-
26	Line readiness – Line readiness remarks	Long text	Vendor	PIC	Manual entry	-	-
27	Line readiness – Line readiness remarks – target date	Date	Vendor	PIC	Manual entry	-	-
28	Manpower – Availability of manpower (in numbers)	Number	Vendor	PIC	Manual entry	-	-
29	Manpower – Training status	Dropdown	Vendor	PIC	Manual entry	-	Completed / Pending
30	Manpower – Manpower remarks	Long text	Vendor	PIC	Manual entry	-	-
31	Manpower – Manpower remarks – target date	Date	Vendor	PIC	Manual entry	-	-
32	Tier-2 preparedness – Parts confirmation (as per drawing)	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Evaluation Pending
33	Tier-2 preparedness – Capacity confirmation	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Evaluation Pending
34	Tier-2 preparedness – IFM readiness	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Evaluation Pending
35	Tier-2 preparedness – Tier-2 Pending/NG details	Long text	Vendor	PIC	Manual entry	-	-
36	Tier-2 preparedness – Tier-2 Pending/NG details – target date	Date	Vendor	PIC	Manual entry	-	-
37	Part evaluation – Appearance, dimensions, material & performance	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Evaluation Pending
38	Part evaluation – Part evaluation Pending/NG details	Long text	Vendor	PIC	Manual entry	-	-
39	Part evaluation – Part evaluation Pending/NG details – target date	Date	Vendor	PIC	Manual entry	-	-
40	Part evaluation – Durability and regulatory testing – status	Dropdown	Vendor	PIC	Manual entry	-	OK / NG / Evaluation Pending / N/A
41	Part evaluation – Durability and regulatory testing – details	Long text	Vendor	PIC	Manual entry	-	-
42	Part evaluation – Durability and regulatory testing – target date	Date	Vendor	PIC	Manual entry	-	-
43	Closure of pending points – Process Audit/PPVT: all points closed	Yes / No	Vendor	PIC	Manual entry	-	-

#	Field	Type	Entered by	Validated by	Source	Flags	Values / columns
44	Closure of pending points – Pending points details	Long text	Vendor	PIC	Manual entry	-	-
45	Closure of pending points – Pending points details – target date	Date	Vendor	PIC	Manual entry	-	-
46	ECN confirmation – All eCNs implemented, including vendor proprietary design changes (including Tier 2)	Yes / No	Vendor	PIC	Manual entry	-	-
47	ECN confirmation – ECN implementation details if No	Long text	Vendor	PIC	Manual entry	-	-
48	ECN confirmation – ECN implementation target date	Date	Vendor	PIC	Manual entry	-	-
49	ECN confirmation – Pre-ECN parts Disposal/Scrap details (Annexure-A)	Long text	Vendor	PIC	Manual entry	-	-
50	ECN confirmation – Pre-ECN parts available in Plant/Warehouse	Yes / No	Vendor	PIC	Manual entry	-	-
51	Packaging readiness – Sufficient number of trolleys/bins available (including WIP packaging)	Yes / No	Vendor	PIC	Manual entry	-	-
52	Packaging readiness – Packaging readiness remarks	Long text	Vendor	PIC	Manual entry	-	-
53	4M change – Any 4M change (process/method/material after MPT trial) – Change details	Long text	Vendor	PIC	Manual entry	-	-
54	4M change – Any 4M change (process/method/material after MPT trial) – Reason	Long text	Vendor	PIC	Manual entry	-	-
55	IFM station readiness – Separate IFM station available with required manpower	Yes / No	Vendor	PIC	Manual entry	-	-
56	IFM station readiness – IFM station readiness remarks	Long text	Vendor	PIC	Manual entry	-	-
57	Old parts confirmation – Old parts available in plant (including Tier 2)	Yes / No	Vendor	PIC	Manual entry	-	-
58	Old parts confirmation – Batch code details (if old parts available)	Long text	Vendor	PIC	Manual entry	-	-
59	Old parts confirmation – Shelf life details	Long text	Vendor	PIC	Manual entry	-	-
60	Old parts confirmation – Non-usable parts Disposal/Scrap details (Annexure-A)	Long text	Vendor	PIC	Manual entry	-	-
61	Old parts confirmation – Old parts can be used for SOP supply	Yes / No	Vendor	PIC	Manual entry	-	-
62	Old parts confirmation – Reason for old part Usage/Non-Usage	Long text	Vendor	PIC	Manual entry	-	-
63	Set parts – Set parts F-Drawing & WIS available	Yes / No	Vendor	PIC	Manual entry	-	-
64	Set parts – Approved MIS-P available as per set part Drawing/WIS	Yes / No	Vendor	PIC	Manual entry	-	-
65	Set parts – Set parts remarks	Long text	Vendor	PIC	Manual entry	-	-
66	Spare kit parts – Spare kit parts verification & process audit completed	Yes / No	Vendor	PIC	Manual entry	-	-
67	Spare kit parts – Mix-up control with similar parts available for each kit part	Yes / No	Vendor	PIC	Manual entry	-	-
68	Spare kit parts – Spare kit parts remarks	Long text	Vendor	PIC	Manual entry	-	-
69	BOM confirmation – BOM verified against MSIL BOM for set parts, spare kit parts and part colour matrix	Yes / No	Vendor	PIC	Manual entry	-	-
70	BOM confirmation – BOM confirmation remarks	Long text	Vendor	PIC	Manual entry	-	-
71	EOL inspection parameters – Old and new inspection parameter comparison verified	Yes / No	Vendor	PIC	Manual entry	-	-
72	EOL inspection parameters – Difference found between old and new inspection parameters	Yes / No	Vendor	PIC	Manual entry	-	-
73	EOL inspection parameters – EOL inspection parameters comparison remarks	Long text	Vendor	PIC	Manual entry	-	-

Reviewer: _____ Accepted □ Accepted with comments □ Rejected □

APPENDIX B

Sign-off summary

Capability / screen	Accepted	With comments	Rejected	Comments
Chapter 1: Plan & schedule	☐	☐	☐	
Models & MRDs	☐	☐	☐	
Section Template	☐	☐	☐	
Applicability	☐	☐	☐	
Settings	☐	☐	☐	
Chapter 2: Parts & ownership	☐	☐	☐	
Parts & Audit: part numbers	☐	☐	☐	
Add dummy part	☐	☐	☐	
ECN transfer	☐	☐	☐	
PIC Assignments	☐	☐	☐	
Chapter 3: Activity design	☐	☐	☐	
Activities	☐	☐	☐	
Builder: activity list	☐	☐	☐	
Builder: Basics	☐	☐	☐	
Builder: Fields	☐	☐	☐	
Builder: Flow	☐	☐	☐	
Builder: Timeline	☐	☐	☐	
Chapter 4: Release & acknowledge	☐	☐	☐	
My Work: parts released to you	☐	☐	☐	
Return parts to the PIC	☐	☐	☐	
My Work: pending release	☐	☐	☐	
My Work: released to vendor	☐	☐	☐	
Part form: returned by vendor	☐	☐	☐	
Chapter 5: Data entry	☐	☐	☐	
My Work: Workspace	☐	☐	☐	
My Work: Worklist	☐	☐	☐	
Entry grid (Vendor)	☐	☐	☐	
Entry grid (PIC)	☐	☐	☐	
Part Workspace	☐	☐	☐	
Bulk Entry Grid	☐	☐	☐	
Activity page	☐	☐	☐	

Part form	☐	☐	☐	
AI import panel	☐	☐	☐	
AI review: dropdown matches and failed updates	☐	☐	☐	
Chapter 6: Validation & approvals	☐	☐	☐	
Validation grid	☐	☐	☐	
Deviation Tracker	☐	☐	☐	
Part form: Actions	☐	☐	☐	
Part form: History	☐	☐	☐	
Chapter 7: Status & risk insight	☐	☐	☐	
Lessons Learnt	☐	☐	☐	
Vendor scorecards	☐	☐	☐	
Chapter 8: Project view	☐	☐	☐	
WBS / Project	☐	☐	☐	
Activity Dependencies	☐	☐	☐	
Set dependency	☐	☐	☐	
Chapter 9: Resource & travel planning	☐	☐	☐	
Manpower Planning: PIC load	☐	☐	☐	
Manpower Planning: vendor visits	☐	☐	☐	
Chapter 10: Monitoring & reporting	☐	☐	☐	
Foundation: Foundation: roles, access and Home	☐	☐	☐	
Home (Admin)	☐	☐	☐	
Home (PIC)	☐	☐	☐	
Appendix A: 46 activity pages and 467 field definitions	☐	☐	☐	
